



Supplied aerial: post-demolition / pre-excavation context. Orange footprint and tree labels are user annotations, not surveyed geometry. Tree positions/IDs conflict with parts of the permit set: see EC-03.

Proposed erection logic

Work one released level at a time. From Jordan Avenue, build stable far-side cells before their near-side returns. Complete rear/middle cells, then the frontage. Receive large pieces from above before closing their overhead framing.

Primary crane strategy - ASSUMED

A: mid/rear Jordan Avenue candidate. B: forward Jordan Avenue relocation candidate only if A fails coverage or clearance. No verified crane capacity, radius, outrigger footprint or street occupation is available.

Building facts - CONFIRMED

Eight stories plus basement, with roof terrace and headhouses (T1.1; A1.1-A1.10; A5.1). CFS bearing/nonbearing walls and steel framing are shown. The reference residence is not the target building.

Release-critical gaps - FIELD VERIFY

Panel shop model, joints, weights and pick points; crane chart and 3D lift envelope; engineered temporary stability and deck loads; tree survey; L8 structural mapping; floor-system conflicts; parking equipment routes.


This package is a coordination concept. It does not establish a safe lifting capacity or prove panel-by-panel constructability. The proposed sequence is conditional on the hold points and must be converted to a released erection/lift plan.



T = truck/container | S = inspect/rig staging | R = conditional crane relocation | != critical closure / verification hold | Hatching = restricted / no staging | Dashed red boxes = proposed work groups

All new sequence and crane selections are ASSUMED. Read: reference > site > substructure > vertical cycle > floors > roof > packing > replay > holds > sequence register.

Reference PDF: one page, Sarkar Residence, 10510 Madera Drive, Cupertino | Source A-1.004 plus superimposed first-floor snapshot

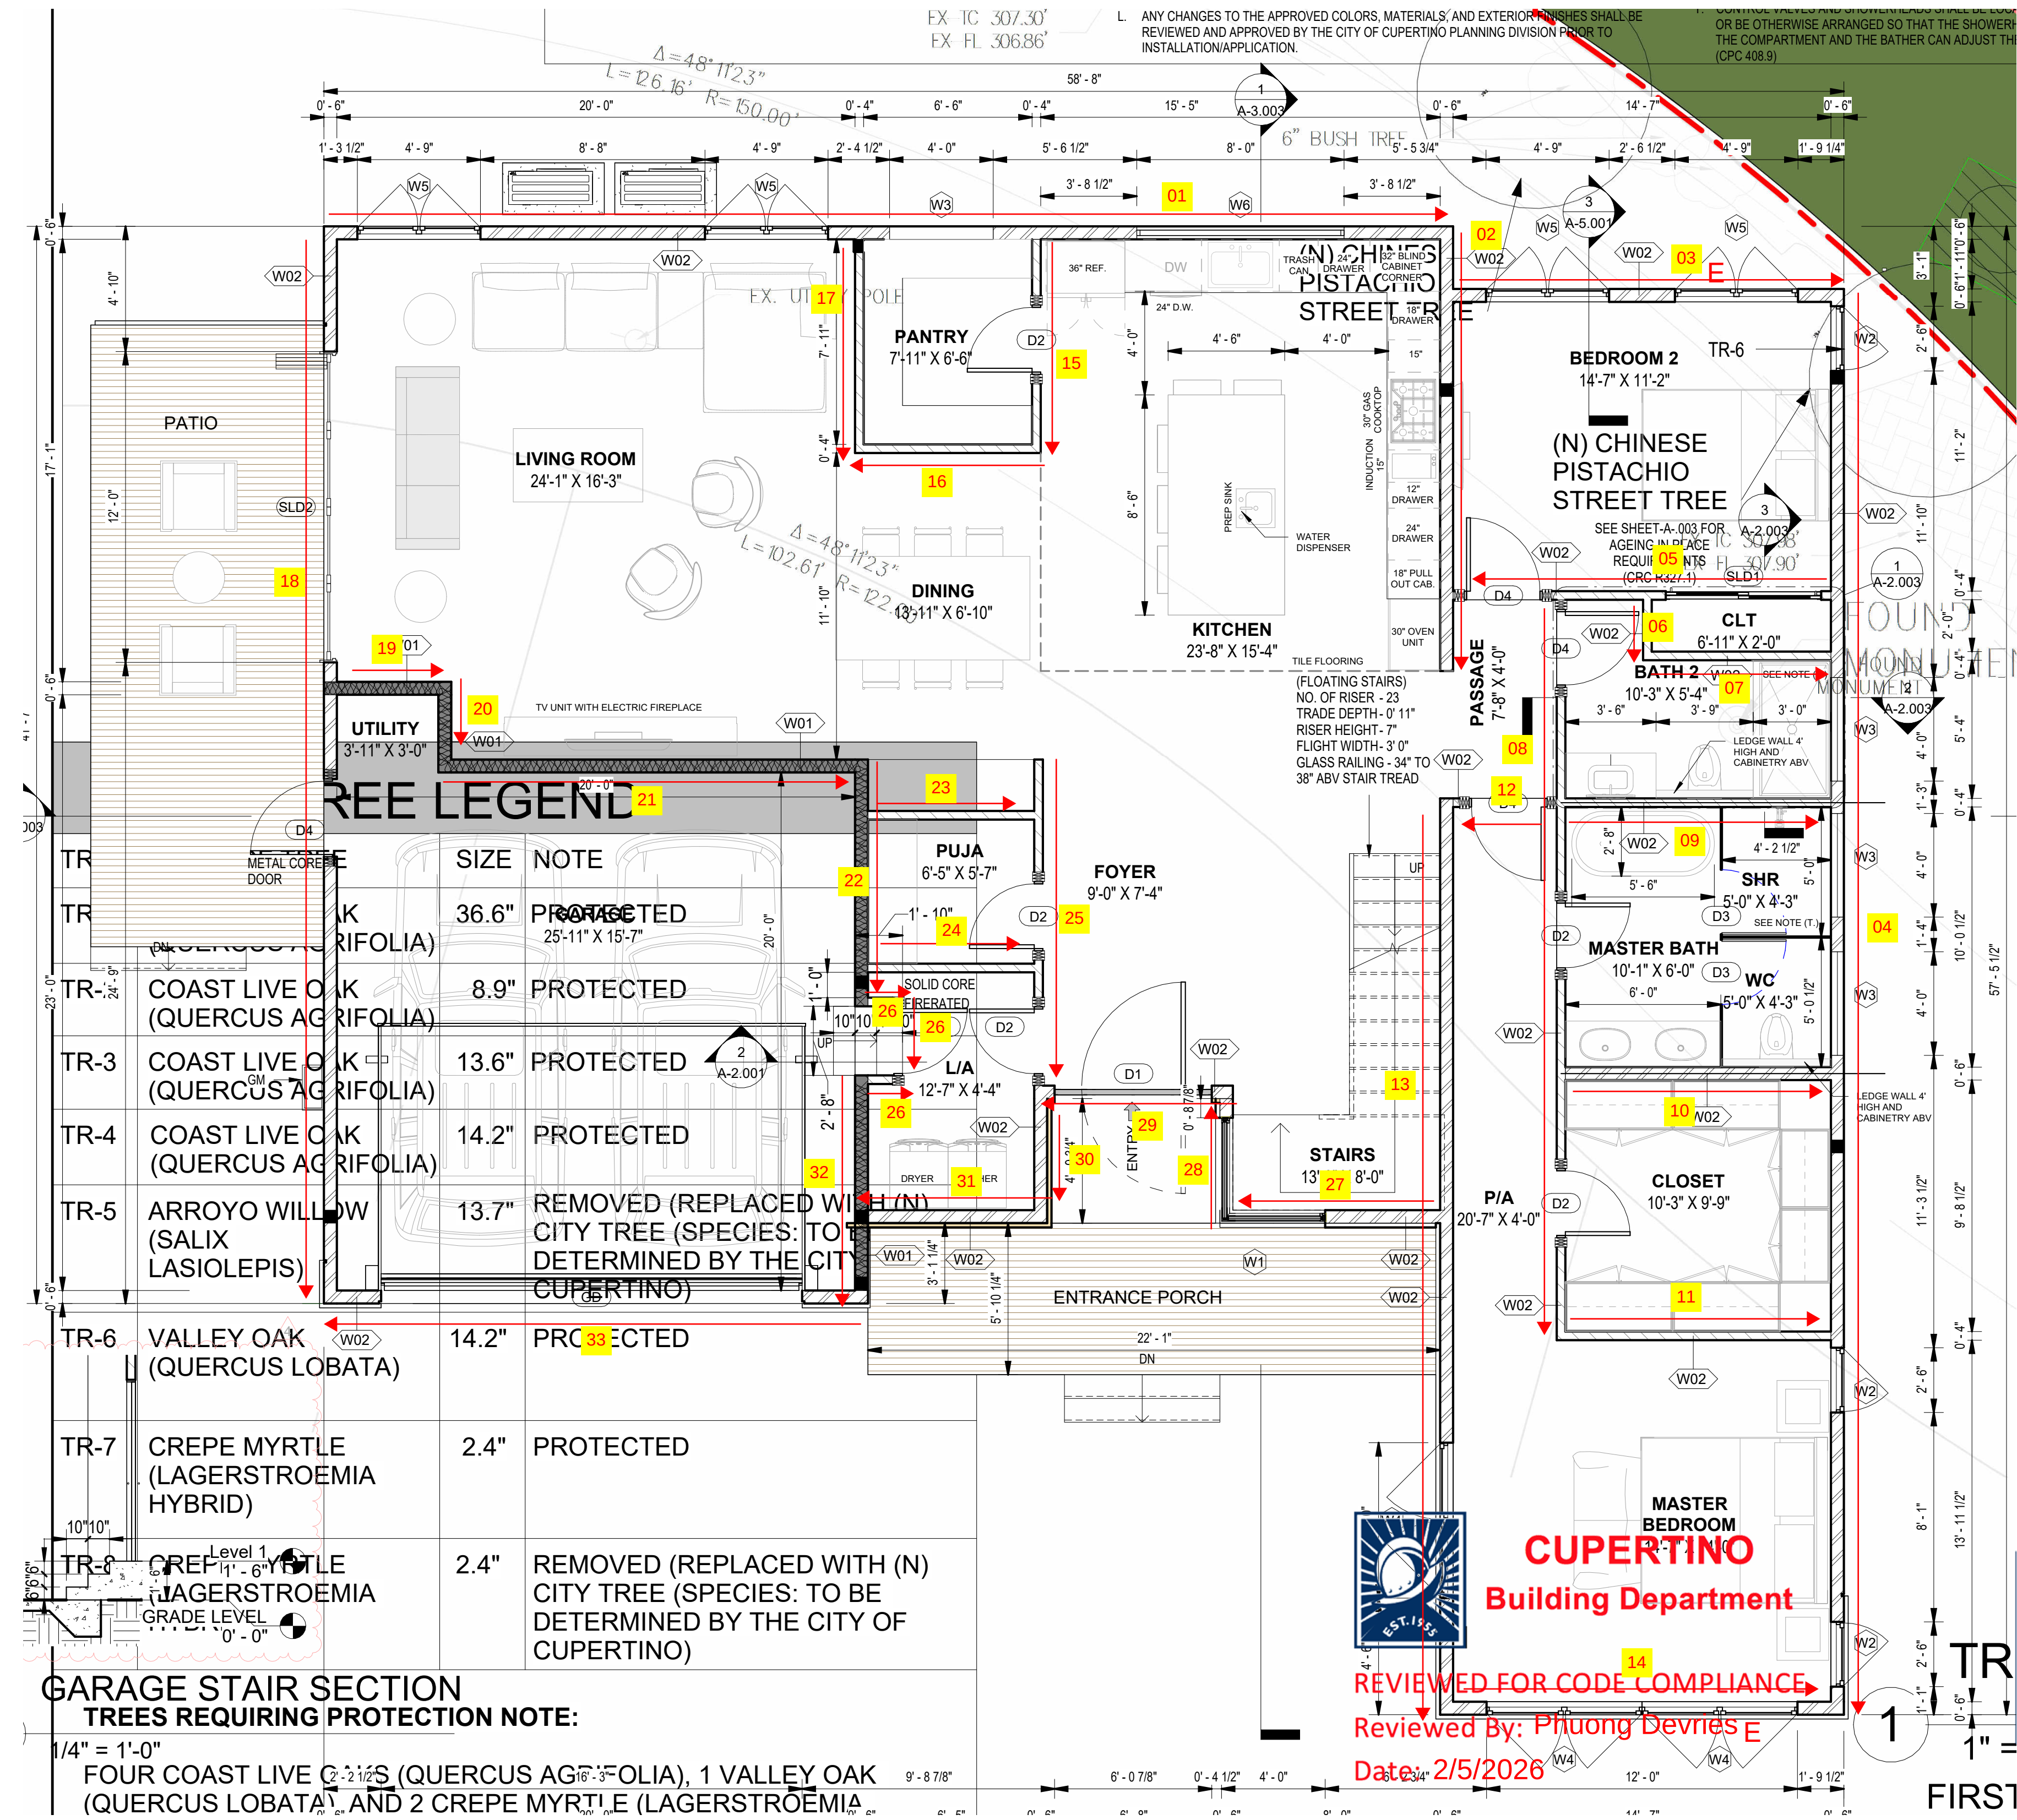

Observed sequence - CONFIRMED

01-04 trace the top and right perimeter. 05-14 move through bedroom/bathroom crosswalls, passage and the lower return. 15-17 wrap the pantry. 18-25 continue the left perimeter, garage/living interface and puja/foyer.

Last groups - CONFIRMED

26 is repeated on three local segments. 27-33 complete the stair/entry/laundry/garage-side area. Red arrows indicate direction along wall runs; yellow tags label groups. The arrows are not a crane-radius or capacity diagram.

Underlying logic - PROBABLE

Use a stable perimeter start; resolve returns and crosswalls before adjacent closures; work in local clusters; finish restricted entry/service areas after larger groups. Connection-face access may explain several turns. These reasons are inferred, not written on the reference.

Not established by the reference


No C/T/S symbols, crane setup, relocation schedule, packing manifest, bracing design or step-by-step access validation is shown. Do not claim those items were reverse-engineered as facts.

LIVIO ERECTION SEQUENCE LOGIC: group by constructible wall runs, show direction, place trapped pieces before closures, preserve connection and future delivery access, and test the changed condition after each group. Add a stability/diaphragm cycle for this multistory project.

Improved here: unique numbers, clean source crops, distinct access/material styles, documented assumptions, explicit closure and crane-move checks.

Authority: civil C2.0 p75 + A1.0 p15, ER-1 p90, landscape L1.01 p98, joint trench p215 | Symbols indicate candidate zones, not equipment footprints

R: A to B only after a stable sector stop

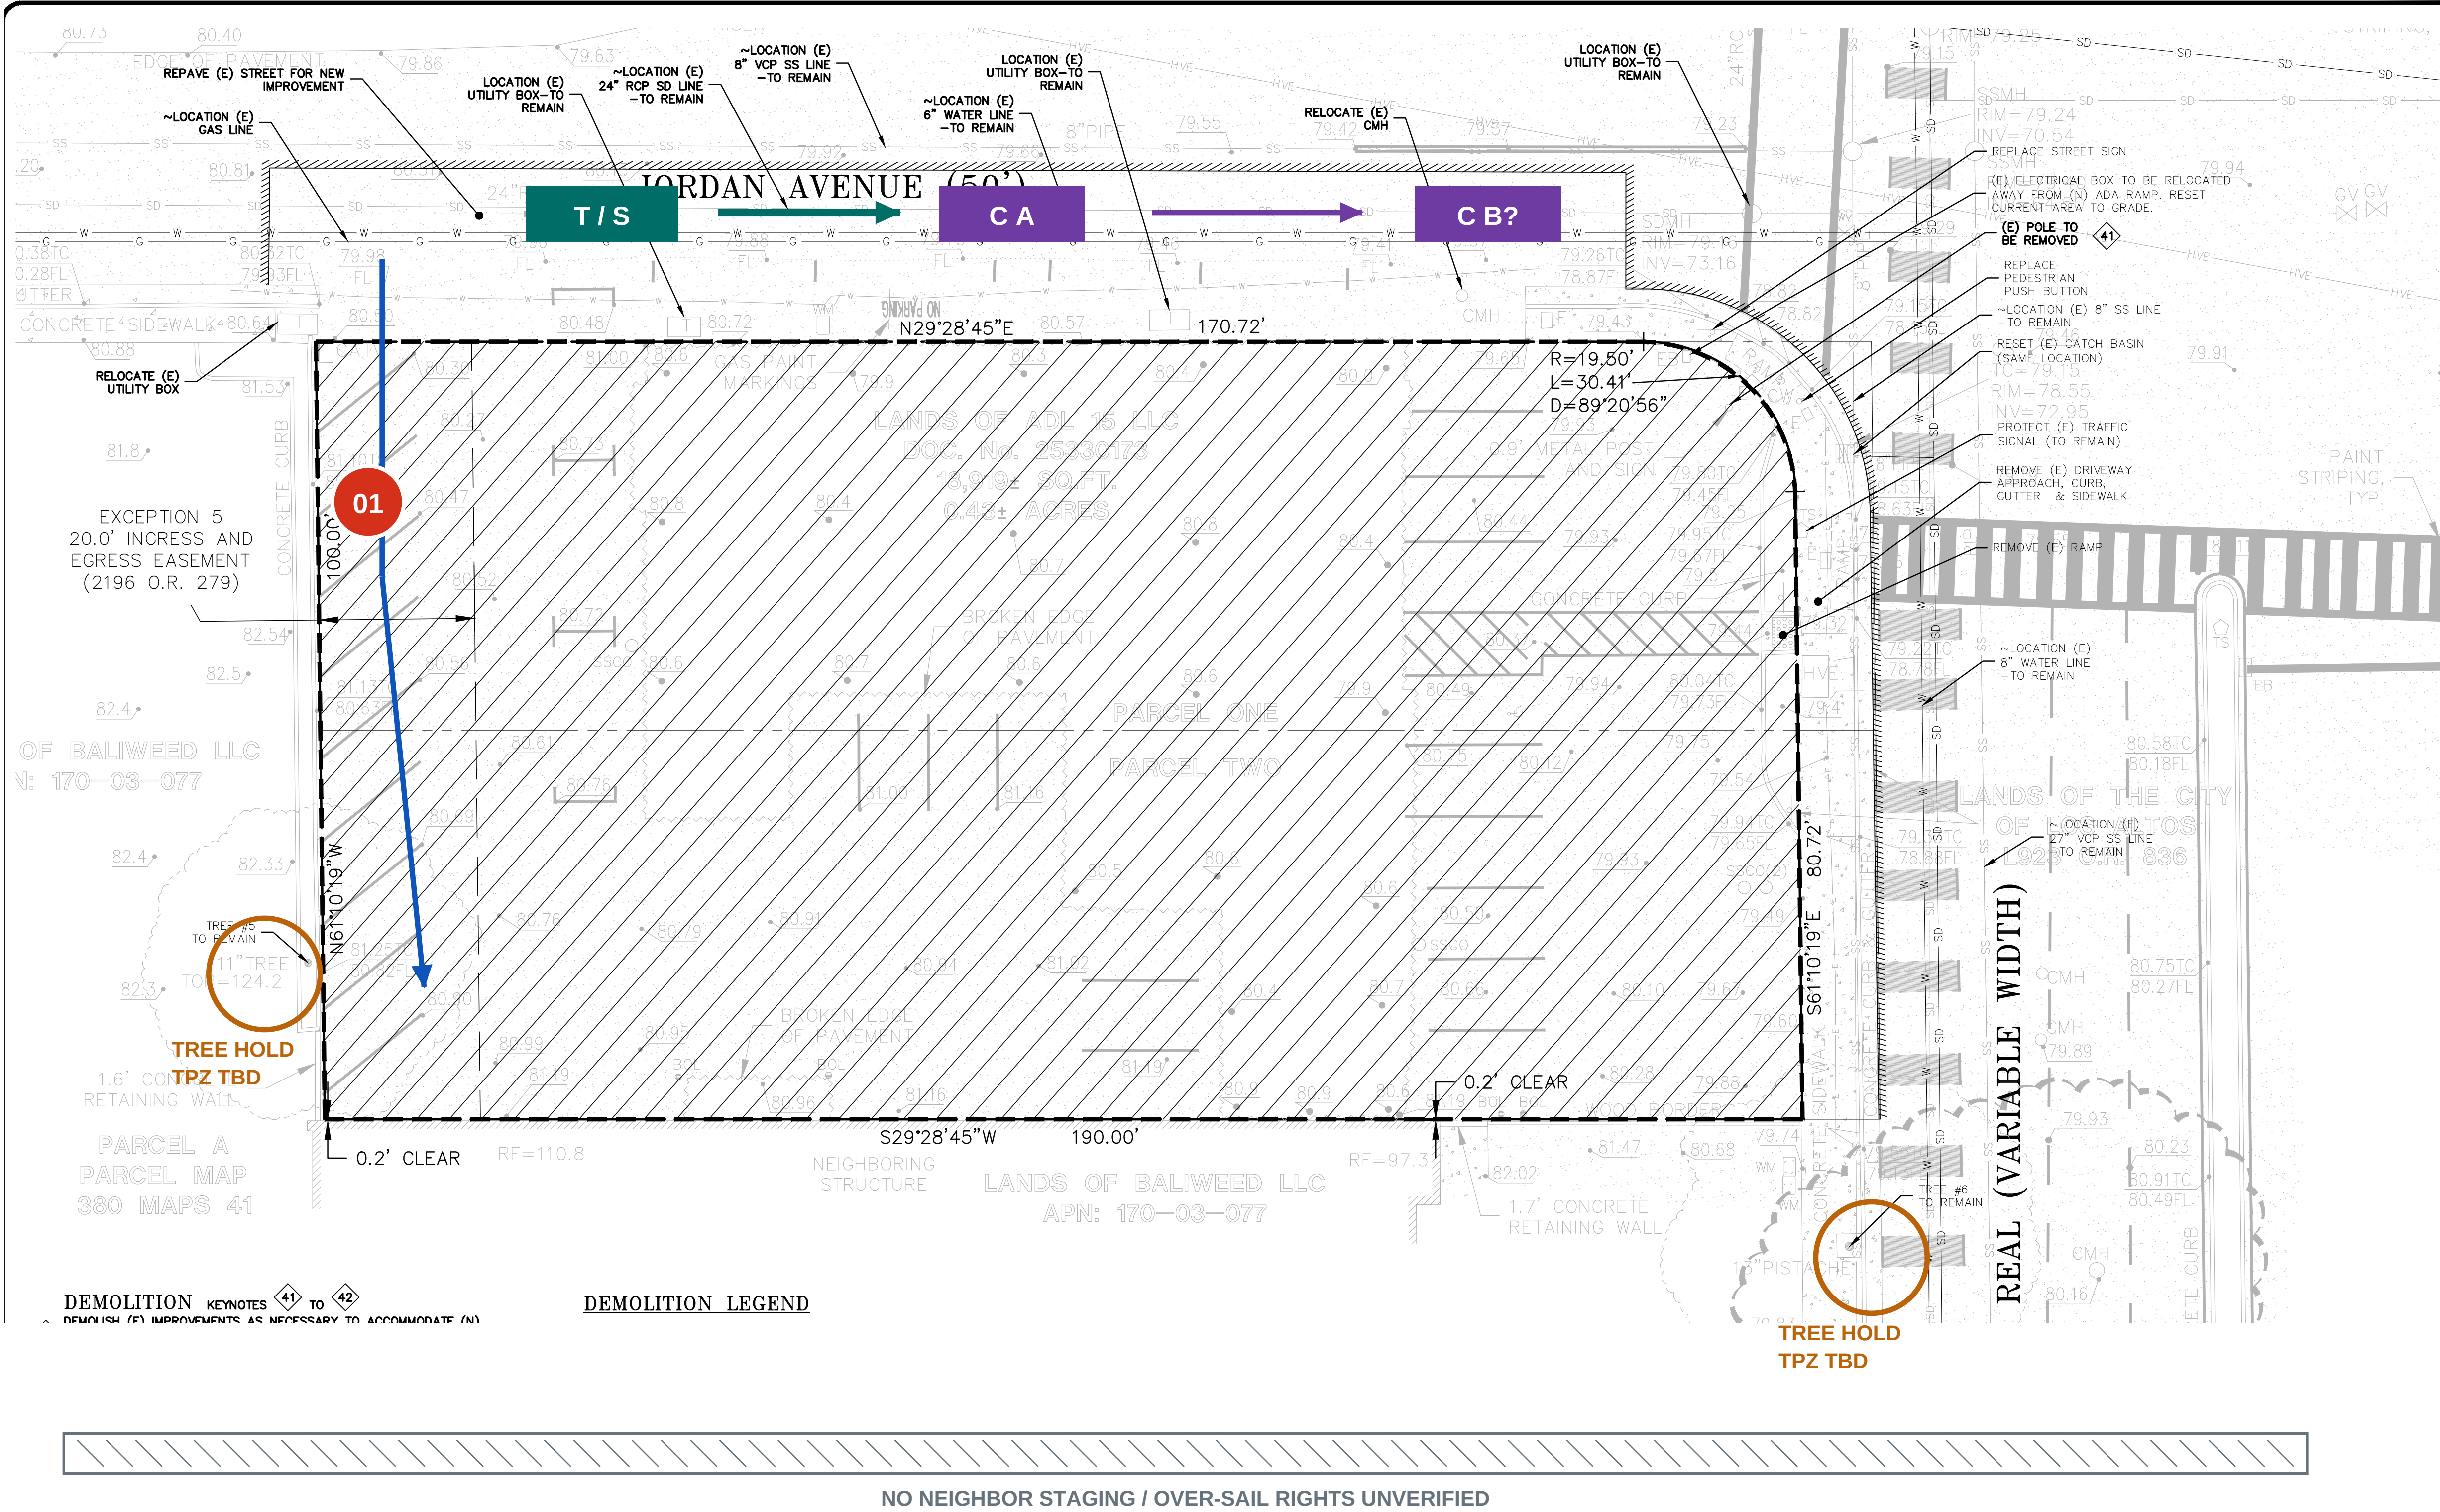

A - primary candidate

Mid/rear Jordan frontage. Keep setup outside the excavation influence zone and clear of utilities, transformer access, drive apron and retained trees. Location and support system: FIELD VERIFY.

B - conditional candidate

Forward Jordan frontage, away from the intersection. Use only if A cannot serve the front groups. B must pass the same ground, utility, traffic, tree and load-chart checks. No default El Camino lane setup.

T / S - timed deliveries

Truck/container and inspection/rigging space share a permitted working zone by time, not by assumed simultaneous fit. No on-site stockyard is demonstrated. Use off-site holding and one called-off kit at a time.

Tree conflict - FIELD VERIFY

C2.0 labels rear-side tree #5 and front-side tree #6 to remain. L1.01 uses #4 and #6. The aerial labels #6 at the street corner. Protect all candidate retained trees until survey/arborist reconciliation.

Blue access is a proposed controlled route, not truck-turning proof. Existing rear ingress/egress easement and ER-1 construction entrance must remain coordinated with neighbors.

01 Sequence group Erection progression Material transfer Keep access open

C Candidate crane

No reach circles are drawn: a circle without a crane model, load, height and configuration would imply unverified capacity. Tree circles are issue markers, not protection radii.

SUPPORTING CONTEXT ONLY - Esri World Imagery retrieved 29 SEP 2026 at the project coordinate; capture date NOT verified | Permit drawings remain authoritative

EL CAMINO REAL (multi-lane arterial)



Imagery source - PROBABLE

Esri World Imagery tile mosaic retrieved 29 SEP 2026 at the coordinate supplied with the prompt (37.3980, -122.1080). Direct Google Earth retrieval is unavailable to automation. Capture date is not verified; site conditions shown may pre- or post-date permit photos. Supporting context only - no dimension is taken from imagery.

Frontage check - CONSISTENT

Imagery shows the multi-lane El Camino Real arterial along the north and Jordan Avenue fronting the site, matching EC-03 crane candidates A/B and the T/S timed-delivery zone. No default El Camino lane setup is supported by either source.

Rear constraint - CONSISTENT

Dense mature tree canopy and neighboring structures close off the rear/southwest boundary; no rear staging corridor exists. Confirms the EC-03 NO NEIGHBOR STAGING band and the tree-hold TPZ items. Tree identity/numbering remains FIELD VERIFY.

What this does NOT prove


Crane capacity, reach, outrigger bearing, street-closure permits, utility clearances, tree survey, or current site state. Candidate zones remain ASSUMED pending lift-plan release. Supplied annotated aerial (EC-01) remains the closer-in-time site reference.



~1.4 km context

Same coordinate at 16x zoom: El Camino corridor, Jordan Ave approach and surrounding residential fabric. Use for orientation awareness only.

The building footprint is not a crane hardstand | Basement excavations, parking voids and utilities control what may carry temporary loads

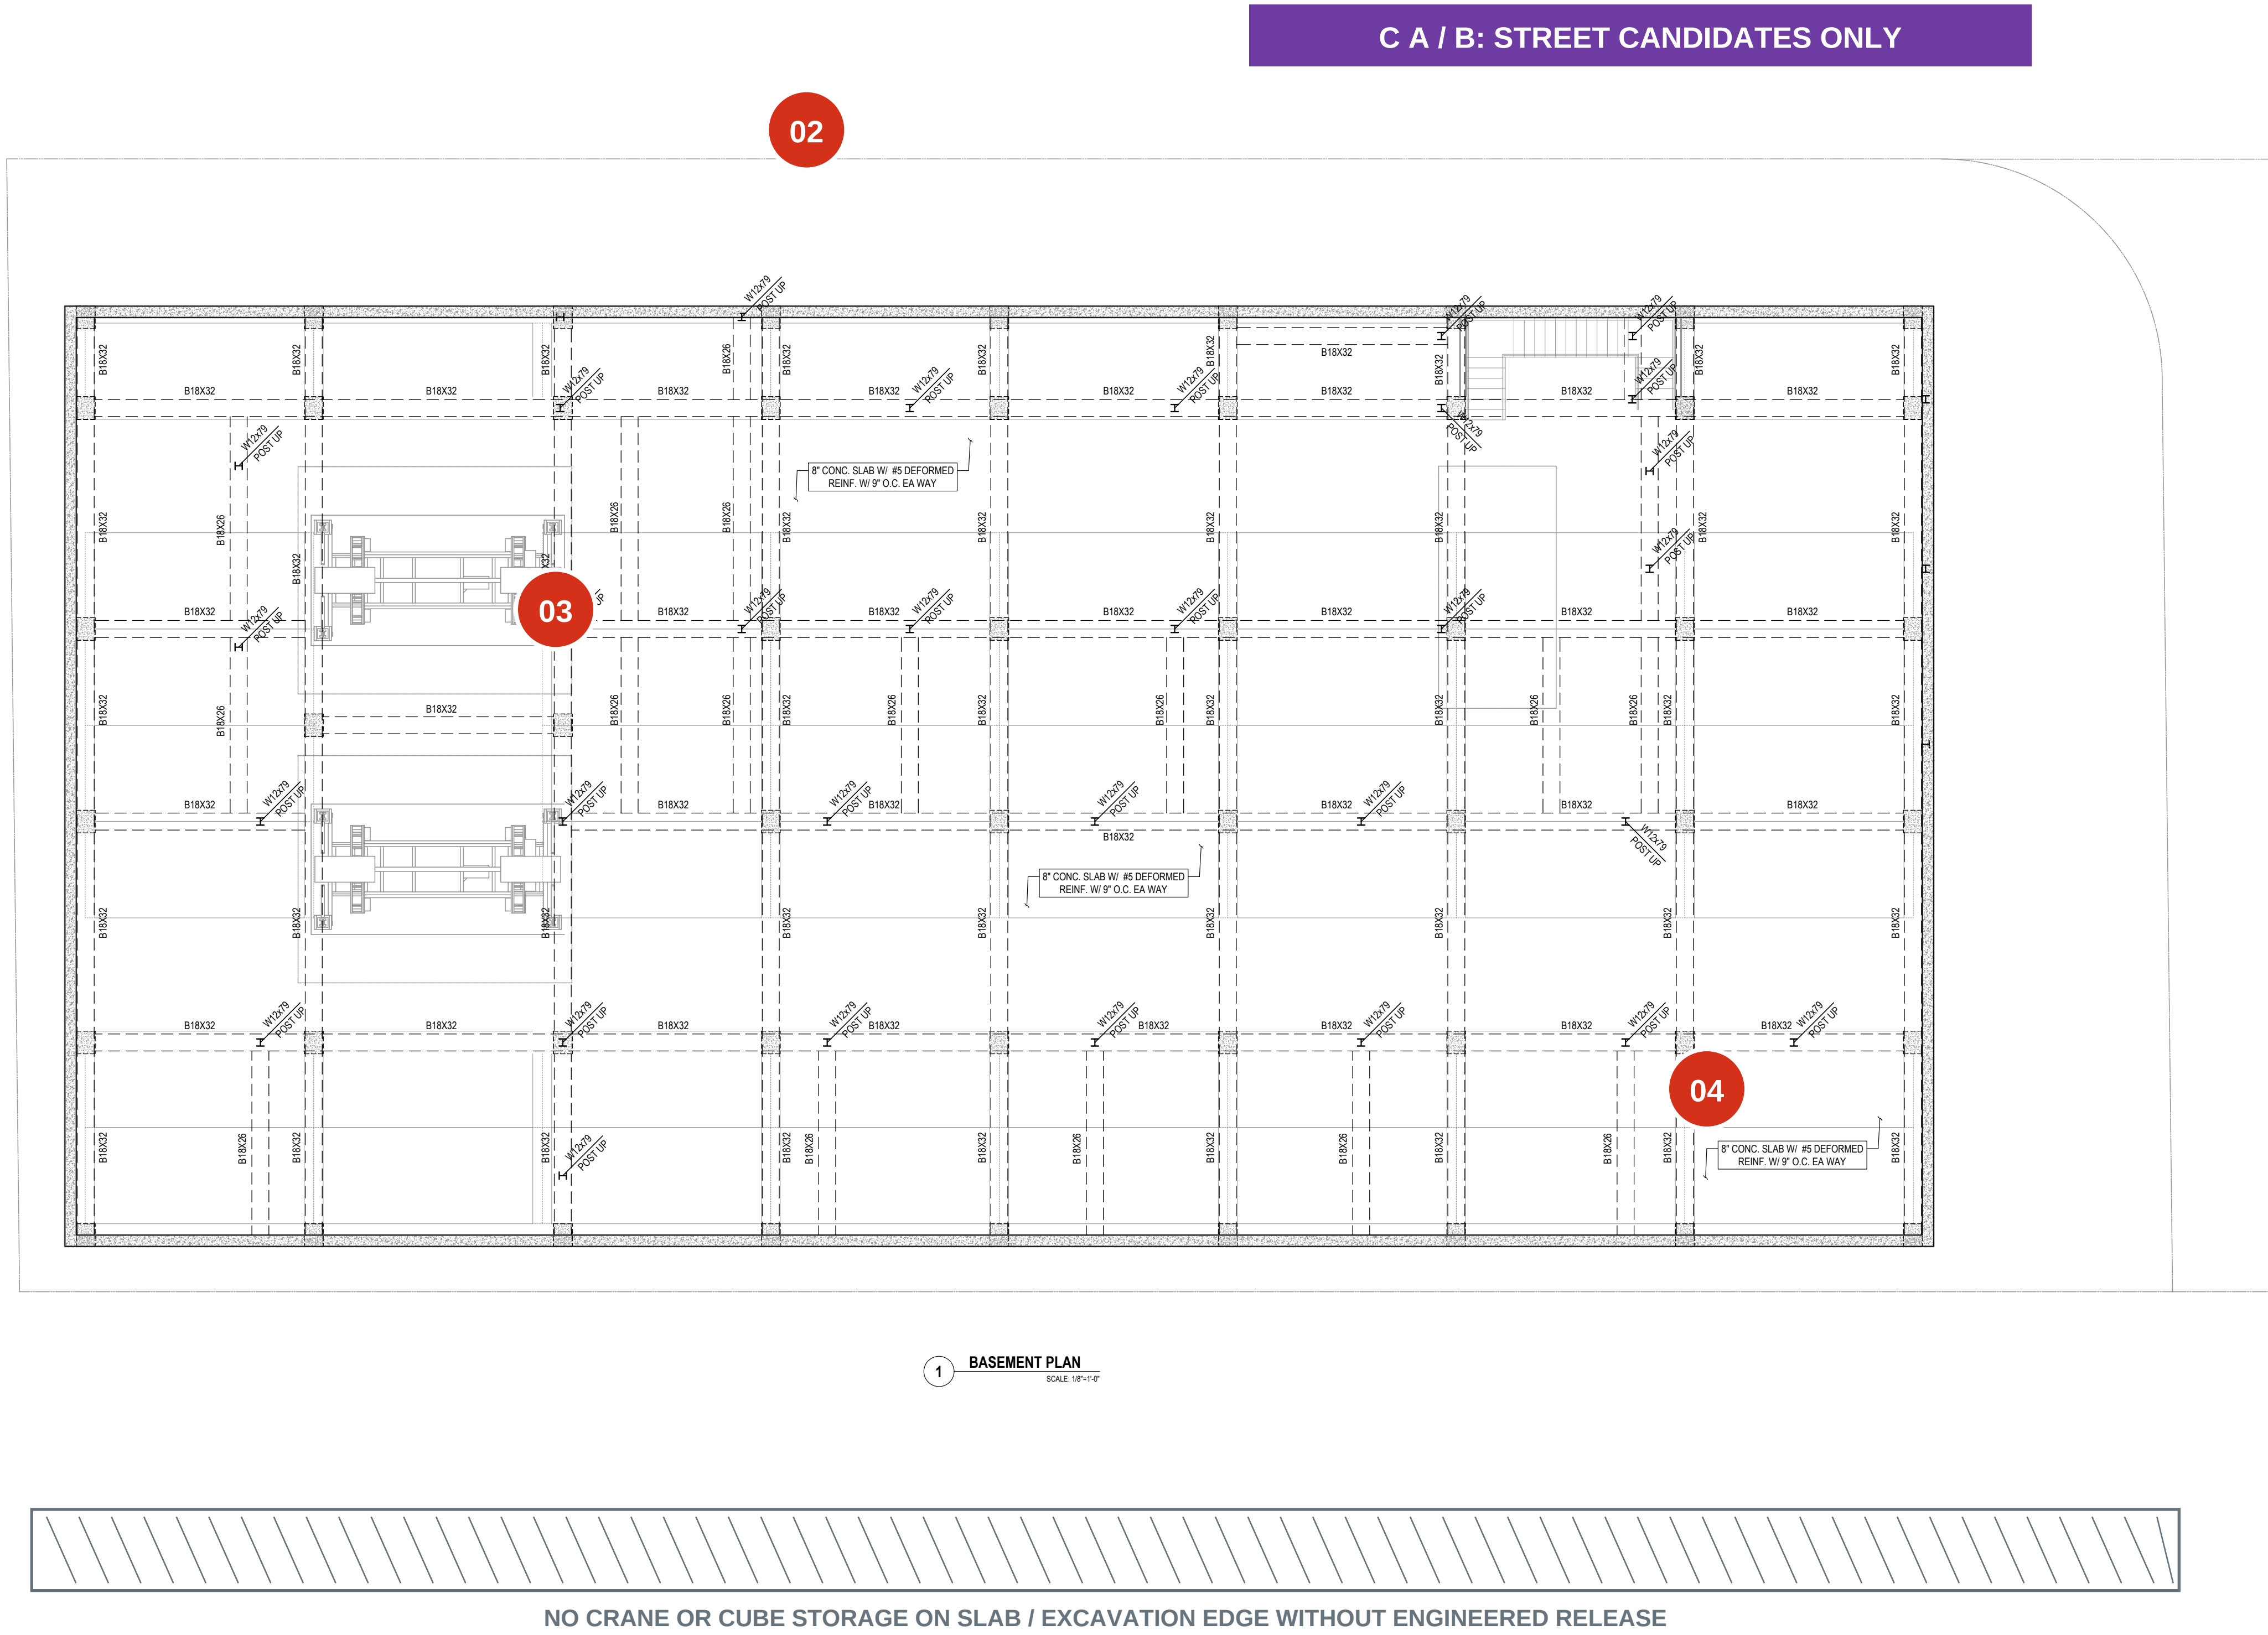


- 01 **Site controls**
- Survey boundaries, utilities and retained trees; install approved protection and access controls. HOLD: tree identity, ROW rights, buried/overhead services and exclusion limits.
- 02 **Substructure**
- Complete engineered shoring, excavation, mat, basement walls and support system. HOLD: excavation surcharge; shoring design and staged removal.
- 03 **Equipment interfaces**
- Resolve automated-parking and electrical equipment installation routes before restricting openings. HOLD: deferred parking equipment; delivery dimensions; transformer access.
- 04 **First-floor release**
- Accept supporting slab/frame, anchors, protected access and approved erection stability plan. HOLD: slab strength, storage loading, crane reactions and full lift envelope.

CONFIRMED: S0.1 refers to excavation extending about 22 ft below grade; the separate S1 shoring concept depicts slab about 19 ft below grade. These describe different limits and do not authorize crane surcharge or a temporary support scheme.

Source shown: S1.1 basement framing, permit p50. Car-lift openings remain protected. Parking vendor plans are deferred/preliminary interfaces, not authorization to fill, bridge or load a void.

Vertical cycle | Close each cell only after its last large delivery

Source A5.1 p38 and A4.1 p33 | Eight floors plus roof terrace/headhouses | Height is not hook-height clearance

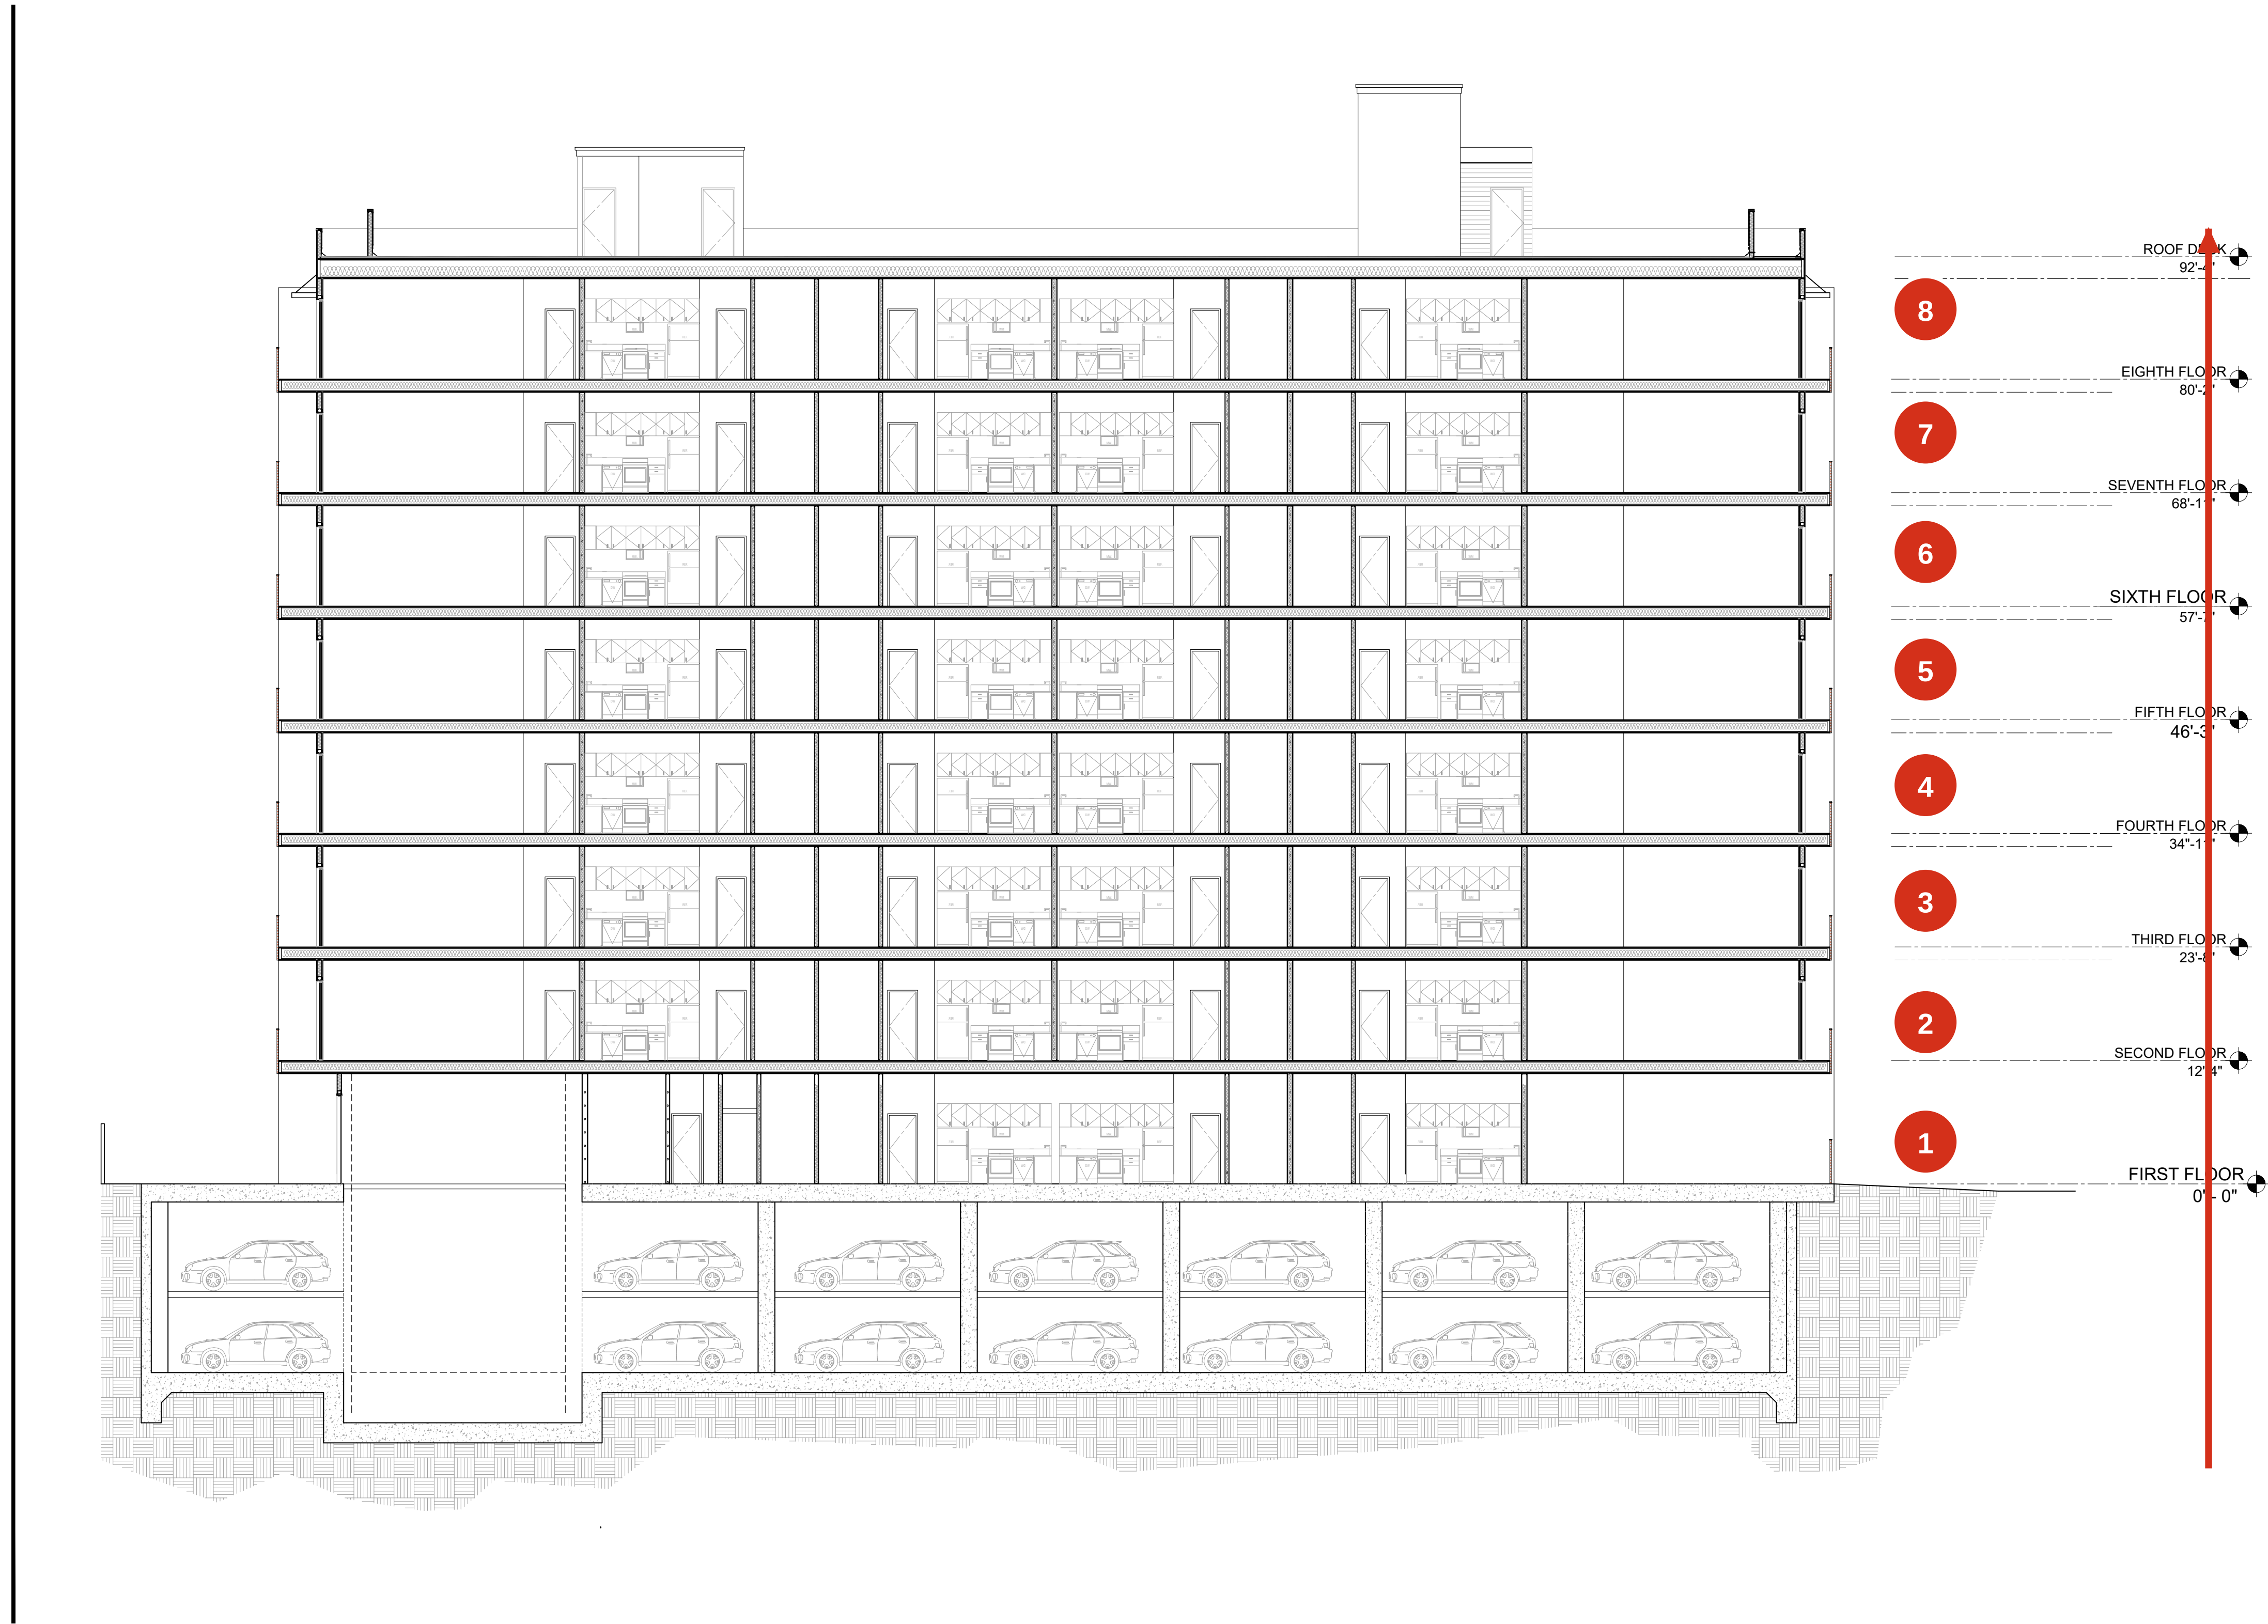

Repeat on every floor

1. Accept the working deck, anchors and approved temporary stability arrangement.
2. Erect an approved steel/CFS cell. Land trapped internals while the receiving space is open.
3. Connect, plumb and brace before release.
4. Close only that cell's joists/deck after a pre-deck inventory check.
5. Accept diaphragm and support capacity before advancing upward.

Critical dependency

No blanket instruction to omit a beam, bearing wall, shear-wall return or diaphragm is given. If a support must precede a panel but blocks its delivery, resolve the panel split or engineered sequence before fabrication.


Two structural holds

RFI-01: no separately named L8 framing sheet was found in S1.2-S1.9. Confirm how L8 and roof supports map to the plans.
RFI-02: S0.1 describes composite deck/concrete diaphragms; floor plans call for Megaboard sheathing. Obtain the governing assembly and temporary load path.

The numbered floor bubbles here identify levels, not erection steps. Every floor has its own globally unique step numbers on EC-06 through EC-13. Crane charts must cover actual pick and set positions at each elevation, including load and rigging height.

Published elevations: L1 0'0"; L2 12'4"; L3 23'8"; L4 34'11"; L5 46'3"; L6 57'7"; L7 68'11"; L8 80'2"; roof deck 92'4". A4.1 also labels top of elevator 109'7 1/4" and overall height 109'9"; reconcile datums for lifting.

Actual architectural plan A1.1, permit p16 | Rear/middle sector first, then El Camino frontage | Proposed groups; shop-panel mapping required

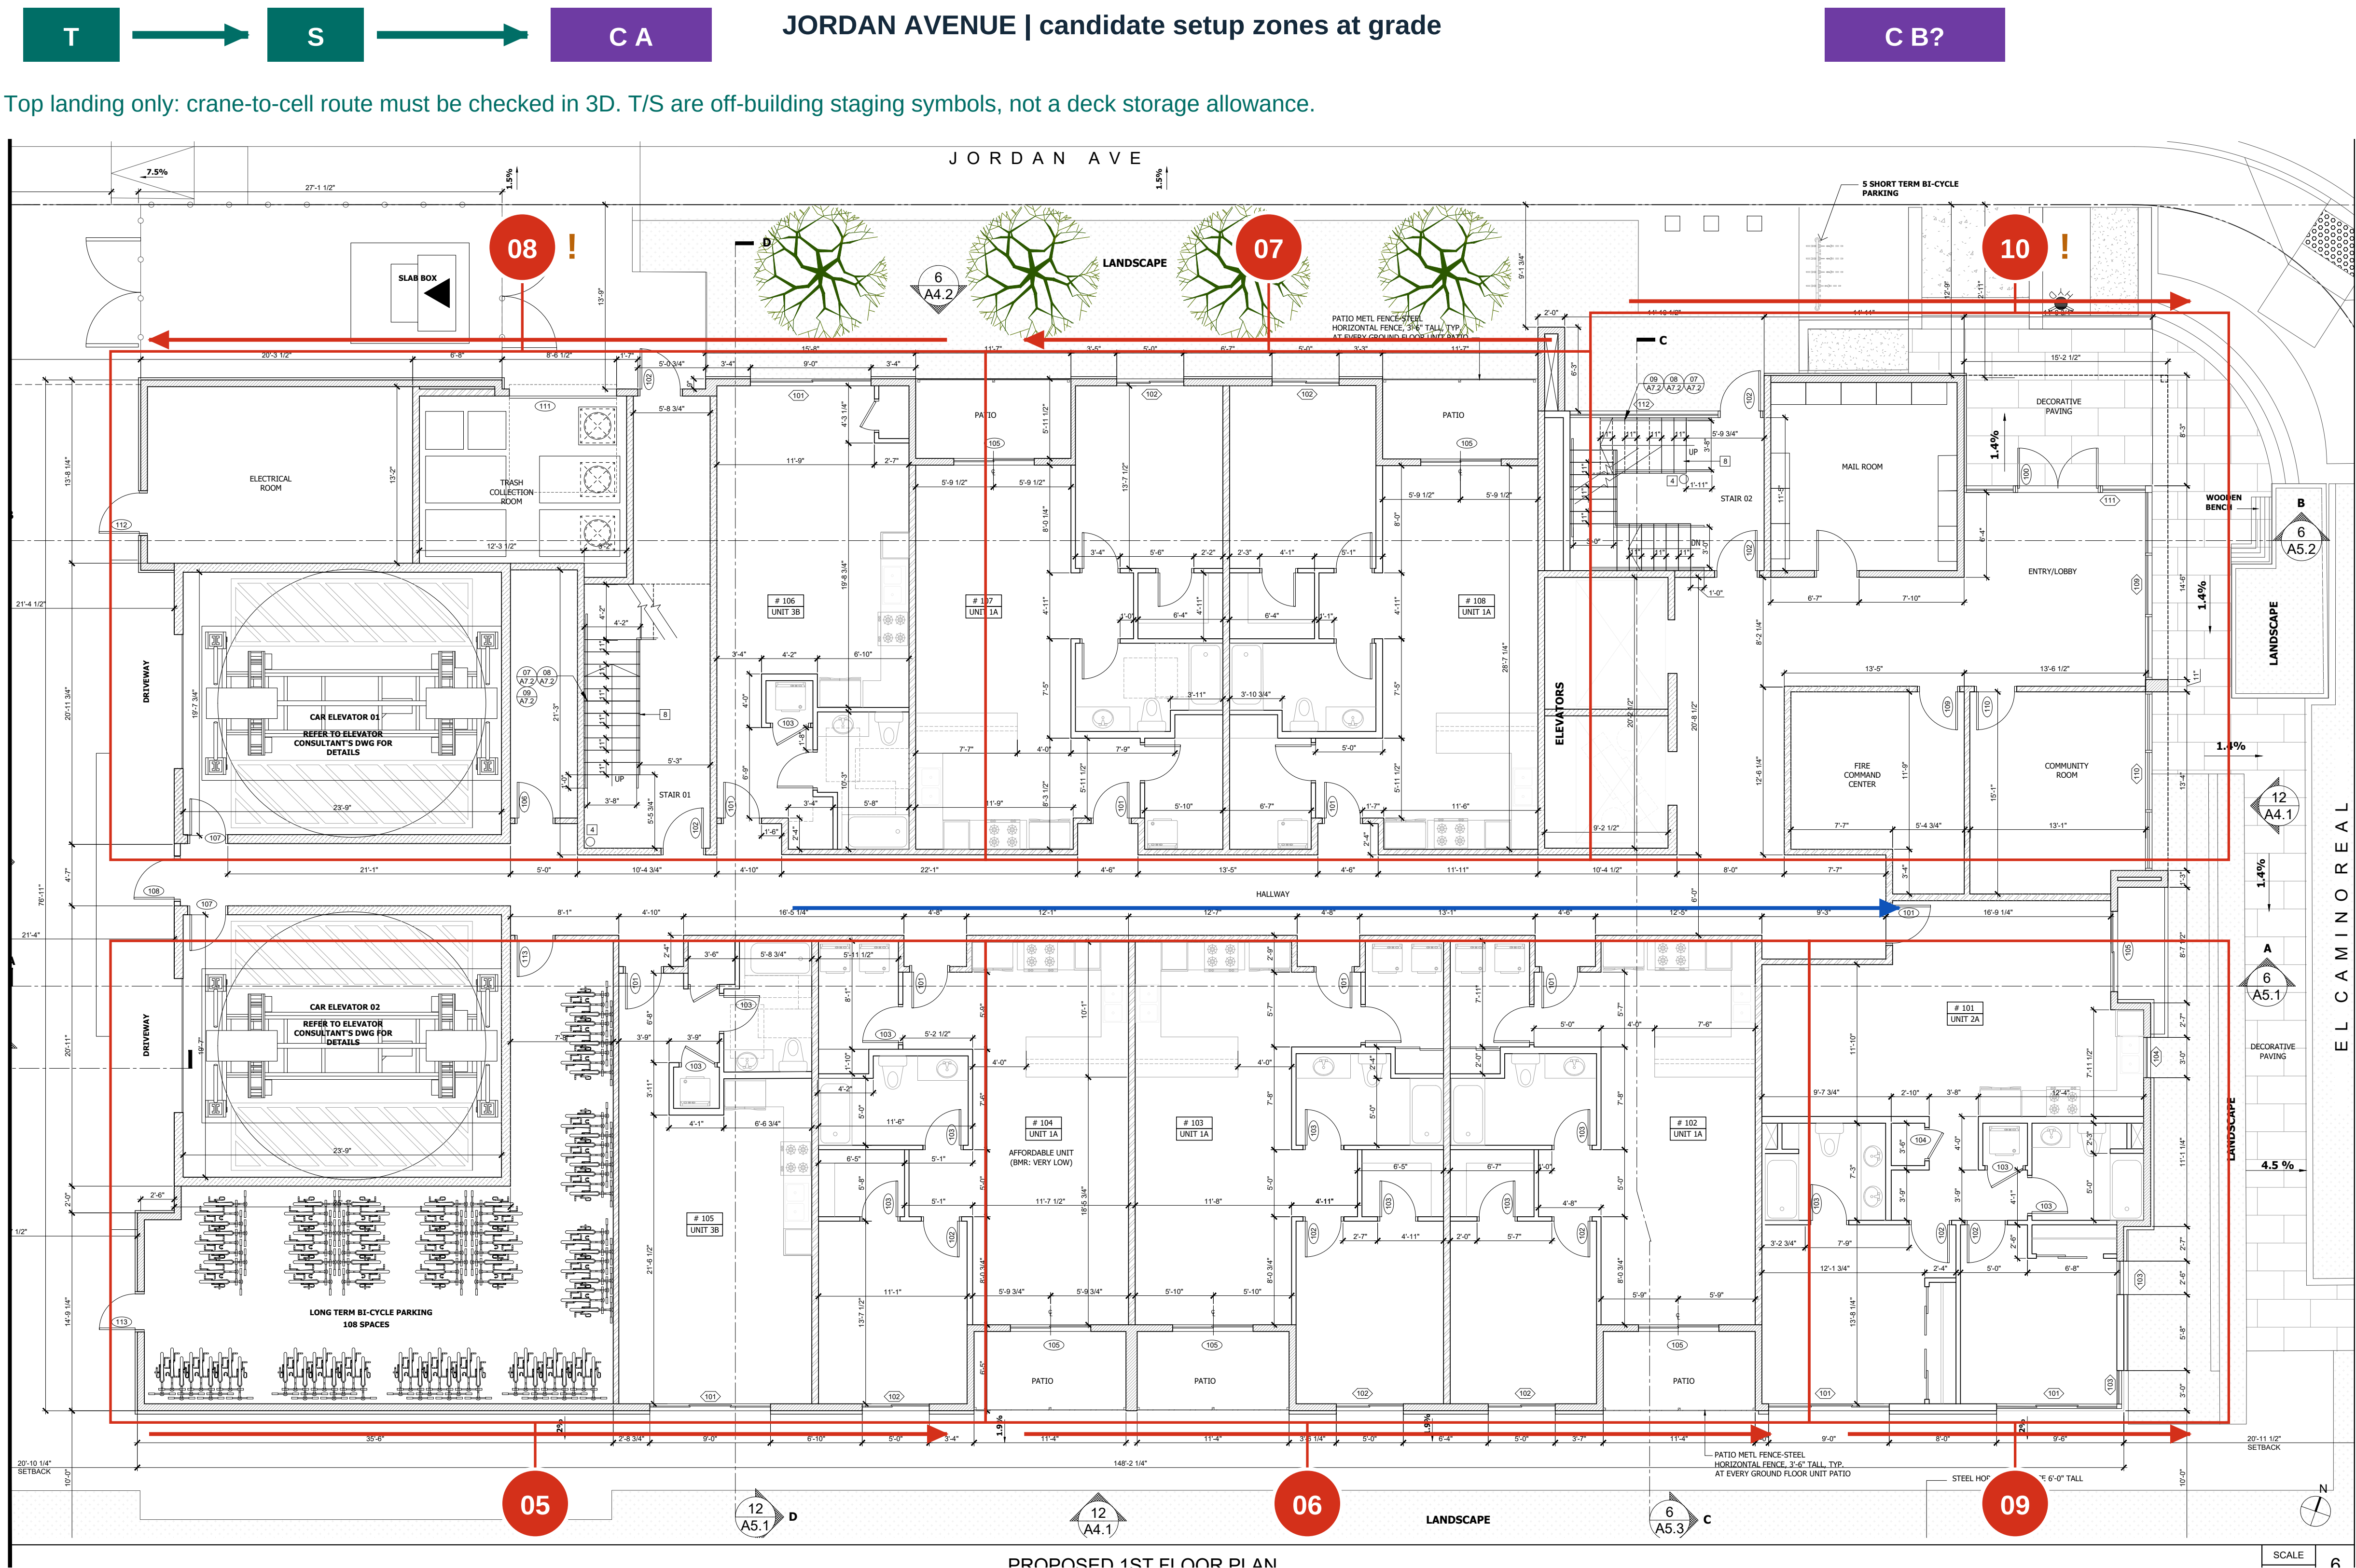

- 05 Neighbor-side rear
- Bike room / unit 105 side. Start stable; protect rear route.
- 06 Neighbor-side middle
- Units 104-102 side. Land all large far-side internals.
- 07 Jordan-side middle
- Units 107-108 side. Close near side after far kit.
- 08 Jordan-side rear
- Electrical / trash / 106 / stair 01. Complete rear sector; prepare R.
- 09 Neighbor-side frontage
- Unit 101 frontage. Verify A coverage or move to B.
- 10 Jordan-side frontage / core
- Lobby / public rooms / stair 02 / elevators. Core interfaces first; last return closes.
- 11 Residual partitions / inventory
- All lift-dependent items installed before overhead closure.
- 12 Joists / diaphragm / release
- Complete each cell only after pre-deck check; approve next level.

CLOSURE: 08 rear-sector last return; 10 front-sector last return. Install cell internals first. Permanent door/stair routes stay usable.


BLUE: preserve central corridor / stair routes for people and small items. Follow actual plan jogs. Group outlines are schematic; include all associated recesses and returns.



Transitions: far middle to near middle = change workforce; near rear to far front = new sector / R if needed. Short plan arrows show local progression, not load-flight paths.

HOLD: floor-specific steel/CFS support, bracing and crane coverage. If A covers all groups, omit R. If not, stabilize rear/middle cells, then relocate A to B for front groups.


Actual architectural plan A1.2, permit p18 | Rear/middle sector first, then El Camino frontage | Proposed groups; shop-panel mapping required

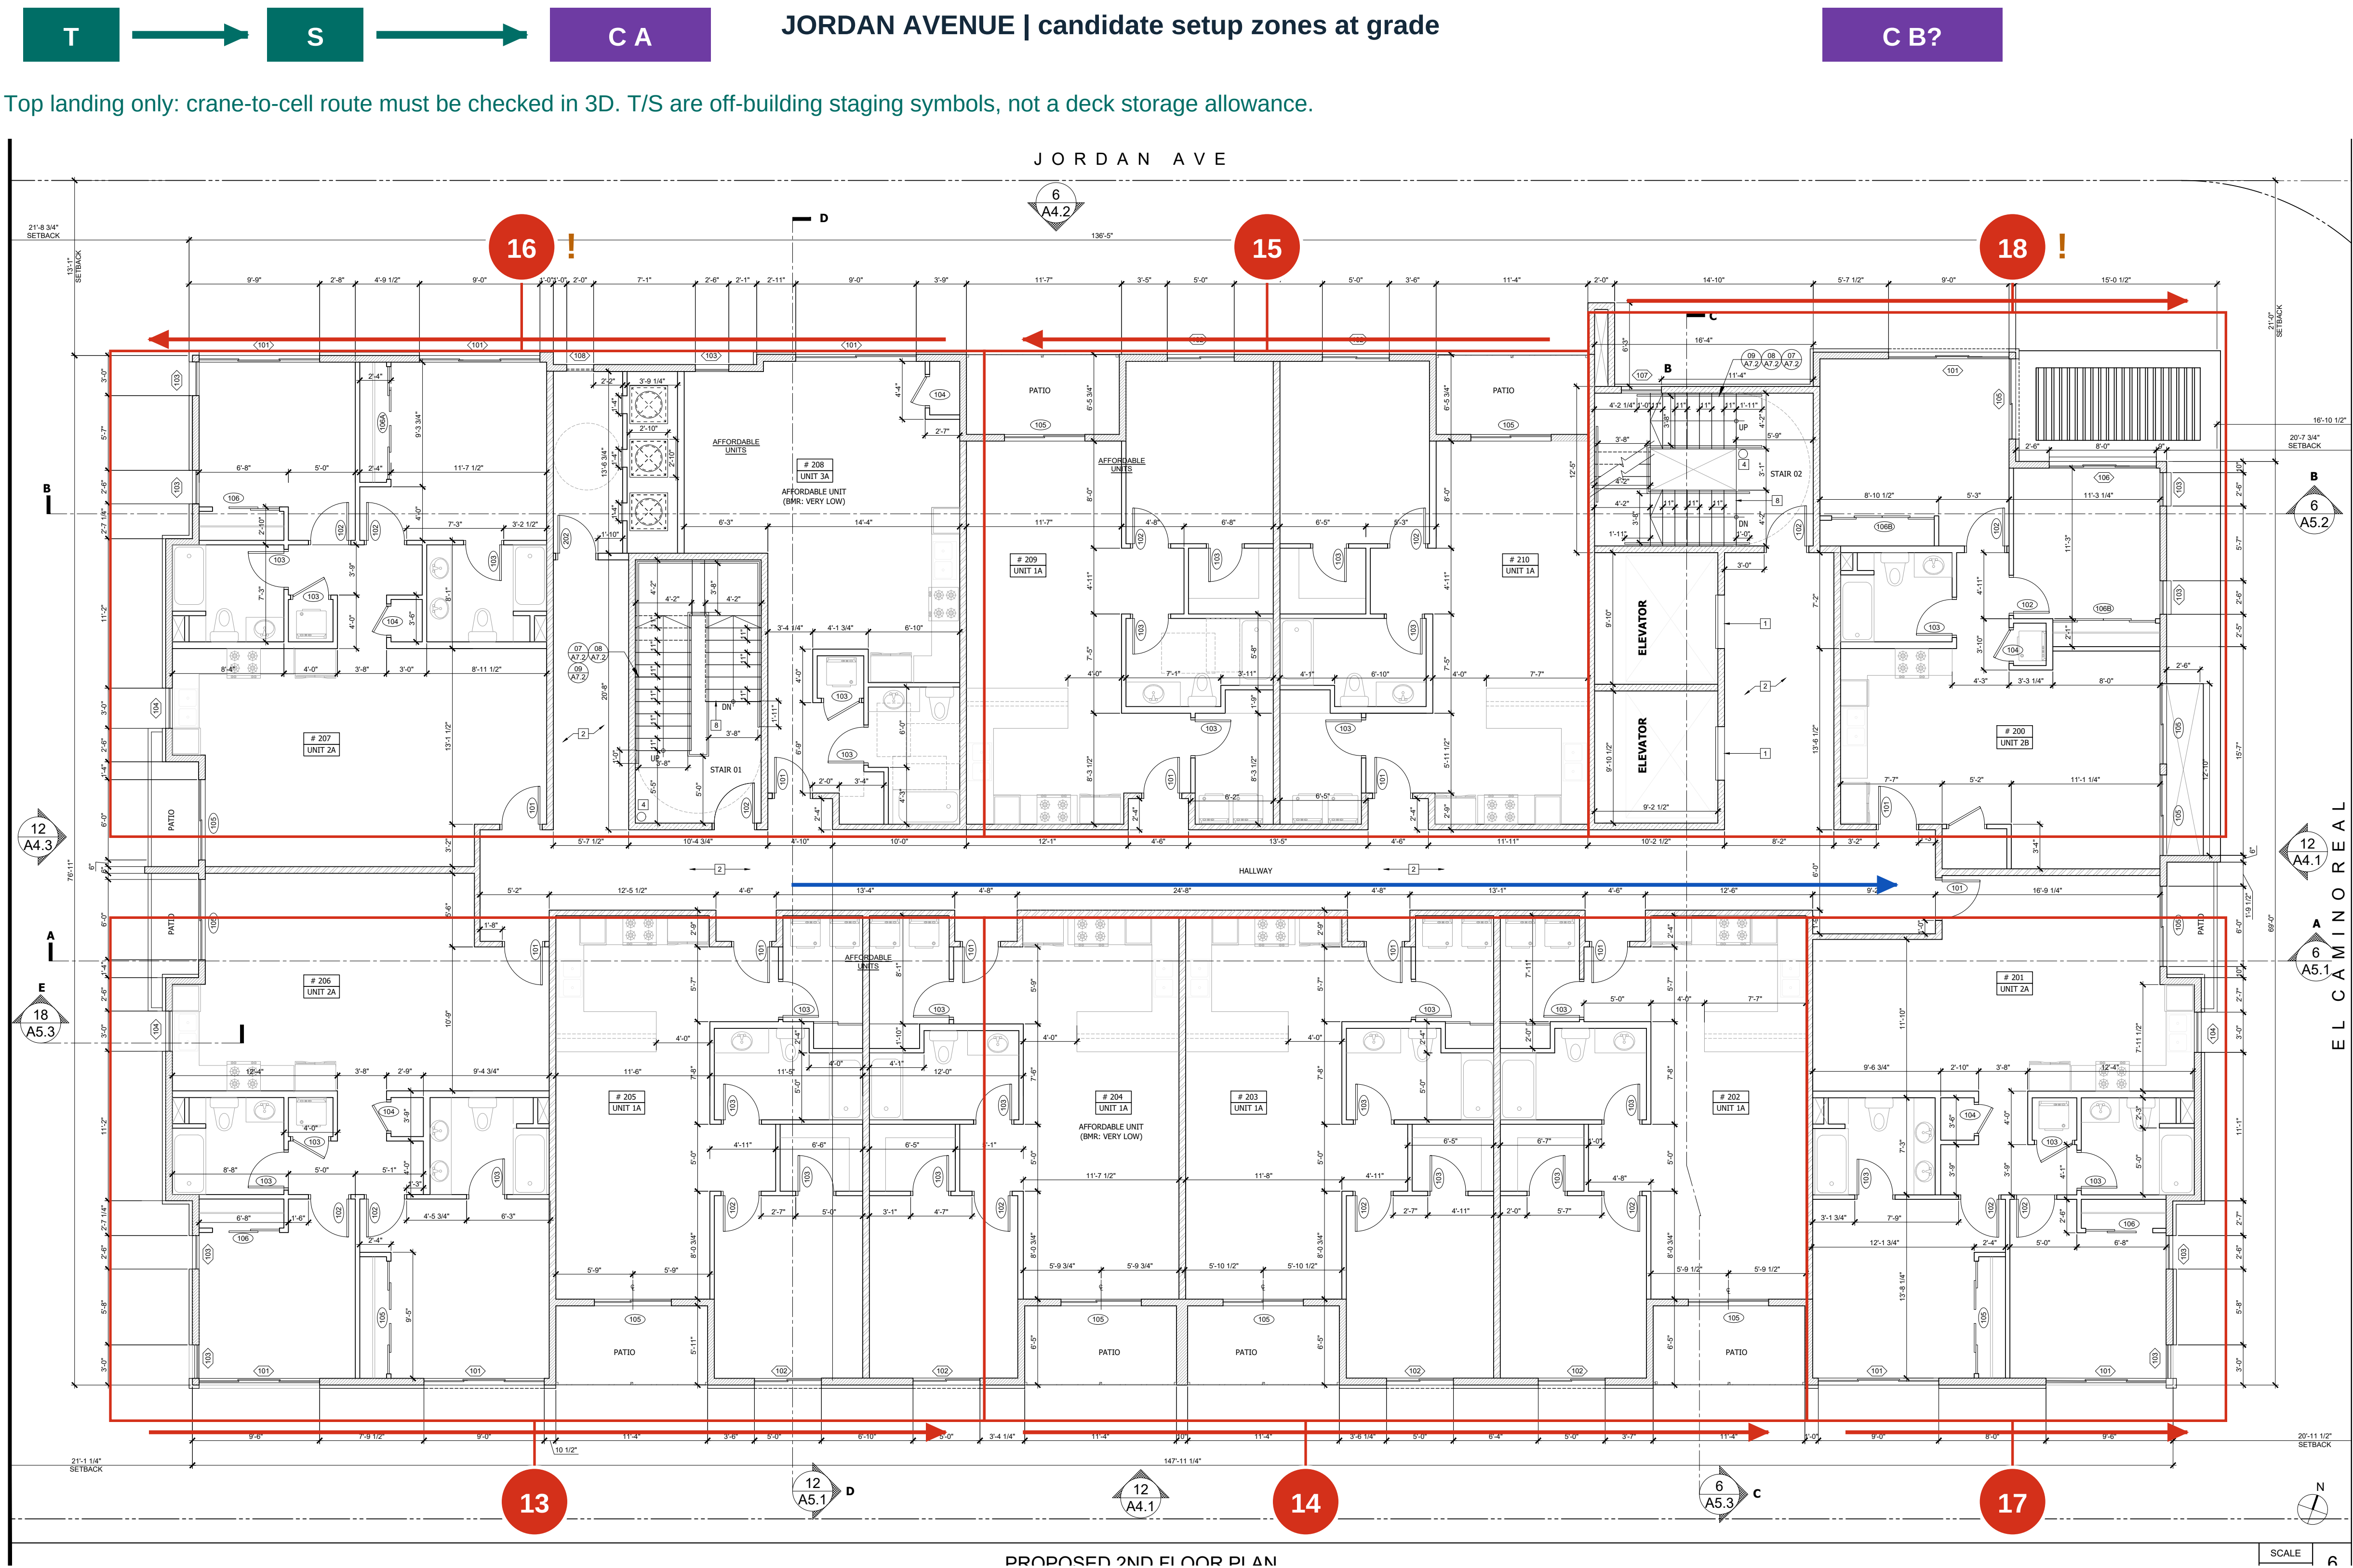

- 13 Neighbor-side rear
Units 206-205 side. Start stable; protect rear route.
- 14 Neighbor-side middle
Units 204-202 side. Land all large far-side internals.
- 15 Jordan-side middle
Units 209-210 side. Close near side after far kit.
- 16 Jordan-side rear
Units 207-208 / stair 01. Complete rear sector; prepare R.
- 17 Neighbor-side frontage
Unit 201 frontage. Verify A coverage or move to B.
- 18 Jordan-side frontage / core
Unit 200 / stair 02 / elevators. Core interfaces first; last return closes.
- 19 Residual partitions / inventory
All lift-dependent items installed before overhead closure.
- 20 Joists / diaphragm / release
Complete each cell only after pre-deck check; approve next level.

CLOSURE: 16 rear-sector last return; 18 front-sector last return. Install cell internals first. Permanent door/stair routes stay usable.


BLUE: preserve central corridor / stair routes for people and small items. Follow actual plan jogs. Group outlines are schematic; include all associated recesses and returns.



HOLD: floor-specific steel/CFS support, bracing and crane coverage. If A covers all groups, omit R. If not, stabilize rear/middle cells, then relocate A to B for front groups.

Transitions: far middle to near middle = change workforce; near rear to far front = new sector / R if needed. Short plan arrows show local progression, not load-flight paths.

Actual architectural plan A1.3, permit p19 | Rear/middle sector first, then El Camino frontage | Proposed groups; shop-panel mapping required

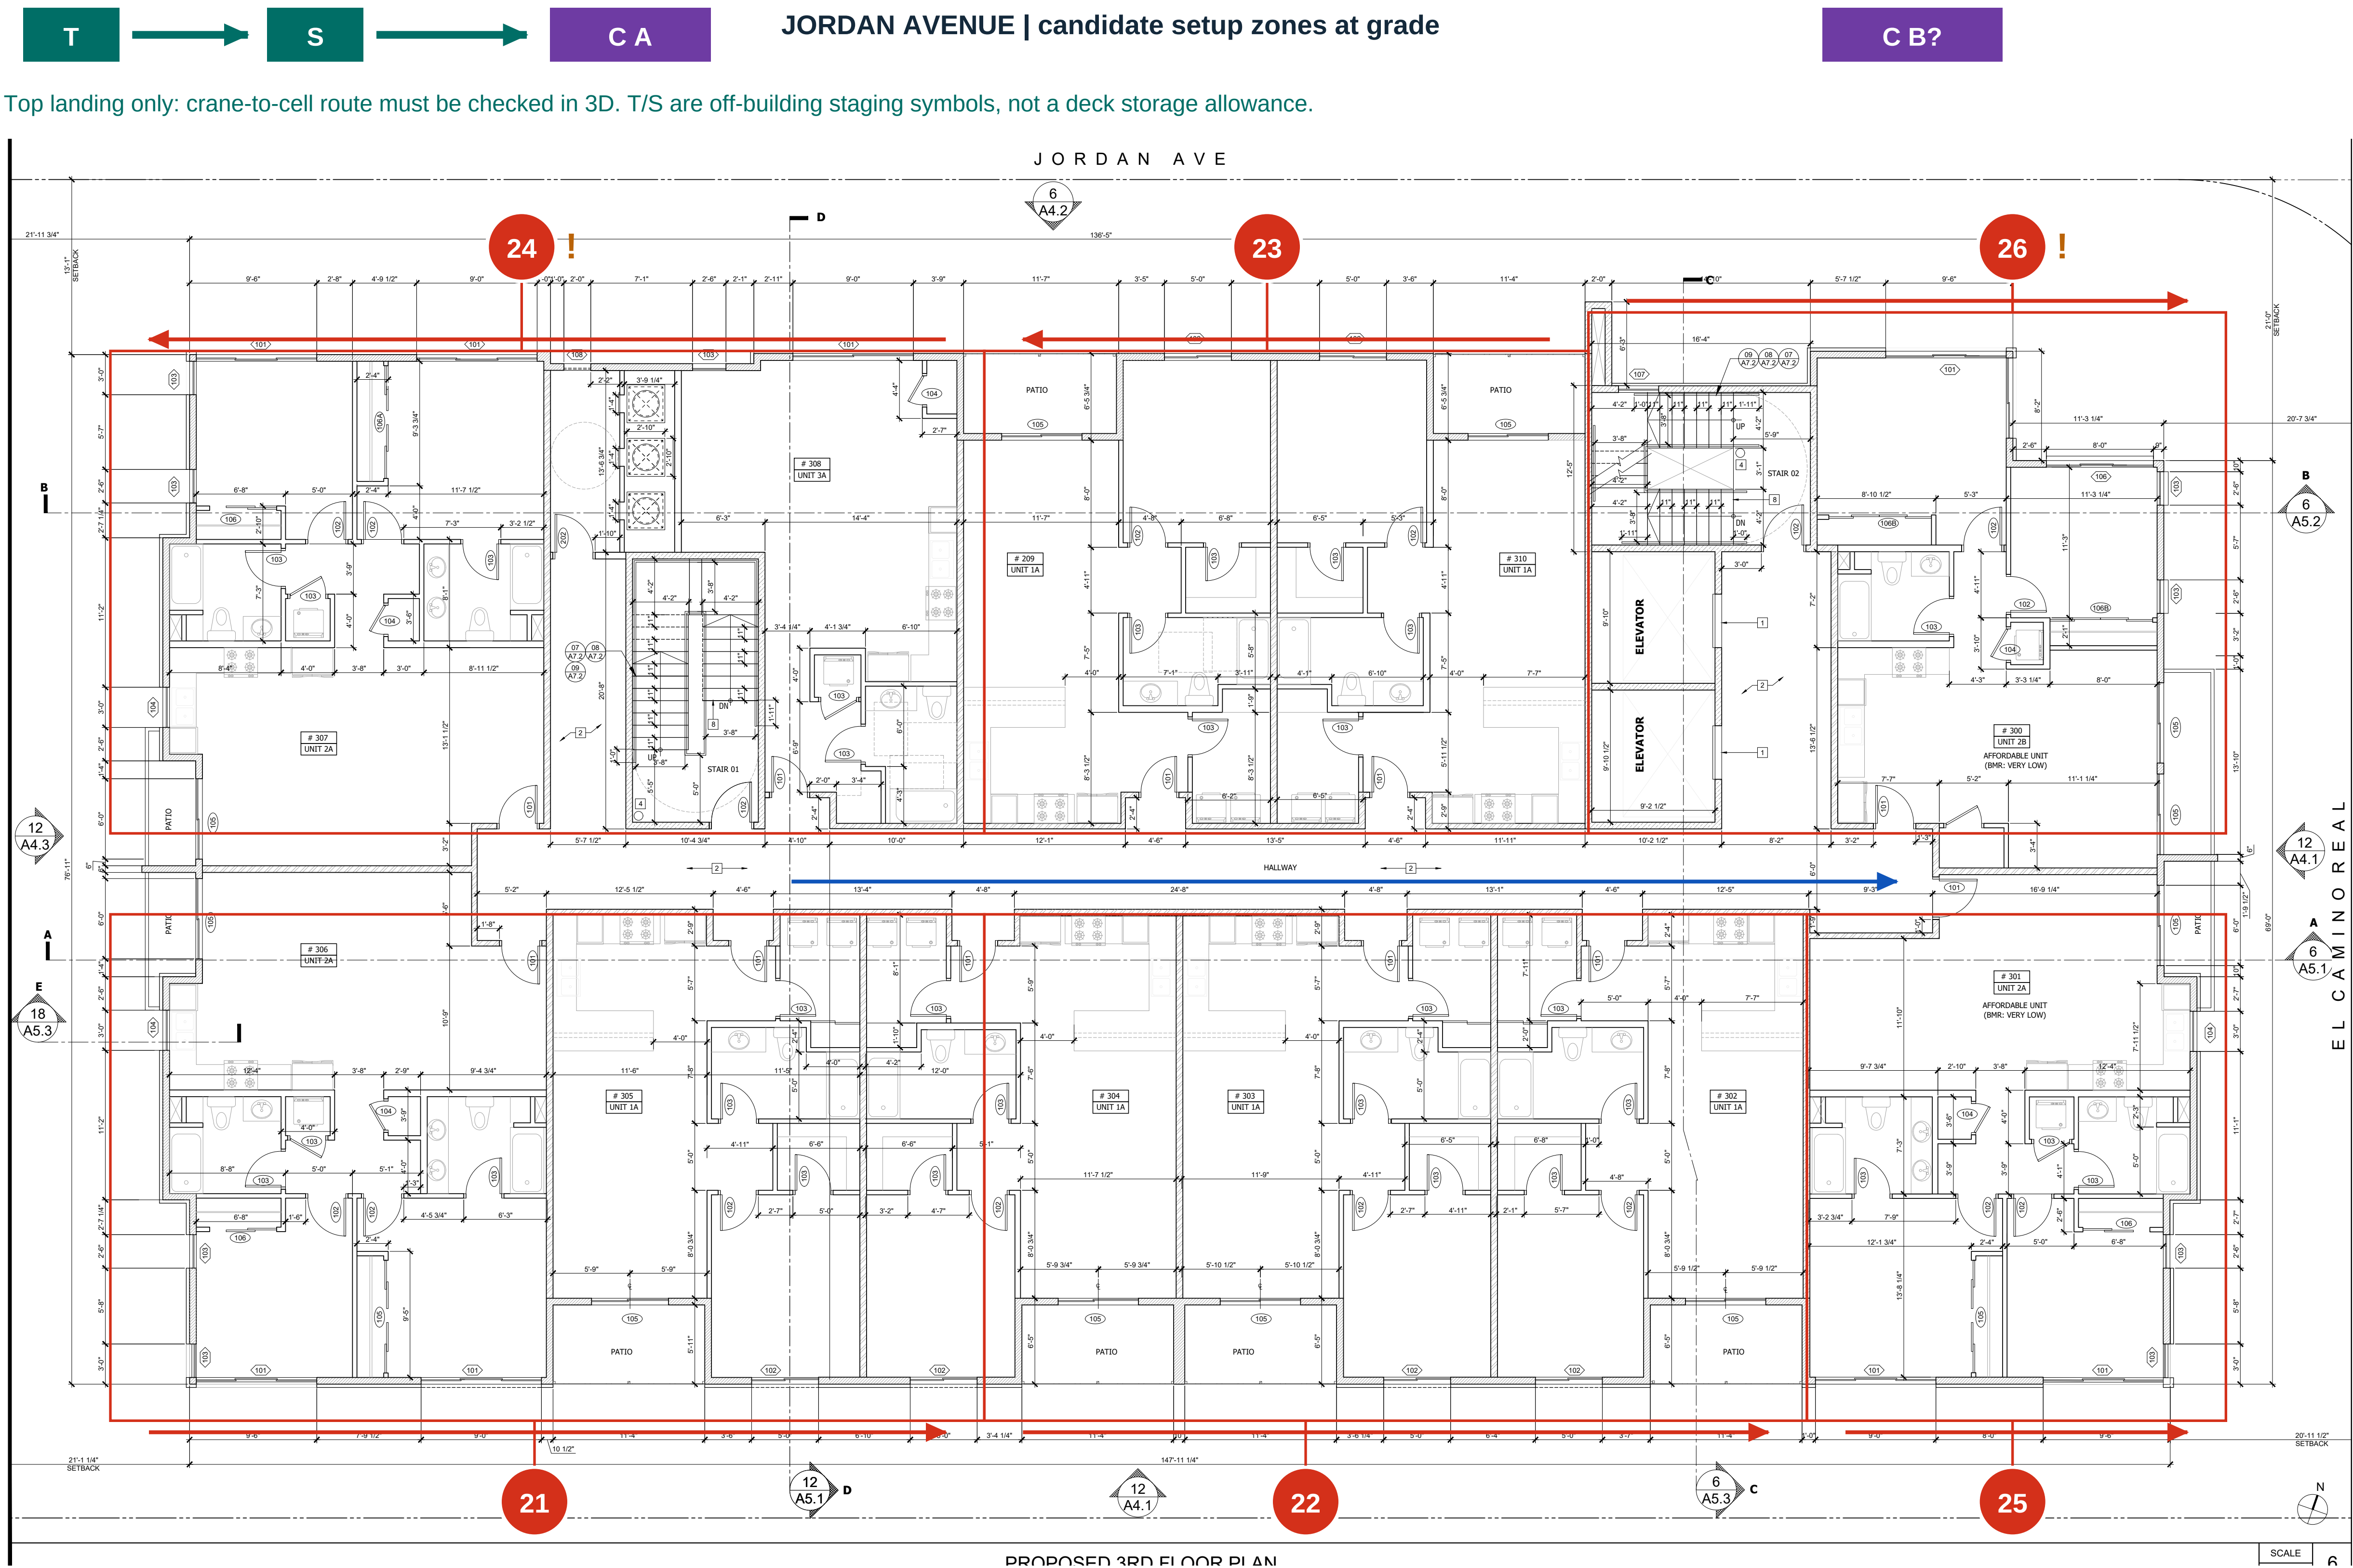

BLUE: preserve central corridor / stair routes for people and small items. Follow actual plan jogs. Group outlines are schematic; include all associated recesses and returns.




Transitions: far middle to near middle = change workforce; near rear to far front = new sector / R if needed. Short plan arrows show local progression, not load-flight paths.

- 21 Neighbor-side rear
Units 306-305 side. Start stable; protect rear route.
- 22 Neighbor-side middle
Units 304-302 side. Land all large far-side internals.
- 23 Jordan-side middle
Units 309-310 side. Close near side after far kit.
- 24 Jordan-side rear
Units 307-308 / stair 01. Complete rear sector; prepare R.
- 25 Neighbor-side frontage
Unit 301 frontage. Verify A coverage or move to B.
- 26 Jordan-side frontage / core
Unit 300 / stair 02 / elevators. Core interfaces first; last return closes.
- 27 Residual partitions / inventory
All lift-dependent items installed before overhead closure.
- 28 Joists / diaphragm / release
Complete each cell only after pre-deck check; approve next level.

CLOSURE: 24 rear-sector last return; 26 front-sector last return. Install cell internals first. Permanent door/stair routes stay usable.

HOLD: floor-specific steel/CFS support, bracing and crane coverage. If A covers all groups, omit R. If not, stabilize rear/middle cells, then relocate A to B for front groups.

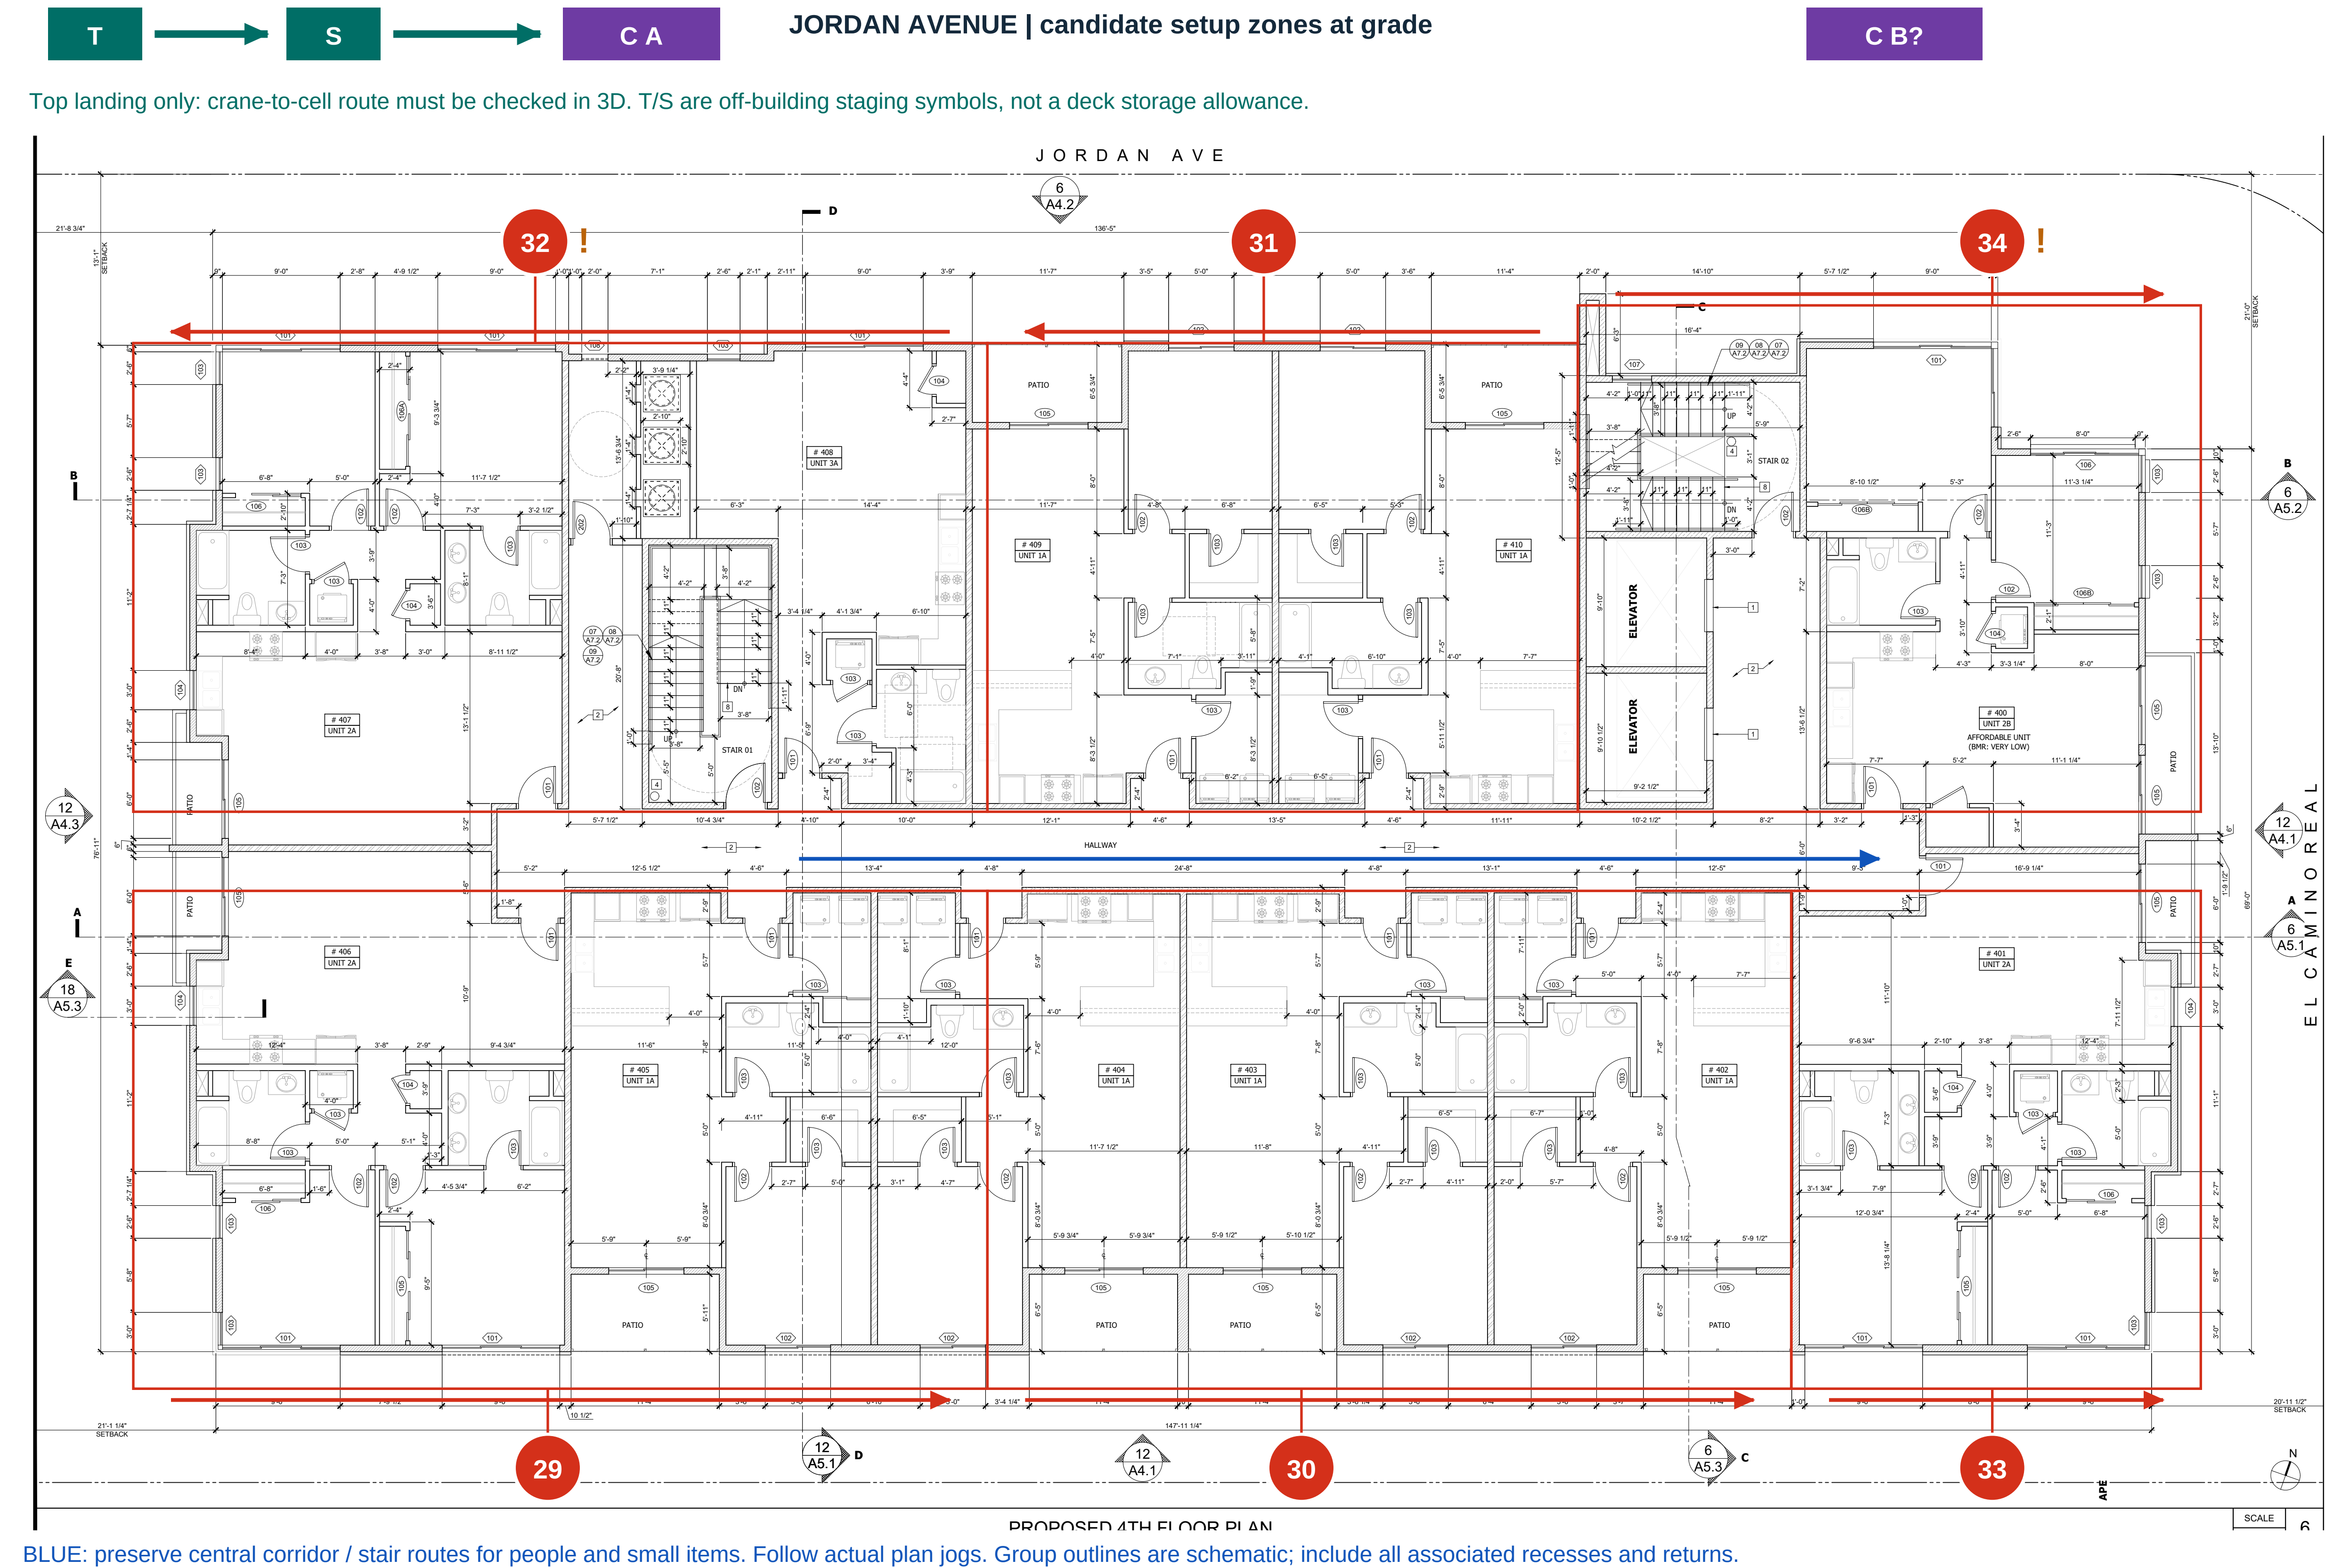

- 29

Neighbor-side rear

Units 406-405 side. Start stable; protect rear route.
- 30

Neighbor-side middle

Units 404-402 side. Land all large far-side internals.
- 31

Jordan-side middle

Units 409-410 side. Close near side after far kit.
- 32

Jordan-side rear

Units 407-408 / stair 01. Complete rear sector; prepare R.
- 33

Neighbor-side frontage

Unit 401 frontage. Verify A coverage or move to B.
- 34

Jordan-side frontage / core

Unit 400 / stair 02 / elevators. Core interfaces first; last return closes.
- 35

Residual partitions / inventory

All lift-dependent items installed before overhead closure.
- 36

Joists / diaphragm / release

Complete each cell only after pre-deck check; approve next level.


CLOSURE: 32 rear-sector last return; 34 front-sector last return. Install cell internals first. Permanent door/stair routes stay usable.



Transitions: far middle to near middle = change workforce; near rear to far front = new sector / R if needed. Short plan arrows show local progression, not load-flight paths.

HOLD: floor-specific steel/CFS support, bracing and crane coverage. If A covers all groups, omit R. If not, stabilize rear/middle cells, then relocate A to B for front groups.

Actual architectural plan A1.5, permit p21 | Rear/middle sector first, then El Camino frontage | Proposed groups; shop-panel mapping required

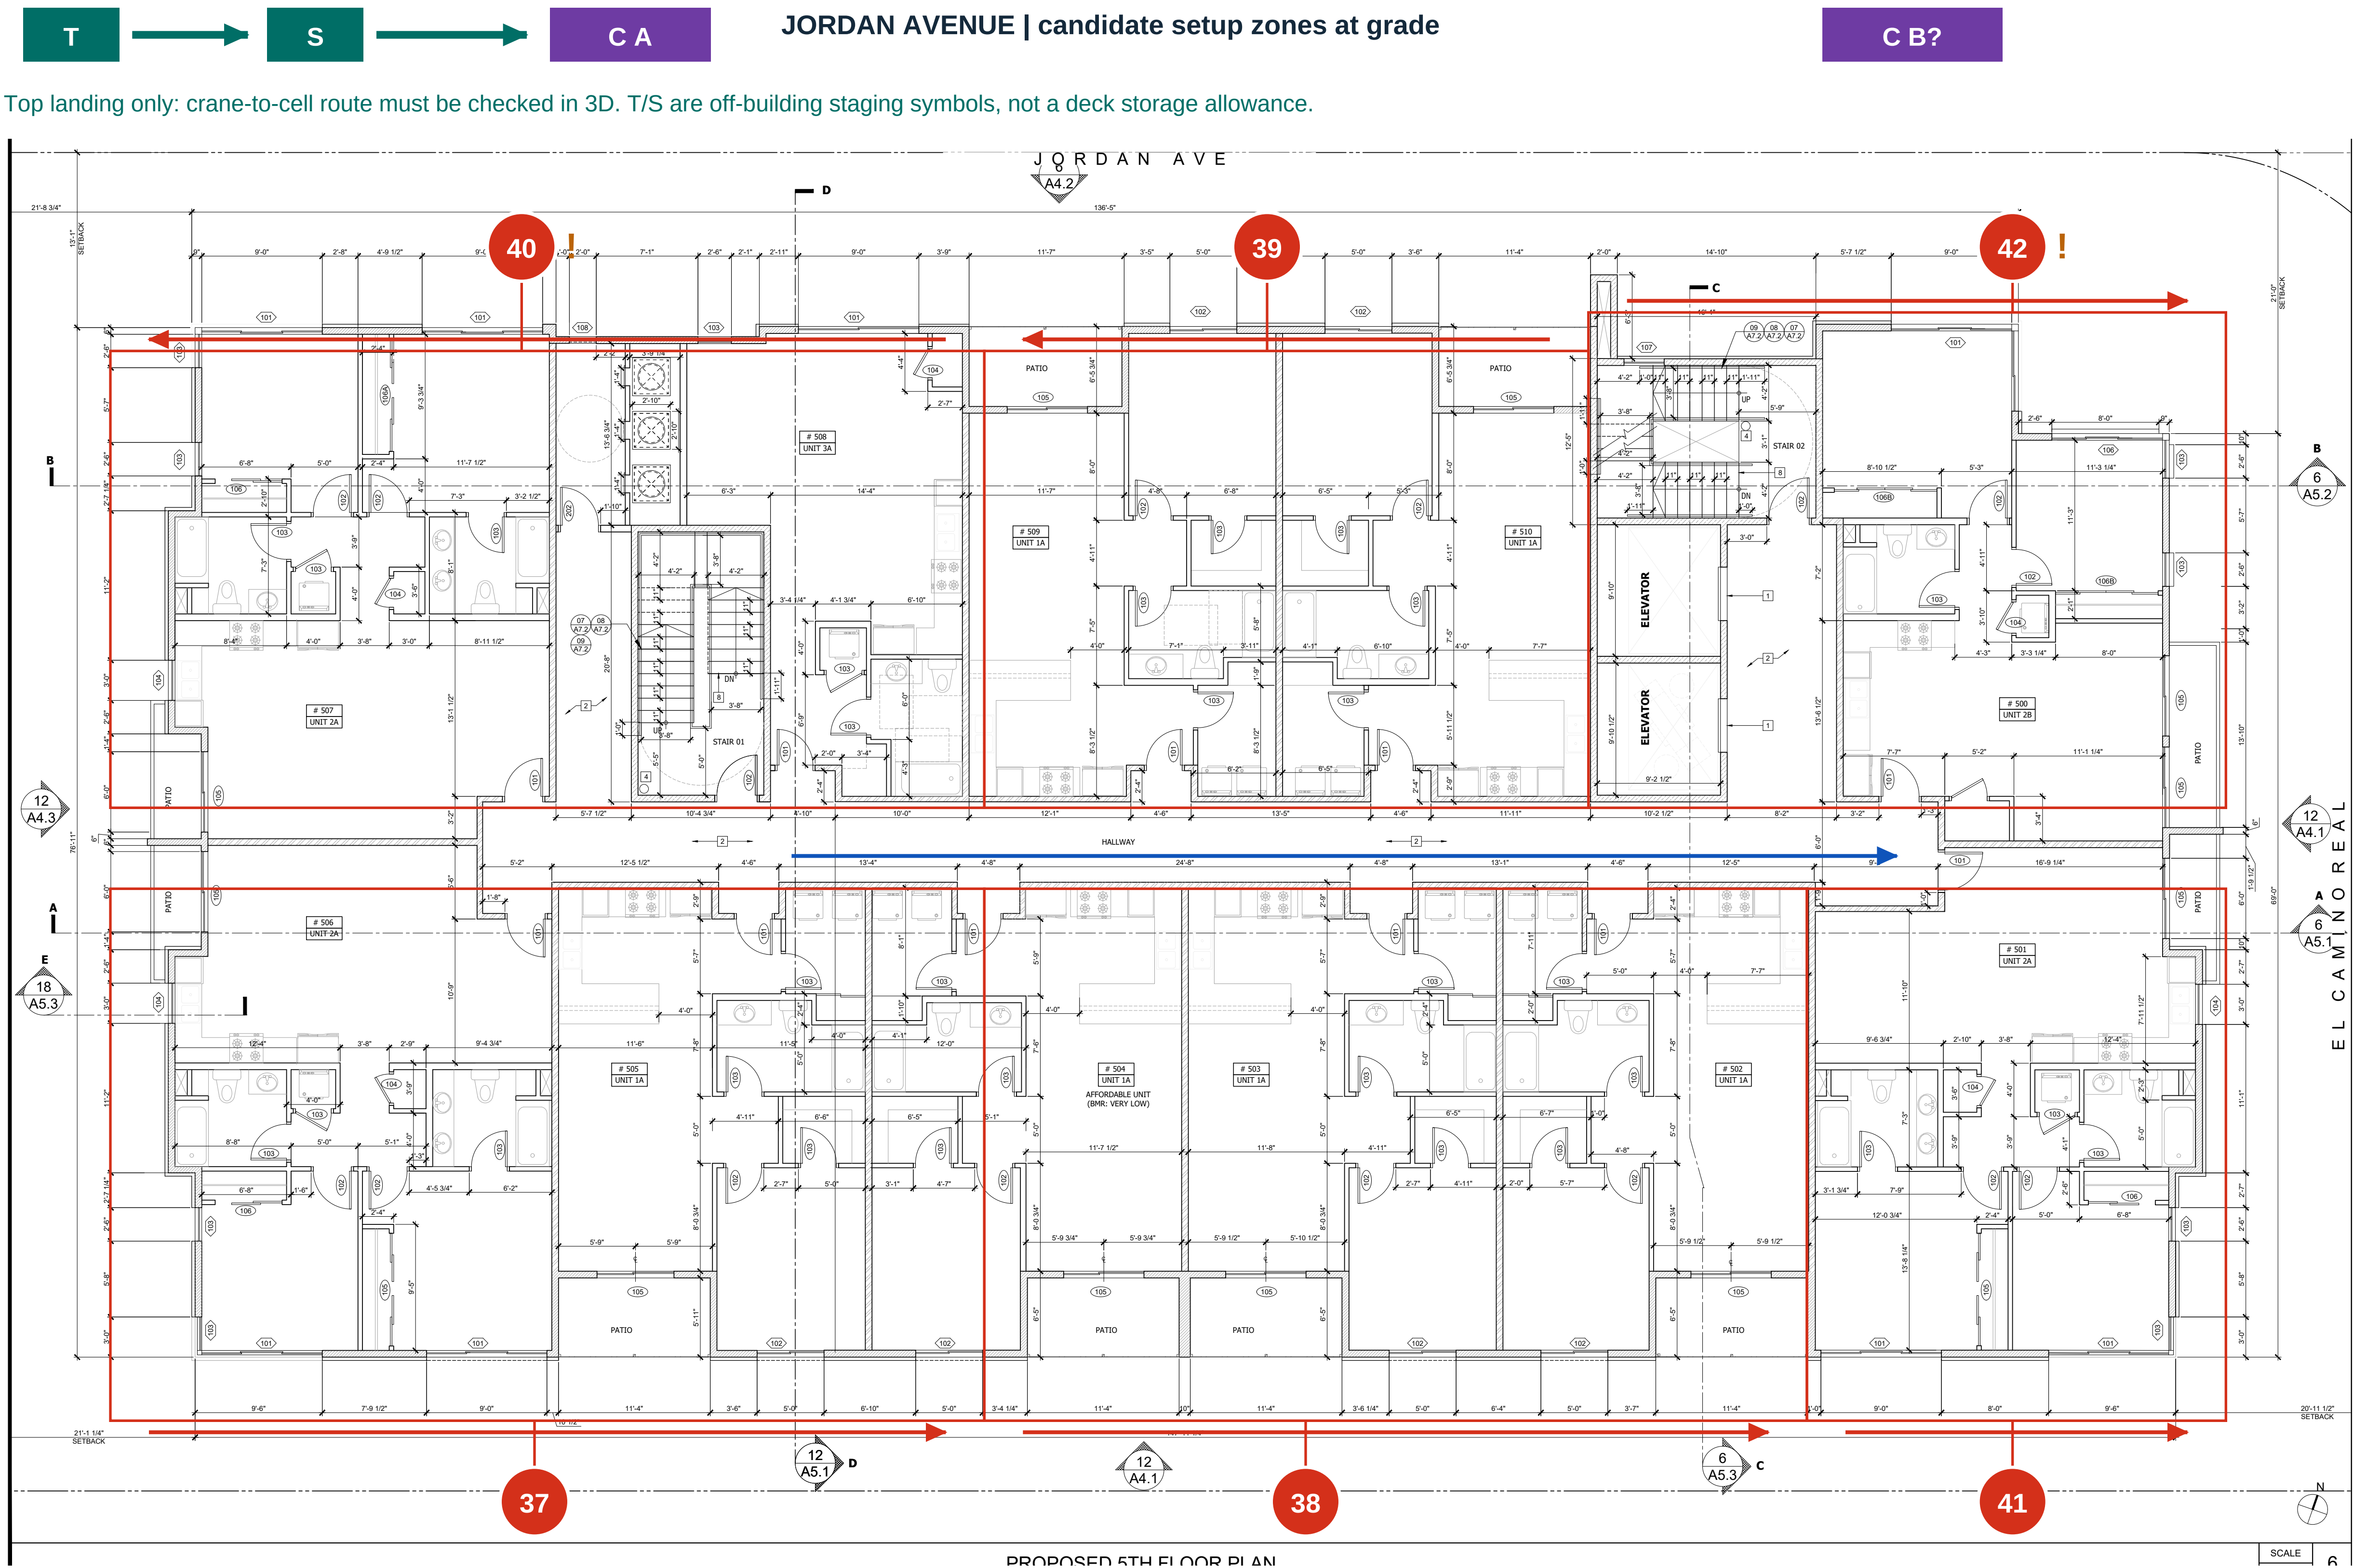

- 37

Neighbor-side rear

Units 506-505 side. Start stable; protect rear route.
- 38

Neighbor-side middle

Units 504-502 side. Land all large far-side internals.
- 39

Jordan-side middle

Units 509-510 side. Close near side after far kit.
- 40

Jordan-side rear

Units 507-508 / stair 01. Complete rear sector; prepare R.
- 41

Neighbor-side frontage

Unit 501 frontage. Verify A coverage or move to B.
- 42

Jordan-side frontage / core

Unit 500 / stair 02 / elevators. Core interfaces first; last return closes.
- 43

Residual partitions / inventory

All lift-dependent items installed before overhead closure.
- 44

Joists / diaphragm / release

Complete each cell only after pre-deck check; approve next level.

CLOSURE: 40 rear-sector last return; 42 front-sector last return. Install cell internals first. Permanent door/stair routes stay usable.


BLUE: preserve central corridor / stair routes for people and small items. Follow actual plan jogs. Group outlines are schematic; include all associated recesses and returns.



Transitions: far middle to near middle = change workforce; near rear to far front = new sector / R if needed. Short plan arrows show local progression, not load-flight paths.

HOLD: floor-specific steel/CFS support, bracing and crane coverage. If A covers all groups, omit R. If not, stabilize rear/middle cells, then relocate A to B for front groups.

Actual architectural plan A1.6, permit p22 | Rear/middle sector first, then El Camino frontage | Proposed groups; shop-panel mapping required

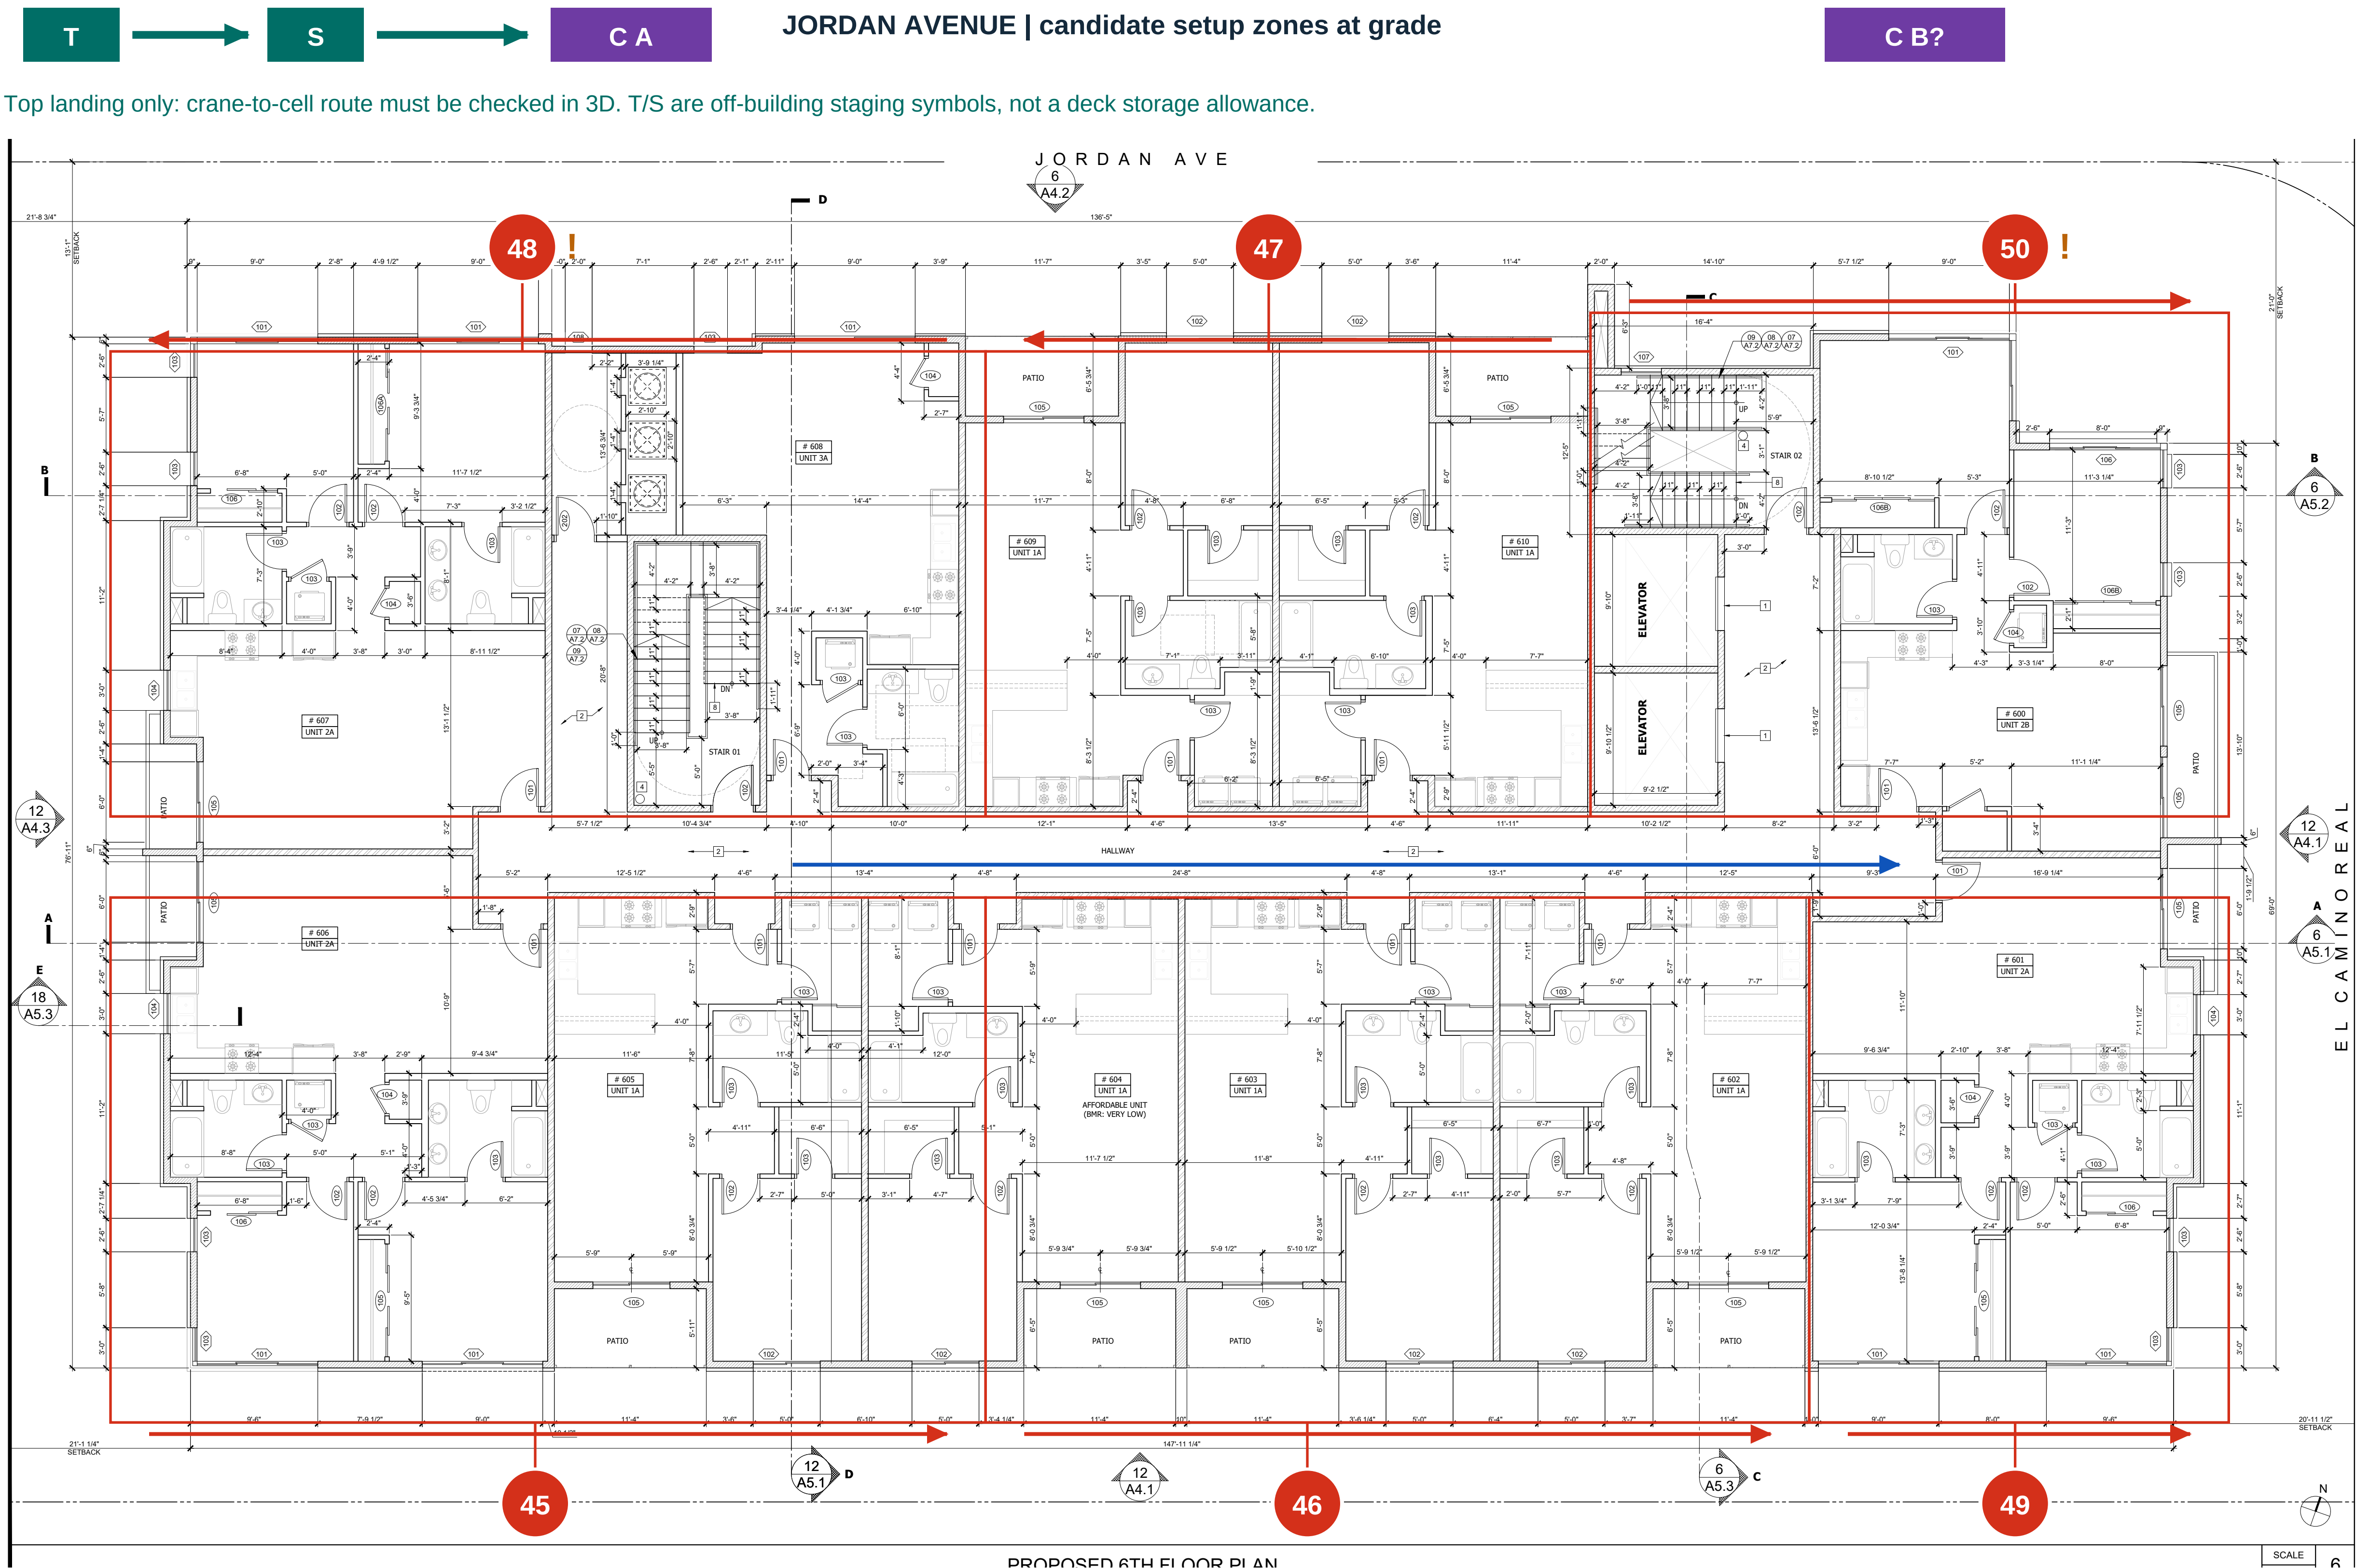

BLUE: preserve central corridor / stair routes for people and small items. Follow actual plan jogs. Group outlines are schematic; include all associated recesses and returns.




Transitions: far middle to near middle = change workforce; near rear to far front = new sector / R if needed. Short plan arrows show local progression, not load-flight paths.

- 45 Neighbor-side rear
Units 606-605 side. Start stable; protect rear route.
- 46 Neighbor-side middle
Units 604-602 side. Land all large far-side internals.
- 47 Jordan-side middle
Units 609-610 side. Close near side after far kit.
- 48 Jordan-side rear
Units 607-608 / stair 01. Complete rear sector; prepare R.
- 49 Neighbor-side frontage
Unit 601 frontage. Verify A coverage or move to B.
- 50 Jordan-side frontage / core
Unit 600 / stair 02 / elevators. Core interfaces first; last return closes.
- 51 Residual partitions / inventory
All lift-dependent items installed before overhead closure.
- 52 Joists / diaphragm / release
Complete each cell only after pre-deck check; approve next level.

CLOSURE: 48 rear-sector last return; 50 front-sector last return. Install cell internals first. Permanent door/stair routes stay usable.

HOLD: floor-specific steel/CFS support, bracing and crane coverage. If A covers all groups, omit R. If not, stabilize rear/middle cells, then relocate A to B for front groups.

Actual architectural plan A1.7, permit p23 | Rear/middle sector first, then El Camino frontage | Proposed groups; shop-panel mapping required

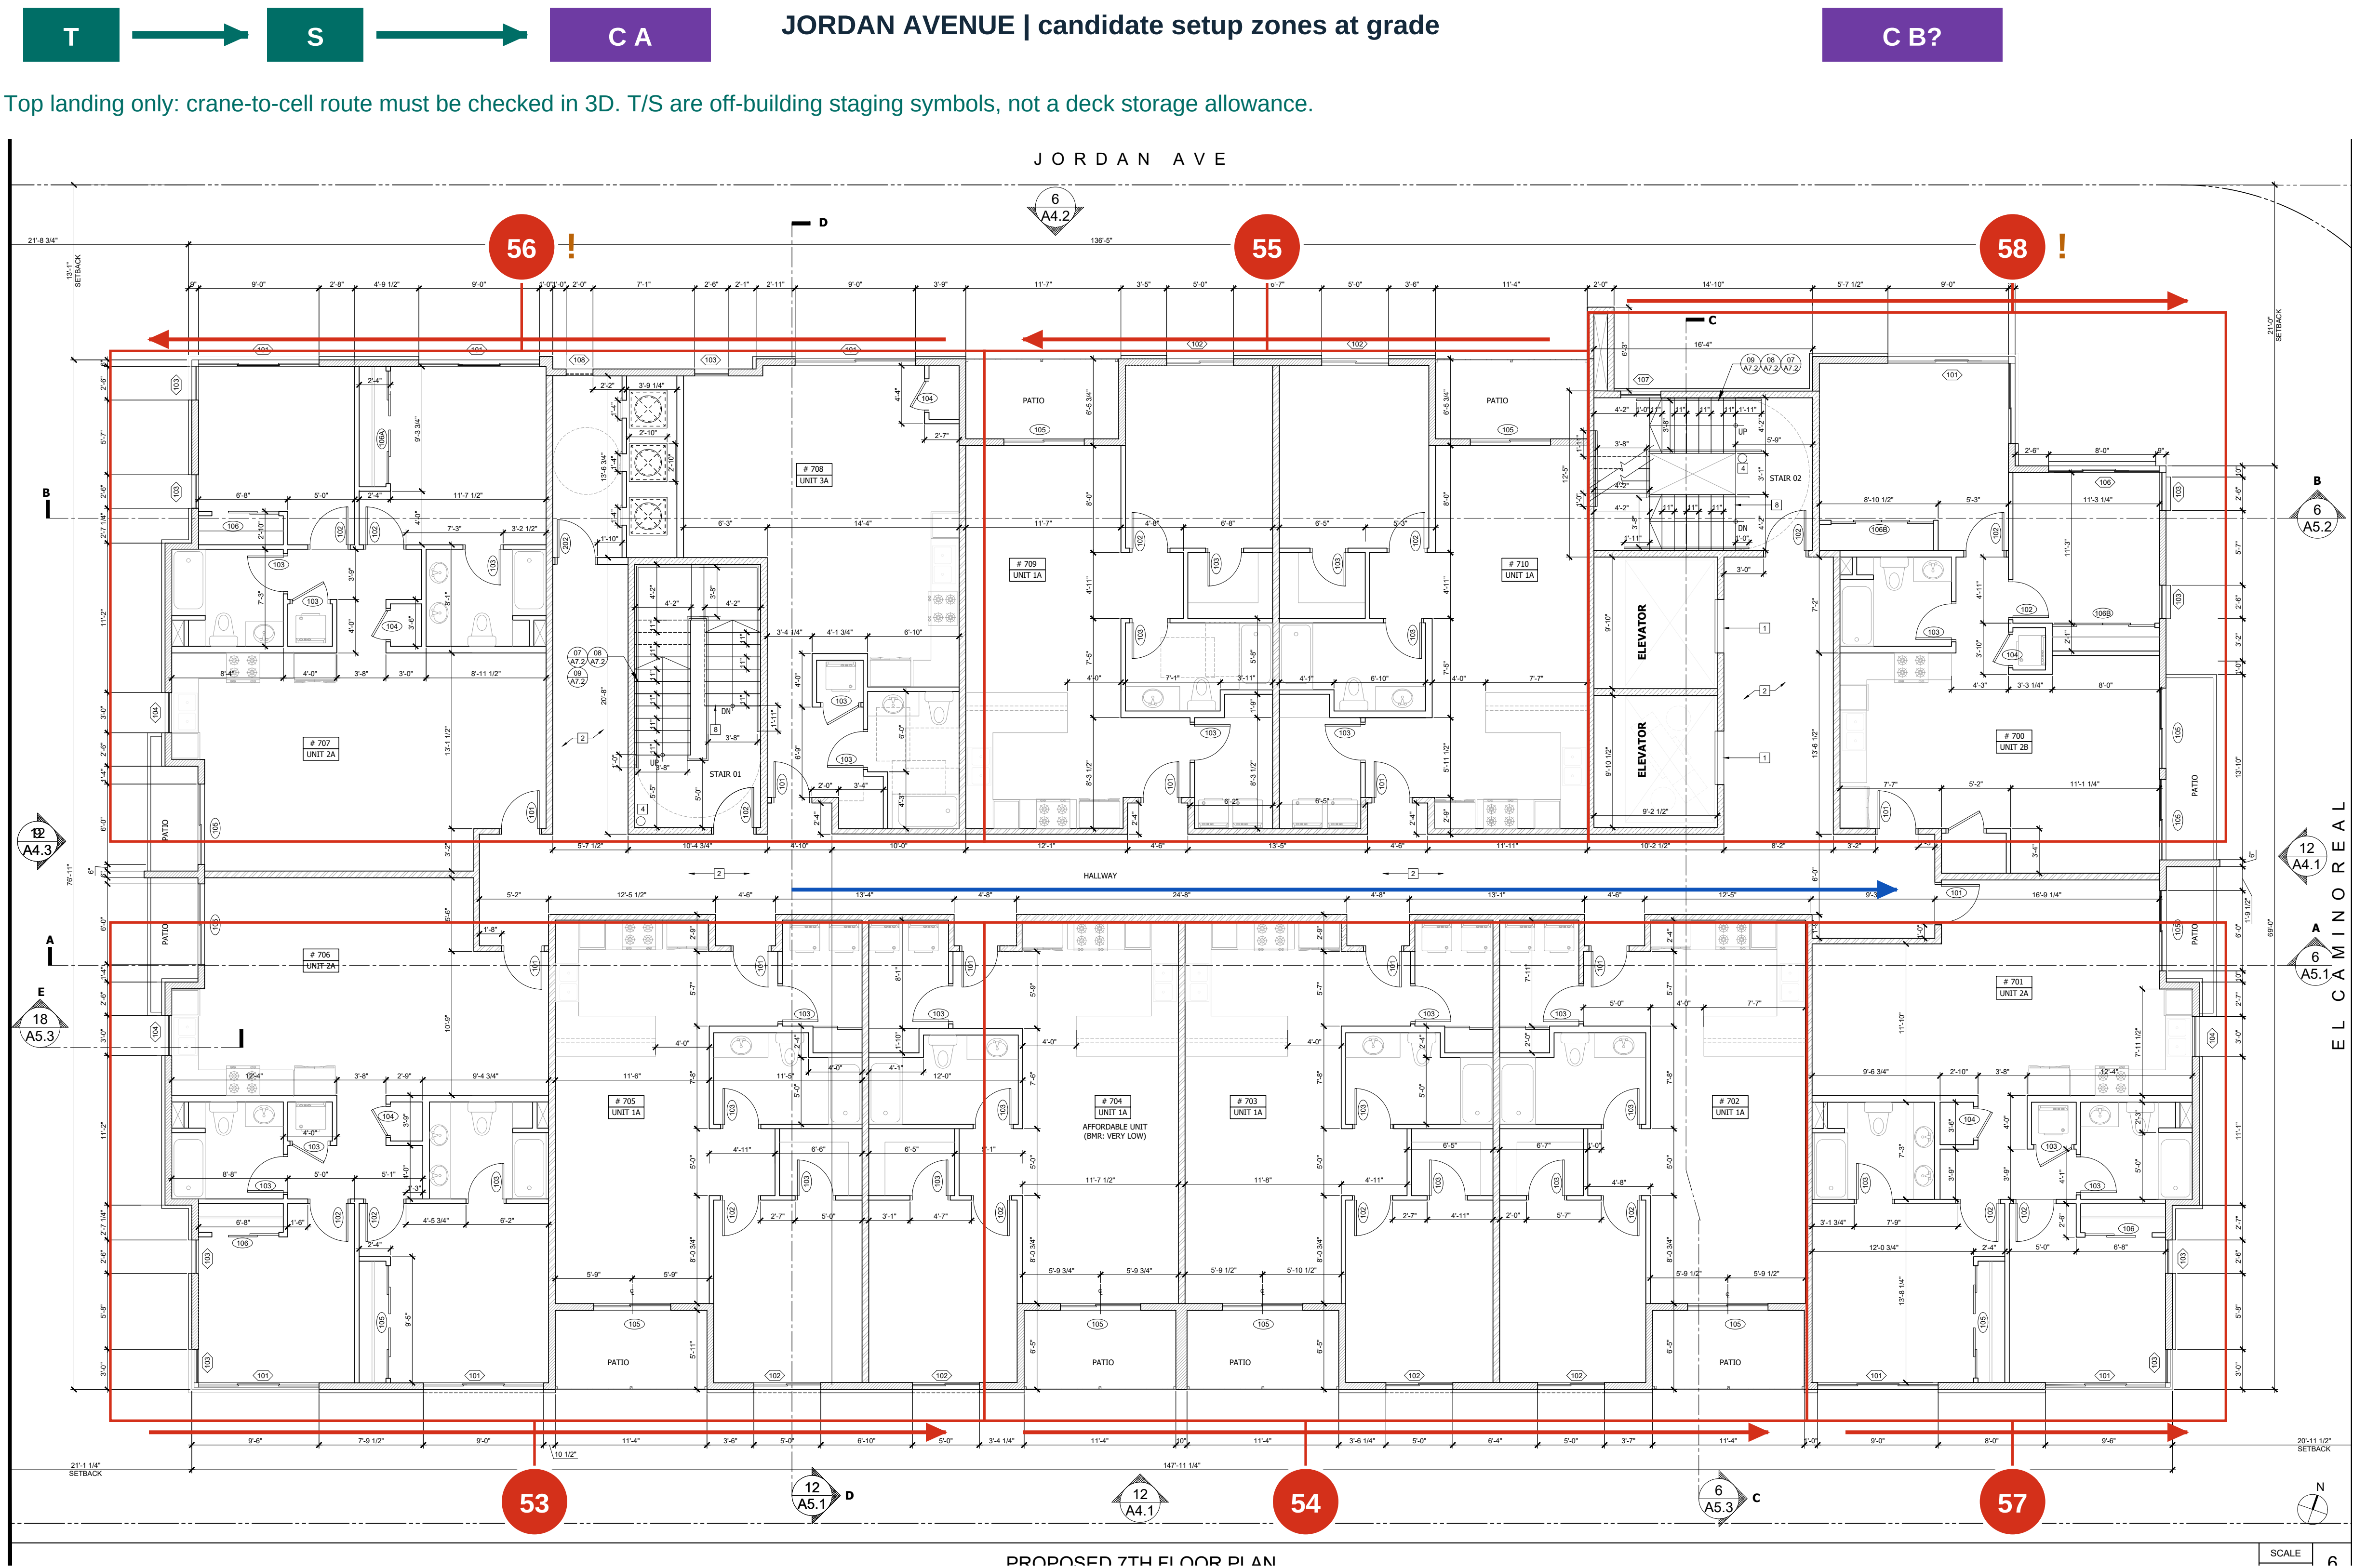

BLUE: preserve central corridor / stair routes for people and small items. Follow actual plan jogs. Group outlines are schematic; include all associated recesses and returns.




Transitions: far middle to near middle = change workforce; near rear to far front = new sector / R if needed. Short plan arrows show local progression, not load-flight paths.

- 53 Neighbor-side rear**
Units 706-705 side. Start stable; protect rear route.
- 54 Neighbor-side middle**
Units 704-702 side. Land all large far-side internals.
- 55 Jordan-side middle**
Units 709-710 side. Close near side after far kit.
- 56 Jordan-side rear**
Units 707-708 / stair 01. Complete rear sector; prepare R.
- 57 Neighbor-side frontage**
Unit 701 frontage. Verify A coverage or move to B.
- 58 Jordan-side frontage / core**
Unit 700 / stair 02 / elevators. Core interfaces first; last return closes.
- 59 Residual partitions / inventory**
All lift-dependent items installed before overhead closure.
- 60 Joists / diaphragm / release**
Complete each cell only after pre-deck check; approve next level.

CLOSURE: 56 rear-sector last return; 58 front-sector last return. Install cell internals first. Permanent door/stair routes stay usable.

HOLD: floor-specific steel/CFS support, bracing and crane coverage. If A covers all groups, omit R. If not, stabilize rear/middle cells, then relocate A to B for front groups.

Actual architectural plan A1.8, permit p24 | Rear/middle sector first, then El Camino frontage | Proposed groups; shop-panel mapping required

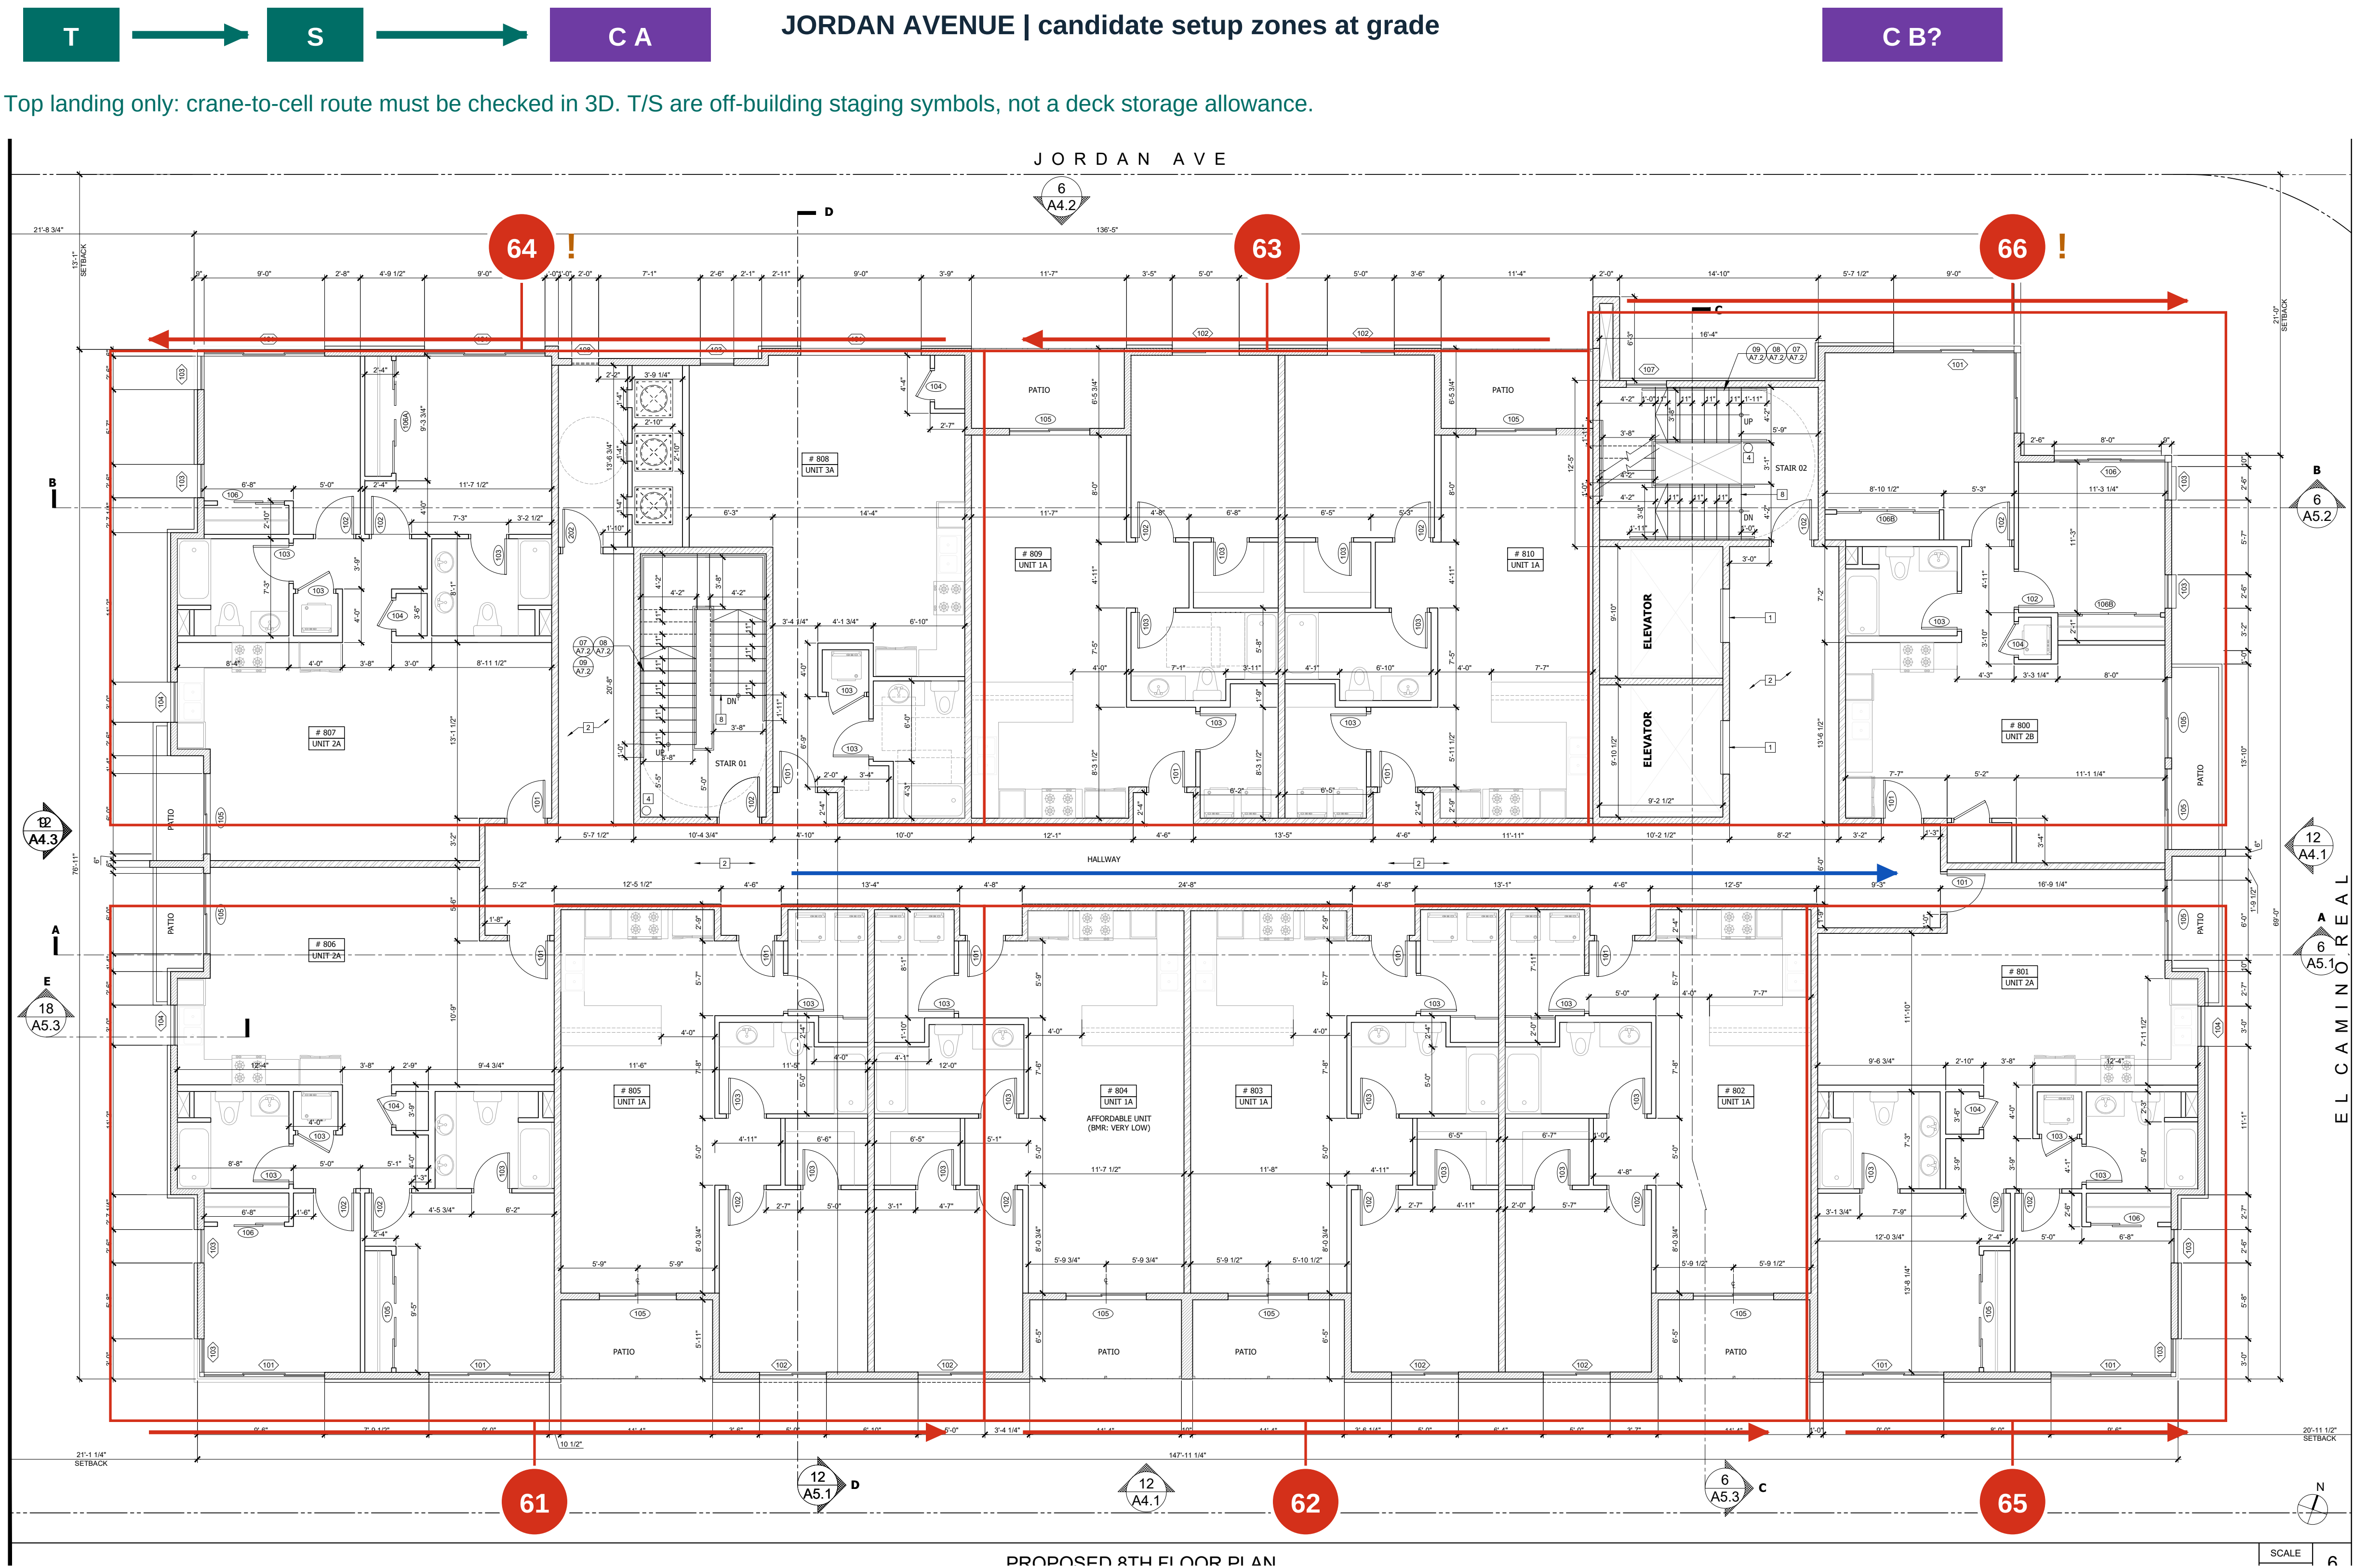


BLUE: preserve central corridor / stair routes for people and small items. Follow actual plan jogs. Group outlines are schematic; include all associated recesses and returns.



Transitions: far middle to near middle = change workforce; near rear to far front = new sector / R if needed. Short plan arrows show local progression, not load-flight paths.

Source A1.9 p25 + A1.10 p26 + A4.1 p33 + S1.9 p58 + M2.8 p128 | Roof framing and headhouse mapping require RFI-01

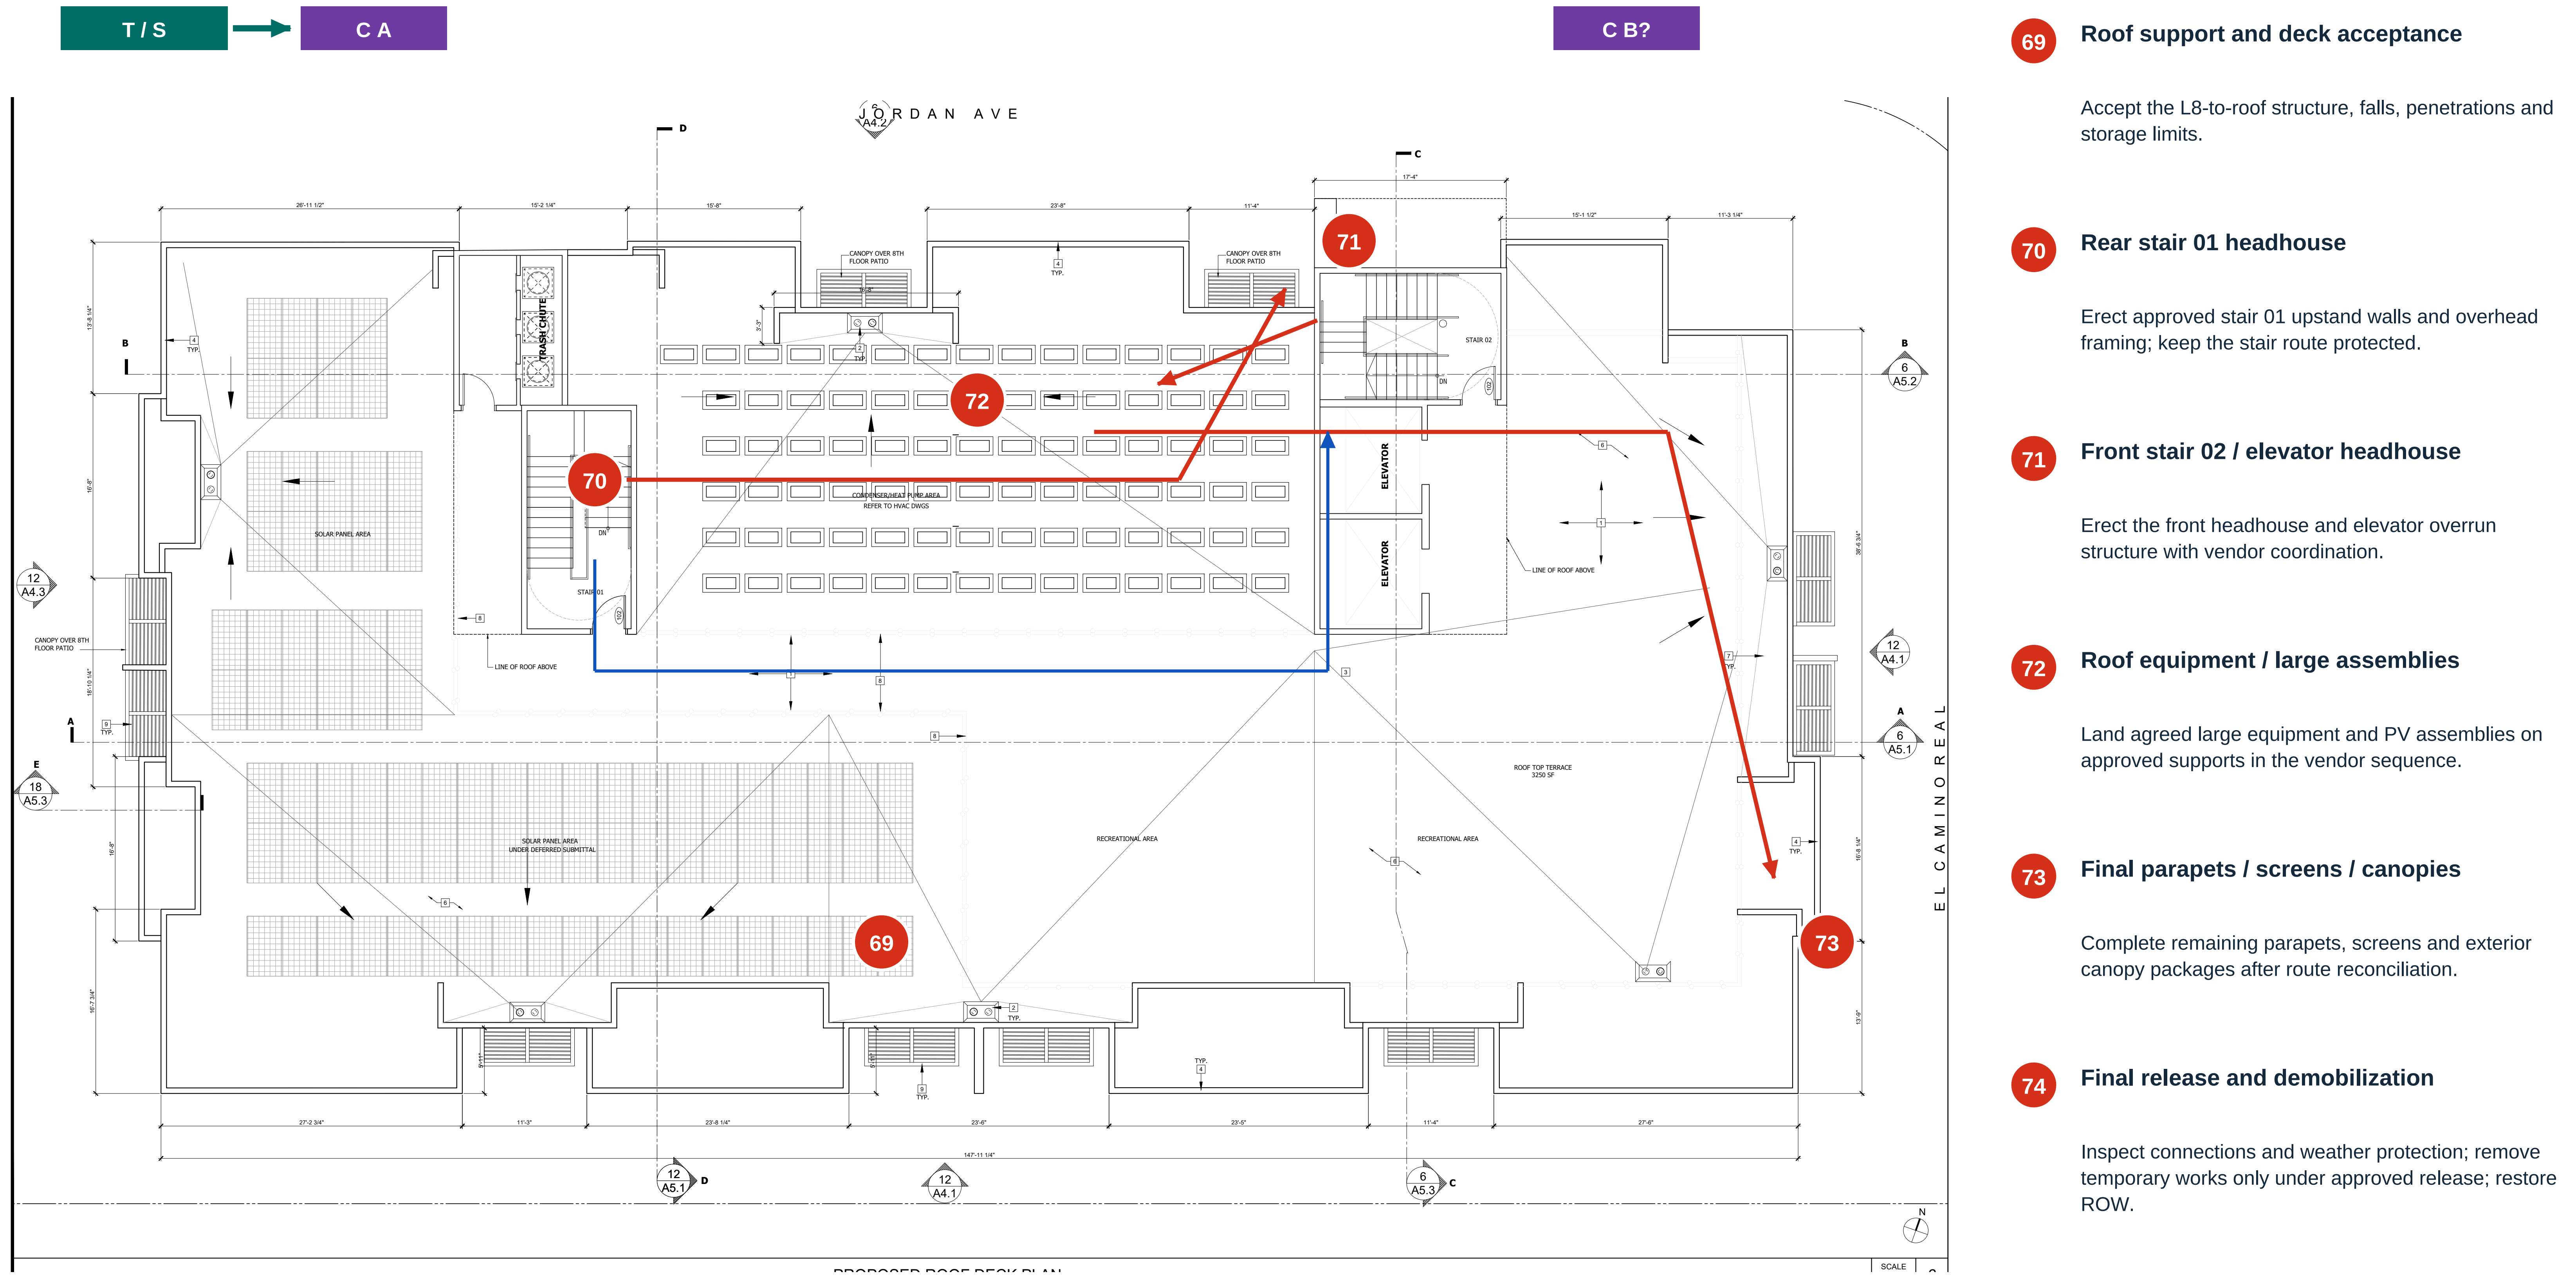



Keep a protected route between stair landings. Do not use the mechanical/PV layout as a temporary storage rating. Final screens and canopies must not trap equipment.



69 support > 70 rear headhouse > 71 front headhouse > 72 equipment > 73 final closures > 74 release / demobilize. ASSUMED stages.

Container logistics | Sequence kits before cube numbers

Approximately 40 ft container; user-specified maximum cube length 39'4" | ASSUMPTION - PACKING TO BE VERIFIED

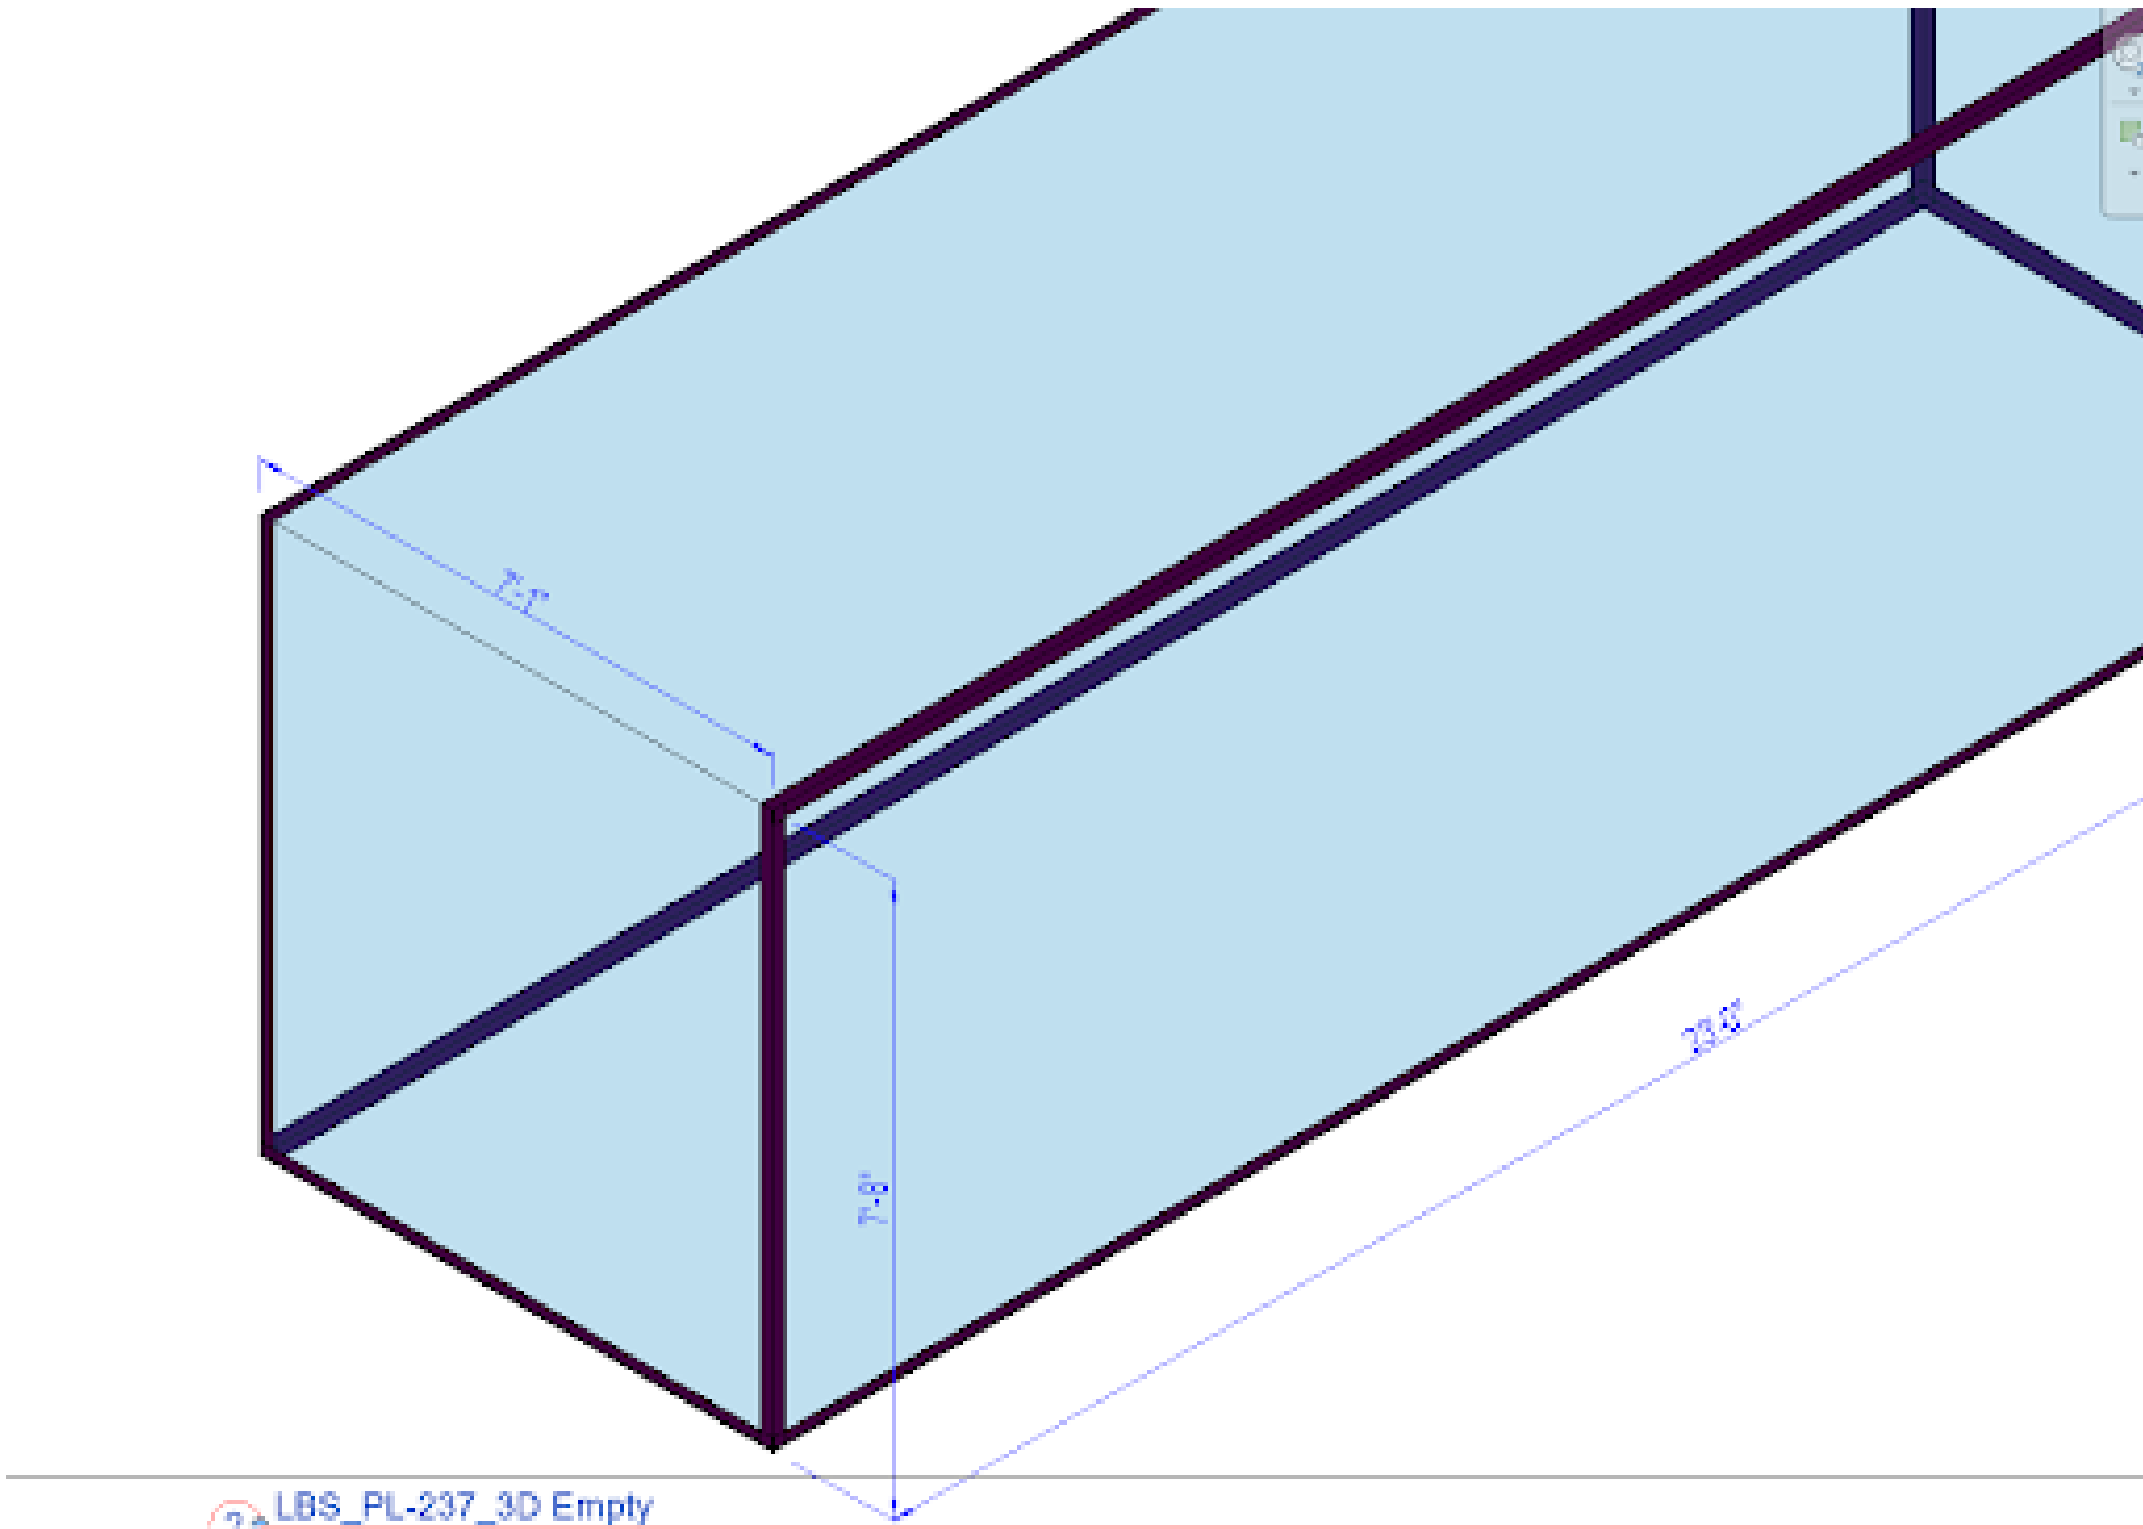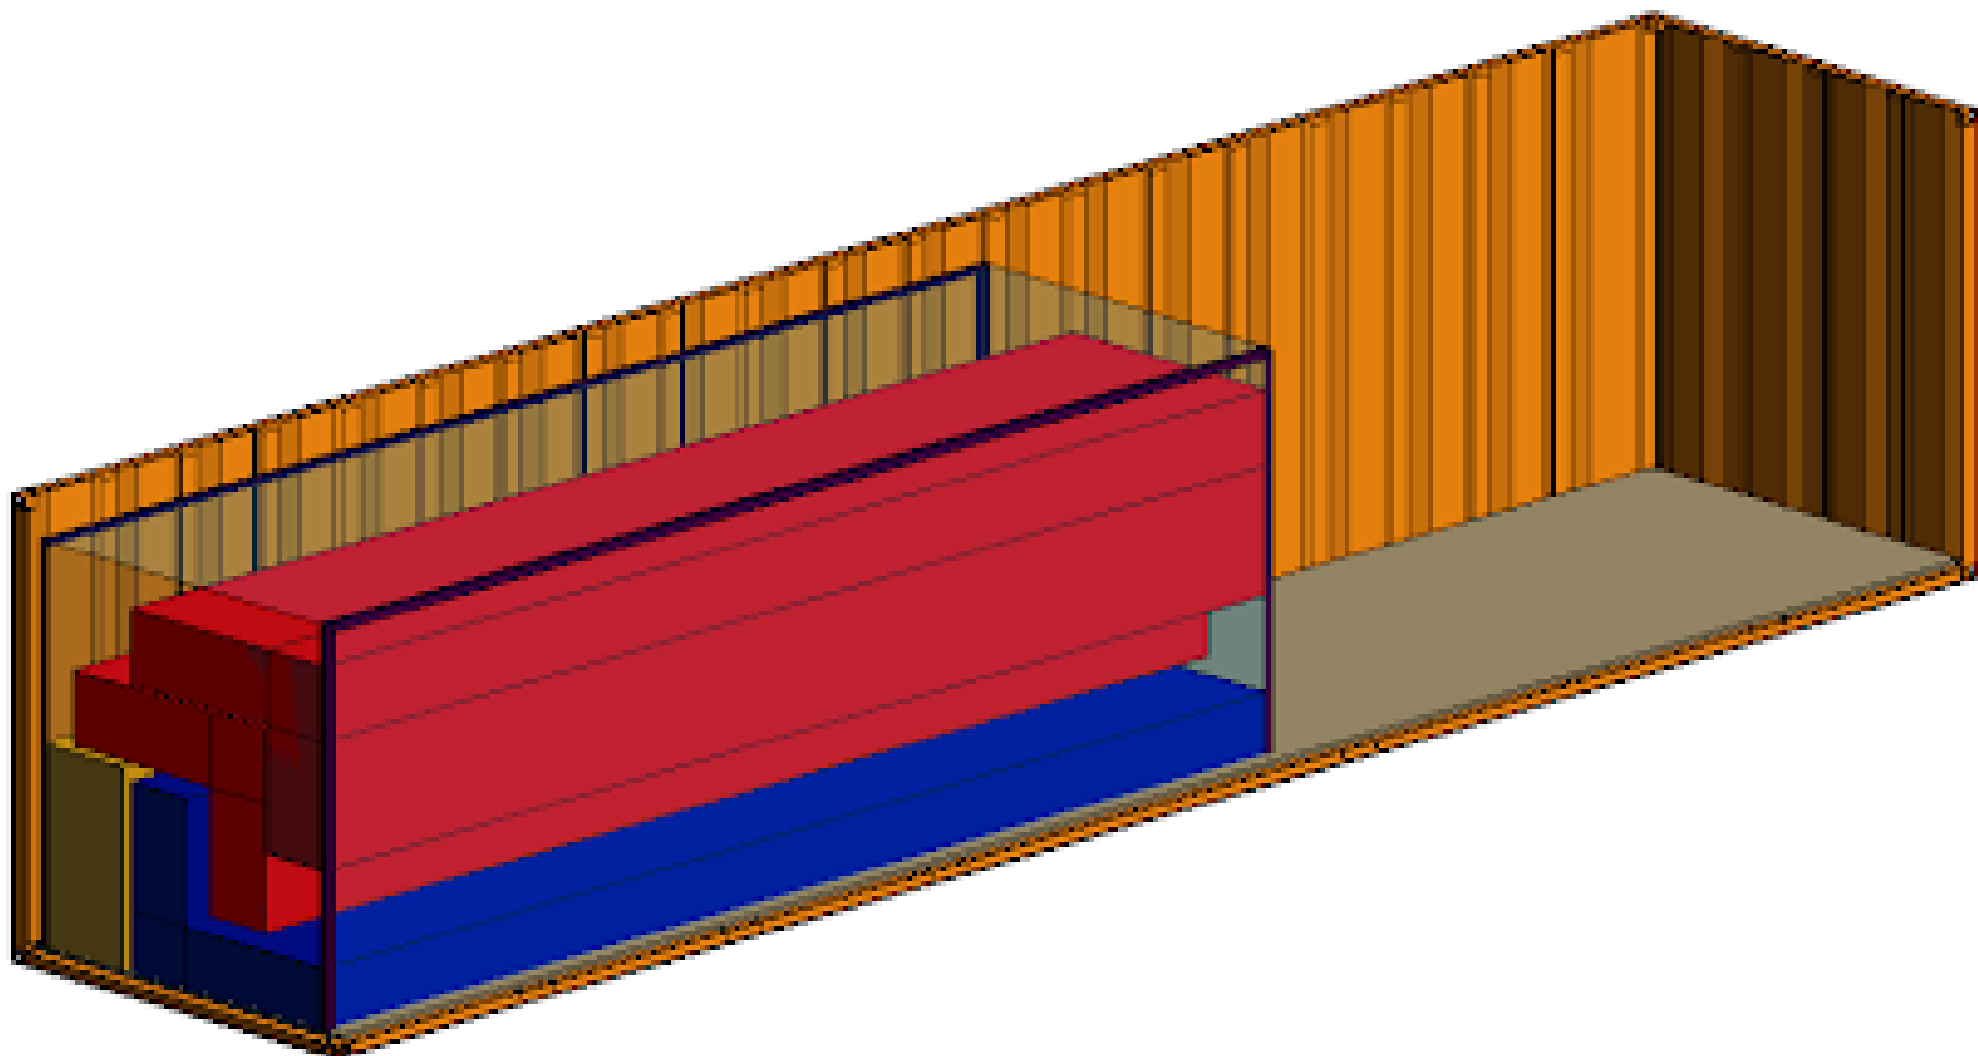

Supplied illustrations establish the intended container/cube concept only. They do not identify this building's packed panels, door clearance, cube weight, handling system or tie-down arrangement. Do not lift a complete cube as one load without a designed lifting method.



Planning kits, not invented cubes

Each level has G1-G6 cell kits, G7 residual partitions and G8 overhead framing. A kit may span several cubes; a cube may contain multiple kits only if extraction remains compatible with the sequence.

Extraction precedes erection

For an end-door container, verify the actual first-out item against the first-needed kit. Retain dunnage/restraints until the remaining pack is stable. Separate independent late closures if they would be buried behind earlier bundles.

39'4" is not a wall-panel length

The limit applies to the user's cube envelope. Check clear internal/door geometry, bracing and handling allowances. A 39'4" shear-wall label on a structural plan is not proof of one transportable panel.

Required manifest: cube ID > extraction position > floor/step > shop panel IDs > gross dimensions and weight > center of gravity/pick points > restraint release order > delivery orientation > receiving cell > special handling.

No container count, panel count, packed cube dimensions beyond the supplied length limit, lift weight, or assumed bulk deck-storage allowance is assigned. Field staging must fit alongside crane/traffic controls or move off-site.

Constructability replay | What changes after each group

Conditional qualitative replay of the proposed groups | Not a crane simulation, panel collision model or temporary-stability calculation

State reached	New obstruction / condition	What the next step must prove
01-04 complete	Excavation, structural supports, parking voids, access and equipment interfaces now govern the work surface.	Verify first cell support, anchors, crane envelope and vendor routes before lifting.
Each floor G1	Rear far-side corner/returns now obstruct low-level rear transfer.	G2 arrives from above into the middle receiving cell; do not route it through the completed rear cell.
Each floor G2	Far rear/middle walls and transverse pieces stand.	All large middle-cell internals are in before G3 closes the near side; check hook and rigging withdrawal.
Each floor G3	Middle near-side wall group has reduced lateral maneuvering room.	G4 is independently top-delivered to the rear near cell; inspect connecting faces before the last return.
Each floor G4 / R	Rear/middle work has reached a stable stop; B may be needed for frontage.	Secure all installed work; remove suspended loads, release travel route and re-establish B setup. Front cell remains open.
Each floor G5	Far-front group now obstructs access from the neighbor edge.	G6 receives from the street side/top. Install large shaft, stair and front-cell pieces before closing its near return.
Each floor G6 / G7	Final crane-delivered wall return and residual partitions are complete.	Full kit reconciliation and connection inspection. A missing trapped piece stops the pre-deck release.
Each floor G8	Joists/diaphragm close overhead receiving space in the accepted cell.	No later large piece may depend on that route. Next level begins only after structural capacity and stability release.
69-74 roof	Head-houses, equipment and final screens progressively remove roof maneuvering space.	Complete large deliveries before permanent screen closure; engineer releases temporary support removal and demobilization.

Reorder applied: the plan does not close the entire perimeter first and then attempt to feed large interior panels through finished openings. Interior large pieces are included in their cell before closure. Remaining geometric, lifting and stability checks are HOLD items, not claimed passes.

FIELD VERIFY includes engineer/vendor verification and document reconciliation, not only a site measurement

RFI-01	L8 / roof structural mapping EOR + architect	Provide the governing L8 framing and roof/headhouse support plans. S1.2-S1.8 name floors 1-7; S1.9 is named roof. Do not interpolate a structural story.
RFI-02	Floor and lateral system EOR	Reconcile S0.1 composite deck/concrete and moment-frame narrative with Megaboard, CFS bearing/shear walls and details on S1.x / S3.x. Issue the construction-stage stability sequence.
RFI-03	Shop-panel and closure map Livio + erector + EOR	Provide panel tags, joints, weights, pick points, loadbearing/shear status, connection access and approved local closure returns. Map every panel exactly once to a step.
RFI-04	Crane A/B and ground support Crane planner + geotech + shoring EOR	Prove actual gross lift loads, chart capacity at all radii/heights, boom/rigging clearance, reactions, mats, utilities and excavation surcharge. Verify B or demonstrate full A coverage.
RFI-05	Trees and site constraints Surveyor + arborist + GC	Reconcile aerial #5/#6 with civil #5/#6 and landscape #4/#6; set approved TPZs and canopy clearances. Do not size protection from the illustration circles.
RFI-06	Truck / ROW / public routes GC + traffic planner + authorities	Obtain working-zone permissions and approved traffic/pedestrian arrangements. Prove truck turning, queuing, offload fit and crane mobilization. Preserve easement and neighbor access.
RFI-07	Parking, elevators and services Vendors + MEP + GC	Resolve automated parking count/layout revisions, delivery openings and route timing; elevator overrun and stair numbering conflicts; transformer and joint-trench work.
RFI-08	Packing / roof / weather Livio + vendors + crane planner	Release extraction manifest, cube dimensions/weights and supports; roof equipment lift data; panel wind/handling limits; stop/recovery procedure. Do not assign numerical limits from this concept.

CONFIRMED drawing evidence

Reference: one annotated Cupertino sheet. Target: 215-page permit compilation. Reviewed relevant architectural plans, elevations and sections; structural plans/connection details; civil access/utilities; landscape trees; shoring and parking/elevator interfaces. MEP/energy material was indexed and consulted selectively, not subjected to a full discipline design review.

Source precedence

Use permit dimensions and released coordinated drawings. Imagery supports adjacency and access awareness only. Rev B adds an independent Esri World Imagery cross-check (EC-03A) retrieved 29 SEP 2026; its capture date is not verified, so the supplied annotated aerial (EC-01) remains the closer-in-time site reference. Direct Google Earth access is unavailable to automation.

Key project sources

T1.1 p2: project scope. A1.0 p15: site. A1.1 p16: ground floor. A1.1A p17: basement. A1.2-A1.8 pp18-24: upper floors.

A1.9-A1.10 pp25-26: roof. A4.1-A4.4 pp33-36: elevations. A5.1-A5.4 pp38-41: sections. A7.1-A7.3 pp42-44: assemblies/offsite system.

S0.1-S0.2 pp47-48: structural notes. S1.0-S1.9 pp49-58: support and framing plans. S3.0-S6.1 pp61-71: framing and connection details.

C2.0 p75: demolition/retained trees/utilities/easement. ER-1 p90: construction entrance. L1.01 p98 and L3.01 p110: site and trees.

QA sheets pp177-181: parking interfaces. S1 p182: shoring concept. Elevator sheets pp183-214 marked preliminary. Joint trench p215.

External practice references (not a project lift approval)

California DIR - load ratings / load handling | <https://www.dir.ca.gov/title8/4923.html>

California DIR - handling loads | <https://www.dir.ca.gov/title8/4999.html>

California DIR - power-line assessment | https://www.dir.ca.gov/title8/5003_1.html

Caltrans - encroachment permit manual | <https://dot.ca.gov/programs/traffic-operations/ep/ep-manual>

Confidence rules

CONFIRMED = directly visible in a supplied project document. PROBABLE = inference from the reference or converging evidence. ASSUMED = proposed sequencing, zoning or logistics. FIELD VERIFY = unresolved information requiring an accountable field, design or vendor decision. All 74 proposed steps are ASSUMED; holds remain open.

Other discrepancies affecting coordination

A1.0 stair numbering is reversed relative to A1.1/upper floor plans; use the floor-plan positions until reconciled. T1.1 parking summary differs from later vendor schedules. A4.1 overall height and elevator-top level are different labels/datums; verify actual lifting elevation. These items are not silently corrected in the source.

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
01	Site controls	Survey boundaries, utilities and retained trees; install approved protection and access controls.	None	None	Prevent setup on an unverified support area or protected feature. AFTER: Protected limits and access are established.	HOLD: tree identity, ROW rights, buried/overhead services and exclusion limits. NEXT: Prove excavation and delivery access do not conflict.
02	Substructure	Complete engineered shoring, excavation, mat, basement walls and support system.	Separate plan	Separate schedule	Provide the designed support before superstructure erection. AFTER: Basement and mat exist; car-lift voids remain controlled openings.	HOLD: excavation surcharge; shoring design and staged removal. NEXT: Confirm embeds and support elevations against released drawings.
03	Equipment interfaces	Resolve automated-parking and electrical equipment installation routes before restricting openings.	Separate plan	Vendor packages	Large equipment cannot be assumed to pass through finished personnel openings. AFTER: Reserved vendor routes are documented and protected.	HOLD: deferred parking equipment; delivery dimensions; transformer access. NEXT: Confirm first-floor work will not trap equipment or close required access.
04	First-floor release	Accept supporting slab/frame, anchors, protected access and approved erection stability plan.	A candidate	First floor kits	Release only a checked working surface and a defined temporary load path. AFTER: First-floor survey and staged support prerequisites are accepted.	HOLD: slab strength, storage loading, crane reactions and full lift envelope. NEXT: Confirm first wall group can be landed, connected and braced.
05	L1 - Neighbor-side rear: Bike room / unit 105 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L1-G1 kit; cube TBD	Start at the far rear with an approved stable corner and returns; no later low-level transfer behind it. AFTER: Far rear group is stabilized; middle/front and overhead receiving areas remain open.	High: far reach, adjacent property, initial stability and edge protection. NEXT: Check next group landing and rigging rotation clear of the new rear returns.
06	L1 - Neighbor-side middle: Units 104-102 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L1-G2 kit; cube TBD	Continue the far side while the overhead delivery route and central corridor are open. AFTER: Far middle group is stabilized; near middle receiving slot remains open.	High: large internal pieces can be trapped by top framing or completed near walls. NEXT: Check all large middle-cell internals are installed before its near-side closure.
07	L1 - Jordan-side middle: Units 107-108 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L1-G3 kit; cube TBD	Complete the middle near side only after its far-side kit and internal large pieces are in place. AFTER: Middle cell is bounded; rear near-side receiving slot remains open.	High: connecting faces and long-panel rotation require a verified envelope. NEXT: Check the rear group arrives from above without passing through the completed middle cell.
08	L1 - Jordan-side rear: Electrical / trash / 106 / stair 01	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L1-G4 kit; cube TBD	Finish the rear sector before relocation; protect rear equipment routes and stair access. AFTER: Rear/middle sector is complete and stable for the planned crane move.	High: stair/equipment routes; local rear closure only after kit reconciliation. NEXT: Verify B setup or A full coverage, public controls and forward cell stability before front lifts.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
09	L1 - Neighbor-side frontage: Unit 101 frontage	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L1-G5 kit; cube TBD	From the verified front setup, land the remaining far-side frontage group before the near front closes. AFTER: Far front is complete; near front and core receiving space remain open.	High: front reach, neighboring edge and public El Camino frontage. NEXT: Check shaft pieces, stair members and front internals fit before closing the near-front return.
10	L1 - Jordan-side frontage / core: Lobby / public rooms / stair 02 / elevators	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L1-G6 kit; cube TBD	Complete the front core interfaces and near-side returns last; lower trapped pieces before final closure. AFTER: Crane-delivered wall groups are complete; no remaining large pieces may depend on closed side access.	High: shaft/stair interfaces and final crane-delivered wall closure. NEXT: Reconcile every kit; any missing trapped item requires reordering before closure, not improvisation.
11	L1 - Residual partitions / closure check	Complete remaining non-loadbearing partitions and connections; verify all lift-dependent components and access closures.	A or B as released	L1-G7 kit; cube TBD	Clear all items that would become trapped under the next deck. AFTER: All wall groups and pre-deck large internals are reconciled.	High: shop-panel inventory, connection access and maintained egress. NEXT: Verify no missing panel or connection face will be covered by joists/deck.
12	L1 - Overhead framing / floor release	Complete required joists, blocking, diaphragms and inspections in approved cells; authorize the next working level.	A or B as released	L1-G8 framing kit; cube TBD	Close overhead receiving space only after that cell passes its pre-deck check. AFTER: The receiving route from above is closed in released cells; next deck is an accepted work surface.	HOLD: diaphragm/temporary bracing, support reactions, load capacity and deck-system RFI-02. NEXT: Reset crane coverage for the next level; do not advance an unreleased upper story.
13	L2 - Neighbor-side rear: Units 206-205 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L2-G1 kit; cube TBD	Start at the far rear with an approved stable corner and returns; no later low-level transfer behind it. AFTER: Far rear group is stabilized; middle/front and overhead receiving areas remain open.	High: far reach, adjacent property, initial stability and edge protection. NEXT: Check next group landing and rigging rotation clear of the new rear returns.
14	L2 - Neighbor-side middle: Units 204-202 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L2-G2 kit; cube TBD	Continue the far side while the overhead delivery route and central corridor are open. AFTER: Far middle group is stabilized; near middle receiving slot remains open.	High: large internal pieces can be trapped by top framing or completed near walls. NEXT: Check all large middle-cell internals are installed before its near-side closure.
15	L2 - Jordan-side middle: Units 209-210 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L2-G3 kit; cube TBD	Complete the middle near side only after its far-side kit and internal large pieces are in place. AFTER: Middle cell is bounded; rear near-side receiving slot remains open.	High: connecting faces and long-panel rotation require a verified envelope. NEXT: Check the rear group arrives from above without passing through the completed middle cell.
16	L2 - Jordan-side rear: Units 207-208 / stair 01	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L2-G4 kit; cube TBD	Finish the rear sector before relocation; protect rear equipment routes and stair access. AFTER: Rear/middle sector is complete and stable for the planned crane move.	High: stair/equipment routes; local rear closure only after kit reconciliation. NEXT: Verify B setup or A full coverage, public controls and forward cell stability before front lifts.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

Sequence register | 17-24

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
17	L2 - Neighbor-side frontage: Unit 201 frontage	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L2-G5 kit; cube TBD	From the verified front setup, land the remaining far-side frontage group before the near front closes. AFTER: Far front is complete; near front and core receiving space remain open.	High: front reach, neighboring edge and public El Camino frontage. NEXT: Check shaft pieces, stair members and front internals fit before closing the near-front return.
18	L2 - Jordan-side frontage / core: Unit 200 / stair 02 / elevators	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L2-G6 kit; cube TBD	Complete the front core interfaces and near-side returns last; lower trapped pieces before final closure. AFTER: Crane-delivered wall groups are complete; no remaining large pieces may depend on closed side access.	High: shaft/stair interfaces and final crane-delivered wall closure. NEXT: Reconcile every kit; any missing trapped item requires reordering before closure, not improvisation.
19	L2 - Residual partitions / closure check	Complete remaining non-loadbearing partitions and connections; verify all lift-dependent components and access closures.	A or B as released	L2-G7 kit; cube TBD	Clear all items that would become trapped under the next deck. AFTER: All wall groups and pre-deck large internals are reconciled.	High: shop-panel inventory, connection access and maintained egress. NEXT: Verify no missing panel or connection face will be covered by joists/deck.
20	L2 - Overhead framing / floor release	Complete required joists, blocking, diaphragms and inspections in approved cells; authorize the next working level.	A or B as released	L2-G8 framing kit; cube TBD	Close overhead receiving space only after that cell passes its pre-deck check. AFTER: The receiving route from above is closed in released cells; next deck is an accepted work surface.	HOLD: diaphragm/temporary bracing, support reactions, load capacity and deck-system RFI-02. NEXT: Reset crane coverage for the next level; do not advance an unreleased upper story.
21	L3 - Neighbor-side rear: Units 306-305 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L3-G1 kit; cube TBD	Start at the far rear with an approved stable corner and returns; no later low-level transfer behind it. AFTER: Far rear group is stabilized; middle/front and overhead receiving areas remain open.	High: far reach, adjacent property, initial stability and edge protection. NEXT: Check next group landing and rigging rotation clear of the new rear returns.
22	L3 - Neighbor-side middle: Units 304-302 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L3-G2 kit; cube TBD	Continue the far side while the overhead delivery route and central corridor are open. AFTER: Far middle group is stabilized; near middle receiving slot remains open.	High: large internal pieces can be trapped by top framing or completed near walls. NEXT: Check all large middle-cell internals are installed before its near-side closure.
23	L3 - Jordan-side middle: Units 309-310 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L3-G3 kit; cube TBD	Complete the middle near side only after its far-side kit and internal large pieces are in place. AFTER: Middle cell is bounded; rear near-side receiving slot remains open.	High: connecting faces and long-panel rotation require a verified envelope. NEXT: Check the rear group arrives from above without passing through the completed middle cell.
24	L3 - Jordan-side rear: Units 307-308 / stair 01	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L3-G4 kit; cube TBD	Finish the rear sector before relocation; protect rear equipment routes and stair access. AFTER: Rear/middle sector is complete and stable for the planned crane move.	High: stair/equipment routes; local rear closure only after kit reconciliation. NEXT: Verify B setup or A full coverage, public controls and forward cell stability before front lifts.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
25	L3 - Neighbor-side frontage: Unit 301 frontage	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L3-G5 kit; cube TBD	From the verified front setup, land the remaining far-side frontage group before the near front closes. AFTER: Far front is complete; near front and core receiving space remain open.	High: front reach, neighboring edge and public El Camino frontage. NEXT: Check shaft pieces, stair members and front internals fit before closing the near-front return.
26	L3 - Jordan-side frontage / core: Unit 300 / stair 02 / elevators	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L3-G6 kit; cube TBD	Complete the front core interfaces and near-side returns last; lower trapped pieces before final closure. AFTER: Crane-delivered wall groups are complete; no remaining large pieces may depend on closed side access.	High: shaft/stair interfaces and final crane-delivered wall closure. NEXT: Reconcile every kit; any missing trapped item requires reordering before closure, not improvisation.
27	L3 - Residual partitions / closure check	Complete remaining non-loadbearing partitions and connections; verify all lift-dependent components and access closures.	A or B as released	L3-G7 kit; cube TBD	Clear all items that would become trapped under the next deck. AFTER: All wall groups and pre-deck large internals are reconciled.	High: shop-panel inventory, connection access and maintained egress. NEXT: Verify no missing panel or connection face will be covered by joists/deck.
28	L3 - Overhead framing / floor release	Complete required joists, blocking, diaphragms and inspections in approved cells; authorize the next working level.	A or B as released	L3-G8 framing kit; cube TBD	Close overhead receiving space only after that cell passes its pre-deck check. AFTER: The receiving route from above is closed in released cells; next deck is an accepted work surface.	HOLD: diaphragm/temporary bracing, support reactions, load capacity and deck-system RFI-02. NEXT: Reset crane coverage for the next level; do not advance an unreleased upper story.
29	L4 - Neighbor-side rear: Units 406-405 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L4-G1 kit; cube TBD	Start at the far rear with an approved stable corner and returns; no later low-level transfer behind it. AFTER: Far rear group is stabilized; middle/front and overhead receiving areas remain open.	High: far reach, adjacent property, initial stability and edge protection. NEXT: Check next group landing and rigging rotation clear of the new rear returns.
30	L4 - Neighbor-side middle: Units 404-402 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L4-G2 kit; cube TBD	Continue the far side while the overhead delivery route and central corridor are open. AFTER: Far middle group is stabilized; near middle receiving slot remains open.	High: large internal pieces can be trapped by top framing or completed near walls. NEXT: Check all large middle-cell internals are installed before its near-side closure.
31	L4 - Jordan-side middle: Units 409-410 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L4-G3 kit; cube TBD	Complete the middle near side only after its far-side kit and internal large pieces are in place. AFTER: Middle cell is bounded; rear near-side receiving slot remains open.	High: connecting faces and long-panel rotation require a verified envelope. NEXT: Check the rear group arrives from above without passing through the completed middle cell.
32	L4 - Jordan-side rear: Units 407-408 / stair 01	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L4-G4 kit; cube TBD	Finish the rear sector before relocation; protect rear equipment routes and stair access. AFTER: Rear/middle sector is complete and stable for the planned crane move.	High: stair/equipment routes; local rear closure only after kit reconciliation. NEXT: Verify B setup or A full coverage, public controls and forward cell stability before front lifts.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
33	L4 - Neighbor-side frontage: Unit 401 frontage	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L4-G5 kit; cube TBD	From the verified front setup, land the remaining far-side frontage group before the near front closes. AFTER: Far front is complete; near front and core receiving space remain open.	High: front reach, neighboring edge and public El Camino frontage. NEXT: Check shaft pieces, stair members and front internals fit before closing the near-front return.
34	L4 - Jordan-side frontage / core: Unit 400 / stair 02 / elevators	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L4-G6 kit; cube TBD	Complete the front core interfaces and near-side returns last; lower trapped pieces before final closure. AFTER: Crane-delivered wall groups are complete; no remaining large pieces may depend on closed side access.	High: shaft/stair interfaces and final crane-delivered wall closure. NEXT: Reconcile every kit; any missing trapped item requires reordering before closure, not improvisation.
35	L4 - Residual partitions / closure check	Complete remaining non-loadbearing partitions and connections; verify all lift-dependent components and access closures.	A or B as released	L4-G7 kit; cube TBD	Clear all items that would become trapped under the next deck. AFTER: All wall groups and pre-deck large internals are reconciled.	High: shop-panel inventory, connection access and maintained egress. NEXT: Verify no missing panel or connection face will be covered by joists/deck.
36	L4 - Overhead framing / floor release	Complete required joists, blocking, diaphragms and inspections in approved cells; authorize the next working level.	A or B as released	L4-G8 framing kit; cube TBD	Close overhead receiving space only after that cell passes its pre-deck check. AFTER: The receiving route from above is closed in released cells; next deck is an accepted work surface.	HOLD: diaphragm/temporary bracing, support reactions, load capacity and deck-system RFI-02. NEXT: Reset crane coverage for the next level; do not advance an unreleased upper story.
37	L5 - Neighbor-side rear: Units 506-505 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L5-G1 kit; cube TBD	Start at the far rear with an approved stable corner and returns; no later low-level transfer behind it. AFTER: Far rear group is stabilized; middle/front and overhead receiving areas remain open.	High: far reach, adjacent property, initial stability and edge protection. NEXT: Check next group landing and rigging rotation clear of the new rear returns.
38	L5 - Neighbor-side middle: Units 504-502 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L5-G2 kit; cube TBD	Continue the far side while the overhead delivery route and central corridor are open. AFTER: Far middle group is stabilized; near middle receiving slot remains open.	High: large internal pieces can be trapped by top framing or completed near walls. NEXT: Check all large middle-cell internals are installed before its near-side closure.
39	L5 - Jordan-side middle: Units 509-510 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L5-G3 kit; cube TBD	Complete the middle near side only after its far-side kit and internal large pieces are in place. AFTER: Middle cell is bounded; rear near-side receiving slot remains open.	High: connecting faces and long-panel rotation require a verified envelope. NEXT: Check the rear group arrives from above without passing through the completed middle cell.
40	L5 - Jordan-side rear: Units 507-508 / stair 01	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L5-G4 kit; cube TBD	Finish the rear sector before relocation; protect rear equipment routes and stair access. AFTER: Rear/middle sector is complete and stable for the planned crane move.	High: stair/equipment routes; local rear closure only after kit reconciliation. NEXT: Verify B setup or A full coverage, public controls and forward cell stability before front lifts.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

Sequence register | 41-48

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
41	L5 - Neighbor-side frontage: Unit 501 frontage	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L5-G5 kit; cube TBD	From the verified front setup, land the remaining far-side frontage group before the near front closes. AFTER: Far front is complete; near front and core receiving space remain open.	High: front reach, neighboring edge and public El Camino frontage. NEXT: Check shaft pieces, stair members and front internals fit before closing the near-front return.
42	L5 - Jordan-side frontage / core: Unit 500 / stair 02 / elevators	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L5-G6 kit; cube TBD	Complete the front core interfaces and near-side returns last; lower trapped pieces before final closure. AFTER: Crane-delivered wall groups are complete; no remaining large pieces may depend on closed side access.	High: shaft/stair interfaces and final crane-delivered wall closure. NEXT: Reconcile every kit; any missing trapped item requires reordering before closure, not improvisation.
43	L5 - Residual partitions / closure check	Complete remaining non-loadbearing partitions and connections; verify all lift-dependent components and access closures.	A or B as released	L5-G7 kit; cube TBD	Clear all items that would become trapped under the next deck. AFTER: All wall groups and pre-deck large internals are reconciled.	High: shop-panel inventory, connection access and maintained egress. NEXT: Verify no missing panel or connection face will be covered by joists/deck.
44	L5 - Overhead framing / floor release	Complete required joists, blocking, diaphragms and inspections in approved cells; authorize the next working level.	A or B as released	L5-G8 framing kit; cube TBD	Close overhead receiving space only after that cell passes its pre-deck check. AFTER: The receiving route from above is closed in released cells; next deck is an accepted work surface.	HOLD: diaphragm/temporary bracing, support reactions, load capacity and deck-system RFI-02. NEXT: Reset crane coverage for the next level; do not advance an unreleased upper story.
45	L6 - Neighbor-side rear: Units 606-605 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L6-G1 kit; cube TBD	Start at the far rear with an approved stable corner and returns; no later low-level transfer behind it. AFTER: Far rear group is stabilized; middle/front and overhead receiving areas remain open.	High: far reach, adjacent property, initial stability and edge protection. NEXT: Check next group landing and rigging rotation clear of the new rear returns.
46	L6 - Neighbor-side middle: Units 604-602 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L6-G2 kit; cube TBD	Continue the far side while the overhead delivery route and central corridor are open. AFTER: Far middle group is stabilized; near middle receiving slot remains open.	High: large internal pieces can be trapped by top framing or completed near walls. NEXT: Check all large middle-cell internals are installed before its near-side closure.
47	L6 - Jordan-side middle: Units 609-610 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L6-G3 kit; cube TBD	Complete the middle near side only after its far-side kit and internal large pieces are in place. AFTER: Middle cell is bounded; rear near-side receiving slot remains open.	High: connecting faces and long-panel rotation require a verified envelope. NEXT: Check the rear group arrives from above without passing through the completed middle cell.
48	L6 - Jordan-side rear: Units 607-608 / stair 01	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L6-G4 kit; cube TBD	Finish the rear sector before relocation; protect rear equipment routes and stair access. AFTER: Rear/middle sector is complete and stable for the planned crane move.	High: stair/equipment routes; local rear closure only after kit reconciliation. NEXT: Verify B setup or A full coverage, public controls and forward cell stability before front lifts.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
49	L6 - Neighbor-side frontage: Unit 601 frontage	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L6-G5 kit; cube TBD	From the verified front setup, land the remaining far-side frontage group before the near front closes. AFTER: Far front is complete; near front and core receiving space remain open.	High: front reach, neighboring edge and public El Camino frontage. NEXT: Check shaft pieces, stair members and front internals fit before closing the near-front return.
50	L6 - Jordan-side frontage / core: Unit 600 / stair 02 / elevators	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L6-G6 kit; cube TBD	Complete the front core interfaces and near-side returns last; lower trapped pieces before final closure. AFTER: Crane-delivered wall groups are complete; no remaining large pieces may depend on closed side access.	High: shaft/stair interfaces and final crane-delivered wall closure. NEXT: Reconcile every kit; any missing trapped item requires reordering before closure, not improvisation.
51	L6 - Residual partitions / closure check	Complete remaining non-loadbearing partitions and connections; verify all lift-dependent components and access closures.	A or B as released	L6-G7 kit; cube TBD	Clear all items that would become trapped under the next deck. AFTER: All wall groups and pre-deck large internals are reconciled.	High: shop-panel inventory, connection access and maintained egress. NEXT: Verify no missing panel or connection face will be covered by joists/deck.
52	L6 - Overhead framing / floor release	Complete required joists, blocking, diaphragms and inspections in approved cells; authorize the next working level.	A or B as released	L6-G8 framing kit; cube TBD	Close overhead receiving space only after that cell passes its pre-deck check. AFTER: The receiving route from above is closed in released cells; next deck is an accepted work surface.	HOLD: diaphragm/temporary bracing, support reactions, load capacity and deck-system RFI-02. NEXT: Reset crane coverage for the next level; do not advance an unreleased upper story.
53	L7 - Neighbor-side rear: Units 706-705 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L7-G1 kit; cube TBD	Start at the far rear with an approved stable corner and returns; no later low-level transfer behind it. AFTER: Far rear group is stabilized; middle/front and overhead receiving areas remain open.	High: far reach, adjacent property, initial stability and edge protection. NEXT: Check next group landing and rigging rotation clear of the new rear returns.
54	L7 - Neighbor-side middle: Units 704-702 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L7-G2 kit; cube TBD	Continue the far side while the overhead delivery route and central corridor are open. AFTER: Far middle group is stabilized; near middle receiving slot remains open.	High: large internal pieces can be trapped by top framing or completed near walls. NEXT: Check all large middle-cell internals are installed before its near-side closure.
55	L7 - Jordan-side middle: Units 709-710 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L7-G3 kit; cube TBD	Complete the middle near side only after its far-side kit and internal large pieces are in place. AFTER: Middle cell is bounded; rear near-side receiving slot remains open.	High: connecting faces and long-panel rotation require a verified envelope. NEXT: Check the rear group arrives from above without passing through the completed middle cell.
56	L7 - Jordan-side rear: Units 707-708 / stair 01	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L7-G4 kit; cube TBD	Finish the rear sector before relocation; protect rear equipment routes and stair access. AFTER: Rear/middle sector is complete and stable for the planned crane move.	High: stair/equipment routes; local rear closure only after kit reconciliation. NEXT: Verify B setup or A full coverage, public controls and forward cell stability before front lifts.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

Sequence register | 57-64

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
57	L7 - Neighbor-side frontage: Unit 701 frontage	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L7-G5 kit; cube TBD	From the verified front setup, land the remaining far-side frontage group before the near front closes. AFTER: Far front is complete; near front and core receiving space remain open.	High: front reach, neighboring edge and public El Camino frontage. NEXT: Check shaft pieces, stair members and front internals fit before closing the near-front return.
58	L7 - Jordan-side frontage / core: Unit 700 / stair 02 / elevators	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L7-G6 kit; cube TBD	Complete the front core interfaces and near-side returns last; lower trapped pieces before final closure. AFTER: Crane-delivered wall groups are complete; no remaining large pieces may depend on closed side access.	High: shaft/stair interfaces and final crane-delivered wall closure. NEXT: Reconcile every kit; any missing trapped item requires reordering before closure, not improvisation.
59	L7 - Residual partitions / closure check	Complete remaining non-loadbearing partitions and connections; verify all lift-dependent components and access closures.	A or B as released	L7-G7 kit; cube TBD	Clear all items that would become trapped under the next deck. AFTER: All wall groups and pre-deck large internals are reconciled.	High: shop-panel inventory, connection access and maintained egress. NEXT: Verify no missing panel or connection face will be covered by joists/deck.
60	L7 - Overhead framing / floor release	Complete required joists, blocking, diaphragms and inspections in approved cells; authorize the next working level.	A or B as released	L7-G8 framing kit; cube TBD	Close overhead receiving space only after that cell passes its pre-deck check. AFTER: The receiving route from above is closed in released cells; next deck is an accepted work surface.	HOLD: diaphragm/temporary bracing, support reactions, load capacity and deck-system RFI-02. NEXT: Reset crane coverage for the next level; do not advance an unreleased upper story.
61	L8 - Neighbor-side rear: Units 806-805 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L8-G1 kit; cube TBD	Start at the far rear with an approved stable corner and returns; no later low-level transfer behind it. AFTER: Far rear group is stabilized; middle/front and overhead receiving areas remain open.	High: far reach, adjacent property, initial stability and edge protection. L8 HOLD RFI-01. NEXT: Check next group landing and rigging rotation clear of the new rear returns.
62	L8 - Neighbor-side middle: Units 804-802 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L8-G2 kit; cube TBD	Continue the far side while the overhead delivery route and central corridor are open. AFTER: Far middle group is stabilized; near middle receiving slot remains open.	High: large internal pieces can be trapped by top framing or completed near walls. L8 HOLD RFI-01. NEXT: Check all large middle-cell internals are installed before its near-side closure.
63	L8 - Jordan-side middle: Units 809-810 side	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L8-G3 kit; cube TBD	Complete the middle near side only after its far-side kit and internal large pieces are in place. AFTER: Middle cell is bounded; rear near-side receiving slot remains open.	High: connecting faces and long-panel rotation require a verified envelope. L8 HOLD RFI-01. NEXT: Check the rear group arrives from above without passing through the completed middle cell.
64	L8 - Jordan-side rear: Units 807-808 / stair 01	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A	L8-G4 kit; cube TBD	Finish the rear sector before relocation; protect rear equipment routes and stair access. AFTER: Rear/middle sector is complete and stable for the planned crane move.	High: stair/equipment routes; local rear closure only after kit reconciliation. L8 HOLD RFI-01. NEXT: Verify B setup or A full coverage, public controls and forward cell stability before front lifts.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

Sequence register | 65-72

Exact IDs match the annotated sheets | A/B are conditional candidates | All material cube assignments: ASSUMPTION - PACKING TO BE VERIFIED

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
65	L8 - Neighbor-side frontage: Unit 801 frontage	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L8-G5 kit; cube TBD	From the verified front setup, land the remaining far-side frontage group before the near front closes. AFTER: Far front is complete; near front and core receiving space remain open.	High: front reach, neighboring edge and public El Camino frontage. L8 HOLD RFI-01. NEXT: Check shaft pieces, stair members and front internals fit before closing the near-front return.
66	L8 - Jordan-side frontage / core: Unit 800 / stair 02 / elevators	Erect required steel/supports and CFS as an approved stable cell; place large internals before its last enclosing return.	A or B	L8-G6 kit; cube TBD	Complete the front core interfaces and near-side returns last; lower trapped pieces before final closure. AFTER: Crane-delivered wall groups are complete; no remaining large pieces may depend on closed side access.	High: shaft/stair interfaces and final crane-delivered wall closure. L8 HOLD RFI-01. NEXT: Reconcile every kit; any missing trapped item requires reordering before closure, not improvisation.
67	L8 - Residual partitions / closure check	Complete remaining non-loadbearing partitions and connections; verify all lift-dependent components and access closures.	A or B as released	L8-G7 kit; cube TBD	Clear all items that would become trapped under the next deck. AFTER: All wall groups and pre-deck large internals are reconciled.	High: shop-panel inventory, connection access and maintained egress. NEXT: Verify no missing panel or connection face will be covered by joists/deck.
68	L8 - Overhead framing / floor release	Complete required joists, blocking, diaphragms and inspections in approved cells; authorize the next working level.	A or B as released	L8-G8 framing kit; cube TBD	Close overhead receiving space only after that cell passes its pre-deck check. AFTER: The receiving route from above is closed in released cells; next deck is an accepted work surface.	HOLD: diaphragm/temporary bracing, support reactions, load capacity and deck-system RFI-02. NEXT: Reset crane coverage for the next level; do not advance an unreleased upper story.
69	Roof support and deck acceptance	Accept the L8-to-roof structure, falls, penetrations and storage limits.	None until accepted	Engineering release	The roof may only be used after structural and loading acceptance. AFTER: Roof is released for the planned construction loads.	HOLD RFI-01 / RFI-02; elevations and support mapping. NEXT: Confirm upstand and equipment supports match the coordinated roof layout.
70	Rear stair 01 headhouse	Erect approved stair 01 upstand walls and overhead framing; keep the stair route protected.	A	Roof G2 kit	Complete the rear vertical termination before restricting its lifting access. AFTER: Rear headhouse is stable; equipment landing zones remain available.	High: edge work and incomplete headhouse stability. NEXT: Verify the front headhouse can be approached without crossing occupied areas.
71	Front stair 02 / elevator headhouse	Erect the front headhouse and elevator overrun structure with vendor coordination.	A or B	Roof G3 kit	Respect the highest erection level and unresolved equipment interfaces. AFTER: Both vertical terminations are coordinated; roof equipment routes remain open.	High: maximum hook height and elevator steel/rigging interfaces. NEXT: Verify largest equipment package and the crane envelope at maximum height.
72	Roof equipment / large assemblies	Land agreed large equipment and PV assemblies on approved supports in the vendor sequence.	A or B	Vendor packages	Avoid trapping roof equipment behind permanent screens or final crane demobilization. AFTER: Large roof deliveries are complete and secured.	HOLD: weights, supports, rigging and vendor lifting instructions. NEXT: Reconcile all equipment before screen and parapet closure.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.

STEP	PANEL / GROUP	ACTION	CRANE	MATERIAL	WHY / CHANGED STATE	RISK / NEXT CHECK
73	Final parapets / screens / canopies	Complete remaining parapets, screens and exterior canopy packages after route reconciliation.	A or B	Roof G5 kit	Make final closure only after all required large roof packages are in place. AFTER: Final permanent closures are complete; protected personnel egress remains.	High: wind area and edge lifts; do not defer required fall protection. NEXT: Verify every remaining lift, temporary support and access restoration obligation.
74	Final release and demobilization	Inspect connections and weather protection; remove temporary works only under approved release; restore ROW.	Released demobilization	None	End crane use only when all scheduled lifts and dependent work are accepted. AFTER: Erection coordination scope is closed after acceptance.	HOLD: engineer/GC release; incomplete lifts or temporary support removal. NEXT: Record as-built deviations and hand over to follow-on trades.

Lift-plan handoff worksheet - complete outside this concept before release

For every shop-panel or assembly pick, document the actual data below. Test both pick and set locations and the full swept route. Ground-level plan distance alone does not establish crane feasibility.

CASE	GROSS LOAD / RIGGING	PICK / SET COORDS	MAX RADIUS / HOOK HEIGHT	OBSTACLES / SUPPORT	CHART / APPROVAL RECORD
A: far rear at highest served level	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED
A or B: far front at highest served level	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED
Highest headhouse / roof equipment	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED
Final closure and remaining lift	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED	TO BE PROVIDED

Release owners: Livio / fabricator, erection contractor, structural engineer, crane planner/operator, shoring/geotechnical engineer, GC and relevant road authority. The required sign-offs depend on the final means and methods; no approval is recorded by this worksheet.

Source and status fields for every row, plus the full changed-state / next-step checks, are included in the companion CSV. A sequence group is not a single crane pick.
